


# PROJECT SUMMARY

Hwy 200  
 From Hwy 75 to the western limits of Ada  
 Bridge 2068  
 State Project No. 5407-31


**Substantially Complete**

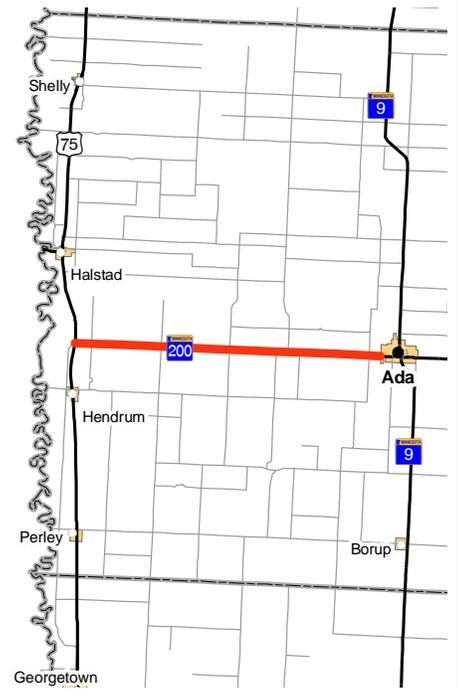

### Primary Purpose:

Performance-based Need: Pavement Condition

### Investment Category:

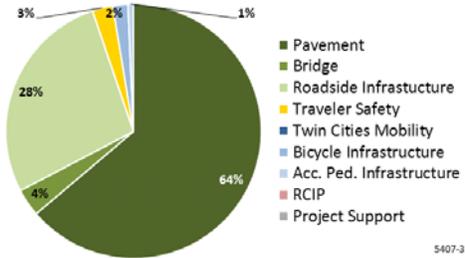

5407-31

### Project Description:

The project consists of improving 13 miles of concrete road surface with a bituminous overlay.

### Recent Changes and Updates

Project is substantially complete.

### Project History:

The project is under construction. The estimate increased because a two-mile portion planned to be an overlay changed to a full pavement replacement.

The local watershed would not allow additional fill in flood overtopping areas.

In September 2012 the project was moved from 2013 to 2014 because of the design time needed to resolve hydraulic issues with the local watershed.

The project improves ride and surface condition, pavement strength and extends pavement life.

### Total Project Cost Estimate (millions)

Date in which the project entered into the STIP: 2007

	<u>Baseline Est.</u>	<u>Current Est.</u>
Construction Letting:	\$ 4.9	\$ 7.0
Other Construction Elements:	\$ 0.3	\$ 0.0
Engineering:	\$ 1.0	\$ 0.7
Right of Way:	\$ 0.0	\$ 0.0
<b>Total:</b>	<b>\$ 6.2</b>	<b>\$ 7.7</b>

*Construction cost estimates are adjusted to the mid-year of construction, using inflation rates provided by OTSM.*

### Key Cost Estimate Assumptions:

The current estimate is the construction letting amount.

### Project Risks:

No project risks remain.

### Schedule:

Environmental Approval Date: 05/29/2013  
 Municipal Consent Approval Date: Not Needed  
 Geometric Layout Approval Date: Not Needed  
 Construction Limits Established Date: Not Needed  
 Original Letting Date: 03/26/2010  
 Current Letting Date: 02/28/2014  
 Construction Season: 2014  
 Estimated Substantial Completion: Oct. 2014



Minnesota Department of Transportation  
 District 2  
 3920 Highway 2 West  
 (218) 755-6500

**District Engineer:** Craig Collison  
**Project Manager:** Todd Vonasek

**Revised Date:** 12/15/2015
