

## PROJECT SUMMARY


Hwy 371

Nisswa

State Project No. 1810-98

<http://www.dot.state.mn.us/d3/hwy371nisswa/index.html>

**Substantially Complete**

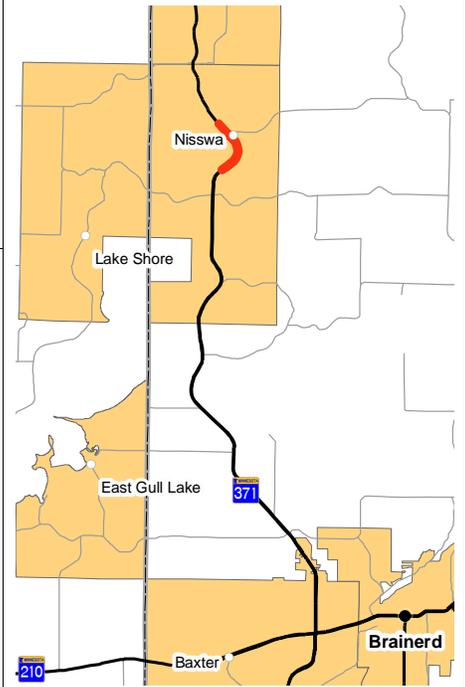

### Primary Purpose:

Performance-based Need: Pavement Condition

### Investment Category:

\*This project was designed and scoped before the current highway investment plan MnSHIP was developed, which breaks projects into investment categories.

### Recent Changes and Updates

Construction was completed in summer 2014 instead of fall 2013 due to weather and other unforeseen construction delays/setbacks.

### Project History:

Phase I of Hwy 371 North Environmental Impact Statement (under SP 1116-22). The project was substantially completed in 2013. Access to a local road was a concern of local government. The current estimate includes work performed by Crow Wing County and Nisswa as required for the realignment of Crow Wing Co Hwy 18. See Key Cost Estimate Assumptions.

### Project Description:

Hwy 371 North Stage 1: Reconstruction of four-lane through Nisswa, including construction of bicycle-pedestrian tunnel.

### Total Project Cost Estimate (millions)

Date in which the project entered into the STIP: 2010

	<u>Baseline Est.</u>	<u>Current Est.</u>
Construction Letting:	\$ 5.0	\$ 7.6
Other Construction Elements:	\$ 0.0	\$ 2.7
Engineering:	\$ 1.0	\$ 1.5
Right of Way:	\$ 1.8	\$ 0.9
<b>Total:</b>	<b>\$ 7.8</b>	<b>\$ 10.0</b>

*Construction cost estimates are adjusted to the mid-year of construction, using inflation rates provided by OTSM.*

### Key Cost Estimate Assumptions:

The current estimate is based on the actual bid amount. The baseline estimate used estimated quantities and average bid prices for similar projects for MnDOT's portion of the work only. The current estimate reflects State and local (e.g. Crow Wing County and City of Nisswa) costs associated with the reconstruction of Hwy 371 and the realignment of Crow Wing Co Hwy 18. MnDOT's construction cost is \$4.9 million.

### Project Risks:

No risks remaining.

### Schedule:

Environmental Approval Date: 10/21/2010  
Municipal Consent Approval Date: 02/16/2011  
Geometric Layout Approval Date: 10/19/2010  
Construction Limits Established Date: 01/01/2011  
Original Letting Date: 02/24/2012  
Current Letting Date: 06/08/2012  
Construction Season: 2012/2013/2014  
Estimated Substantial Completion: Summer 2014



Minnesota Department of Transportation  
District 3  
7694 Industrial Boulevard  
(218) 828-5700

**District Engineer:** Dan Anderson  
**Project Manager:** Jim Hallgren

**Revised Date:** 12/15/2015
