

PROJECT SUMMARY

Hwy 75
Hwy 10 to north Clay County line
State Project No. 1407-25


Substantially Complete



Primary Purpose:

Performance-based Need: Pavement condition

Investment Category:

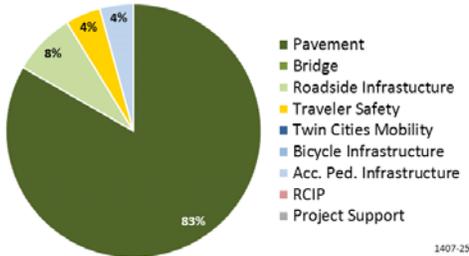

Project Description:

This project consists of pavement resurfacing, culvert replacement and turn lane construction for 19 miles from Hwy 10 in Moorhead to the Clay/Norman County line.

Recent Changes and Updates

Project is substantially complete.

Project History:

In place pavement needs resurfacing and was moved forward due to rapid decline of pavement conditions. Hydraulic/drainage concerns need to be addressed. Project is designed, let and currently being constructed. 4 miles were added to the south limits of the original project, which resulted in additional cost.

Total Project Cost Estimate (millions)

Date in which the project entered into the STIP: 2013

	<u>Baseline Est.</u>	<u>Current Est.</u>
Construction Letting:	\$ 5.2	\$ 7.1
Other Construction Elements:	\$ 0.7	\$ 0.0
Engineering:	\$ 1.2	\$ 0.9
Right of Way:	\$ 0.0	\$ 0.0
Total:	\$ 7.1	\$ 8.0

Construction cost estimates are adjusted to the mid-year of construction, using inflation rates provided by OTSM.

Key Cost Estimate Assumptions:

Project is substantially complete.

Project Risks:

Risks retired.

Schedule:

Environmental Approval Date: 02/24/2014
Municipal Consent Approval Date: Not Needed
Geometric Layout Approval Date: 3/21/2013
Construction Limits Established Date: 03/21/2013
Original Letting Date: 02/19/2016
Current Letting Date: 04/25/2014
Construction Season: 2014
Estimated Substantial Completion: August 2014



Minnesota Department of Transportation
District 4
1000 Hwy 10 W
(218) 846-3600

District Engineer: Jody Martinson
Project Manager: Thomas Pace

Revised Date: 12/15/2015
