


PROJECT SUMMARY

Old Hwy 14

From west to east Janesville city limits


State Project No. 8103-114

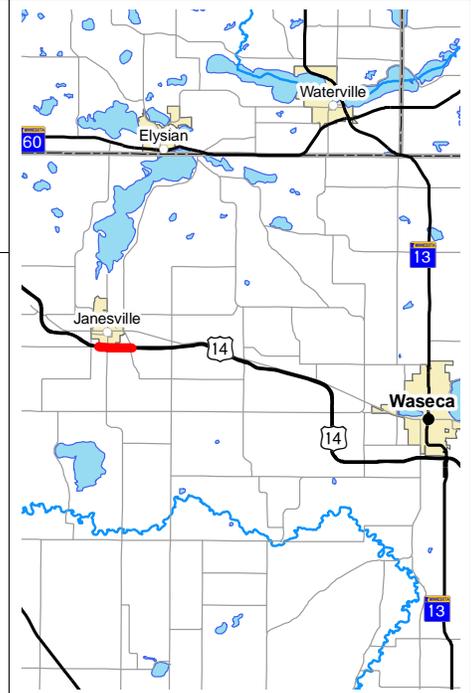

Primary Purpose:

Performance-based Need: Pavement Condition

Investment Category:

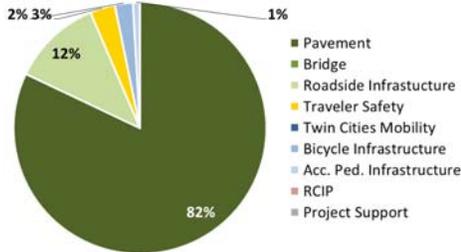

Project Description:

This project consists of the reconstruction of Old Hwy 14 through Janesville. The city will be replacing the utilities in conjunction with this project. A new concrete surface will be provided with curb and gutter.

Recent Changes and Updates

This project is currently being designed. Construction was planned for 2015; however, the city of Janesville is leading the project development and decided to move construction to 2016. The letting date was moved to January 2016 and the cost estimate was updated to account for an additional year of inflation.

Project History:

The Legislature recently passed the law allowing for the construction of this project according to the Settlement Agreement. The turnback of Old Hwy 14 in Waseca and Steele counties was contested. A Settlement Agreement was created to define what was to be constructed.

Total Project Cost Estimate (millions)

Date in which the project entered into the STIP: 2014

	<u>Baseline Est.</u>	<u>Current Est.</u>
Construction Letting:	\$ 4.6	\$ 5.8
Other Construction Elements:	\$ 0.3	\$ 0.3
Engineering:	\$ 0.9	\$ 0.9
Right of Way:	\$ 0.0	\$ 0.0
Total:	\$ 5.8	\$ 7.0

Construction cost estimates are adjusted to the mid-year of construction, using inflation rates provided by OTSM.

Key Cost Estimate Assumptions:

The estimates for the turnback were performed early in the process. Only a certain amount of money was made available for the entire program on Old Hwy 14, so, there is a need to make sure there is enough money for the projects that will come in subsequent years.

Project Risks:

The Settlement Agreement was very prescriptive in some areas and vague in others.

Schedule:

Environmental Approval Date: Pending Approval
 Municipal Consent Approval Date: Not Needed
 Geometric Layout Approval Date: Not Needed
 Construction Limits Established Date: Not Needed
 Original Letting Date: 04/15/2015
 Current Letting Date: 1/15/2016
 Construction Season: May 2015 / Nov 2015
 Estimated Substantial Completion: 11/01/2016



Minnesota Department of Transportation
 District 7
 2151 Bassett Drive
 (507) 304-6100

District Engineer: Greg Ous
Project Manager: Matt Rottermond

Revised Date: 12/15/2015
