


PROJECT SUMMARY


Hwy 75
 Hwy 19 in Ivanhoe to Canby
 State Project No. 4109-29

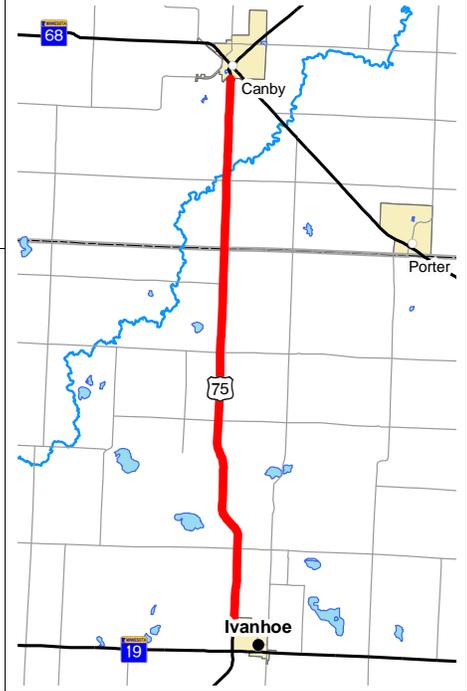

Primary Purpose:

Performance-based Need: Pavement Condition

Investment Category:

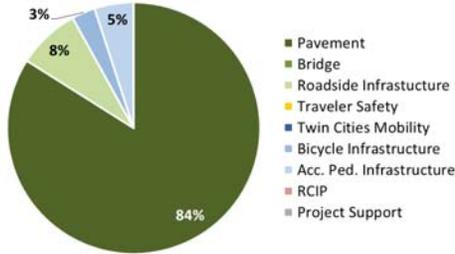

Project Description:

This project is a mill and overlay of approximately 17 miles from Hwy 19 in Ivanhoe to Canby. It also includes the replacement of low-tension guardrail and raising of the approach panel adjacent to the bridge, lining 20 to 30 pipes and replacing 5 culverts.

Recent Changes and Updates

First year in report.

Project History:

Total Project Cost Estimate (millions)

Date in which the project entered into the STIP: 2015

	<u>Baseline Est.</u>	<u>Current Est.</u>
Construction Letting:	\$ 4.6	\$ 4.6
Other Construction Elements:	\$ 0.1	\$ 0.1
Engineering:	\$ 0.8	\$ 0.8
Right of Way:	\$ 0.0	\$ 0.0
Total:	\$ 5.5	\$ 5.5

Construction cost estimates are adjusted to the mid-year of construction, using inflation rates provided by OTSM.

Key Cost Estimate Assumptions:

Engineering estimates reflect 20% of construction letting. This project does have right of way costs, but they are expected to be less than \$0.1M.

Project Risks:

No known significant project risks.

Schedule:

Environmental Approval Date: Not Complete
 Municipal Consent Approval Date: NA
 Geometric Layout Approval Date: Not Complete
 Construction Limits Established Date: Not Complete
 Original Letting Date: 03/22/2019
 Current Letting Date: 03/22/2019
 Construction Season: 2019
 Estimated Substantial Completion: Fall 2019



Minnesota Department of Transportation
 District 8
 2505 Transportation Road
 (320) 231-5195

District Engineer: Jon Huseby
Project Manager: Kent Medalen

Revised Date: 12/15/2015
