


# PROJECT SUMMARY

Hwy 169


Scott County, from Hwy 25 in Belle Plaine to Hwy 282 in Jordan  
State Project No. 7008-111

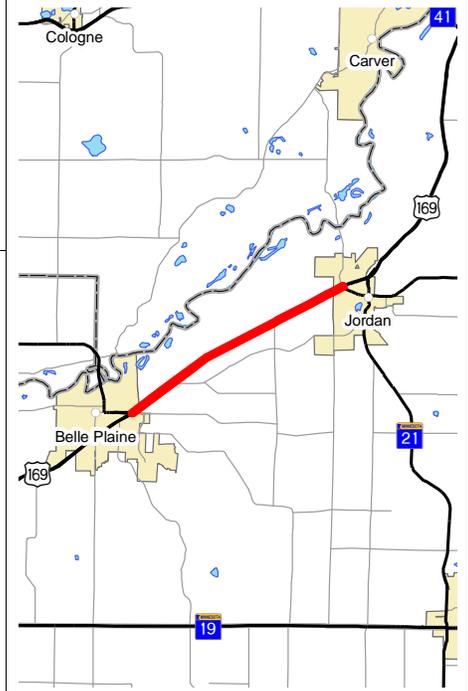

## Primary Purpose:

Performance Need: Pavement Conditions, District Safety Plan

## Investment Category:

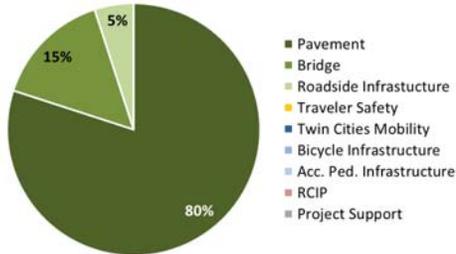

## Project Description:

This project is an unbonded concrete overlay, median closures, add U-turns, and cable guardrails on Hwy 169 from Hwy 25 in Belle Plaine to Hwy 282 in Jordan.

## Recent Changes and Updates

This is the first year this project is included in the MHP report.

The northern project limit is shifting about 1,000 feet south of Hwy 282. This segment is being reconstructed in the 2015 Jordan pavement project so that the Hwy 169/Hwy 282/CR 9 intersection is not impacted again in 2018.

## Project History:

This is the first year this project is included in the MHP report. The project is being driven by pavement needs. Additional access management may be implemented if there is support from local partners.

## Total Project Cost Estimate (millions)

Date in which the project entered into the STIP: 2014

	<u>Baseline Est.</u>	<u>Current Est.</u>
Construction Letting:	\$ 18.0	\$ 18.0
Other Construction Elements:	\$ 0.0	\$ 0.0
Engineering:	\$ 3.0	\$ 3.0
Right of Way:	\$ 0.0	\$ 0.0
<b>Total:</b>	<b>\$ 21.0</b>	<b>\$ 21.0</b>

*Construction cost estimates are adjusted to the mid-year of construction, using inflation rates provided by OTSM.*

## Key Cost Estimate Assumptions:

Median closures and turn lane costs are based on prior projects and will be adjusted after layout preparation and quantity development. Cost will be revised during the Fall of 2014 to cover the 1,000 ft. extension.

## Project Risks:

Potential local opposition to R-cuts. Extent of culvert work not fully known.

## Schedule:

Environmental Approval Date: Pending  
Municipal Consent Approval Date: NA  
Geometric Layout Approval Date: Pending  
Construction Limits Established Date: Pending  
Original Letting Date: 07/21/2017  
Current Letting Date: 07/21/2017  
Construction Season: 2018  
Estimated Substantial Completion: 01/26/2019



Minnesota Department of Transportation  
District M  
1500 West County Road B2  
(651) 234-7500

**District Engineer:** Scott McBride  
**Project Manager:** Chad Casey

**Revised Date:** 12/15/2015
