


# PROJECT SUMMARY

Hwy 10

End of 4-Lane west of Wadena to Oink Joint Rd


State Project No. 8001-40

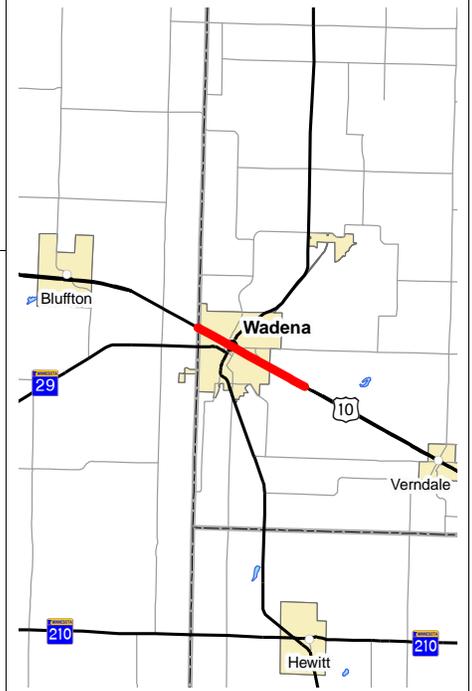

## Primary Purpose:

Performance-based Need: Pavement Condition

## Investment Category:

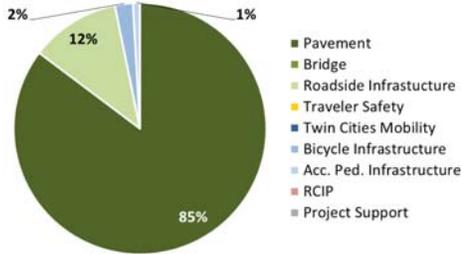

## Project Description:

Resurfacing of the rural segments of Hwy 10 east and west of Wadena and reconstruction of the urban section from 3rd St NW to 2nd St NE within the city limits of Wadena. Work includes replacement of curb, gutter, sidewalks and railroad signal upgrades.

## Recent Changes and Updates

This is a new project. Funding for this project provided jointly by District 3 and District 4.

## Project History:

Several pavement rehabilitation projects have been done on this roadway. The pavement has reached the end of its expected life in the urban area of Wadena and requires full reconstruction. The rural segments require milling and filling.

## Total Project Cost Estimate (millions)

Date in which the project entered into the STIP: 2014

	<u>Baseline Est.</u>	<u>Current Est.</u>
Construction Letting:	\$ 9.6	\$ 9.6
Other Construction Elements:	\$ 0.0	\$ 0.0
Engineering:	\$ 1.9	\$ 1.9
Right of Way:	\$ 5.0	\$ 5.0
<b>Total:</b>	<b>\$ 16.5</b>	<b>\$ 16.5</b>

*Construction cost estimates are adjusted to the mid-year of construction, using inflation rates provided by OTSM.*

## Key Cost Estimate Assumptions:

Based on estimated quantities and average bid prices. The current estimate is based on bids and design changes that reduced costs. Project includes work in District 4.

## Project Risks:

A risk is if the public does not accept the urban pavement replacement along with capacity improvements.

## Schedule:

Environmental Approval Date: Pending  
 Municipal Consent Approval Date: Pending  
 Geometric Layout Approval Date: Pending  
 Construction Limits Established Date: Not Started  
 Original Letting Date: 12/15/2017  
 Current Letting Date: 12/15/2017  
 Construction Season: 2018  
 Estimated Substantial Completion: Fall 2018



Minnesota Department of Transportation  
 District 3  
 7694 Industrial Boulevard  
 (218) 828-5700

**District Engineer:** Dan Anderson  
**Project Manager:** Claudia Dumont

**Revised Date:** 12/15/2015
