


# PROJECT SUMMARY

Hwy 15  
 Hwy 15 and 33rd Street in St. Cloud  
 Bridge 73046  
 State Project No. 7303-48


**Substantially Complete**

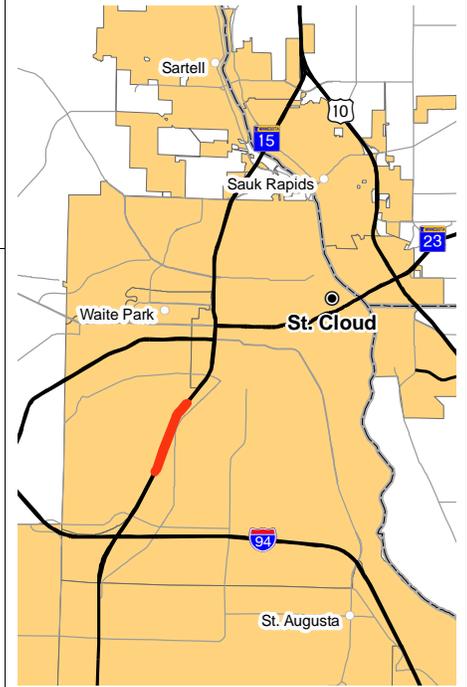

## Primary Purpose:

Regional & Community Improvement Priority:  
 (Transportation Economic Development (TED)  
 Program)

## Investment Category:



## Project Description:

City/county led project to construct a new interchange (Bridge 73046) at Hwy 15 and 33rd St in St. Cloud.

## Recent Changes and Updates

The project is substantially completed.

## Project History:

St. Cloud, Stearns County and other local governments planned an east-west road along the south side of St. Cloud. Part of the planning included an access to Hwy 15. The city applied for a TED grant and was awarded \$8.4 million.

## Total Project Cost Estimate (millions)

Date in which the project entered into the STIP: 2011

	<u>Baseline Est.</u>	<u>Current Est.</u>
Construction Letting:	\$ 7.6	\$ 10.9
Other Construction Elements:	\$ 0.0	\$ 0.0
Engineering:	\$ 1.5	\$ 1.5
Right of Way:	\$ 3.3	\$ 3.3
<b>Total:</b>	<b>\$ 12.4</b>	<b>\$ 15.7</b>

*Construction cost estimates are adjusted to the mid-year of construction, using inflation rates provided by OTSM.*

## Key Cost Estimate Assumptions:

Project let in January 2014 for \$10.9 million including local costs. The amount awarded to the project under the TED grant was \$8.4 million. Due to the new bids, MnDOT will actually award \$6.4 million, which can only be used for the construction of the interchange. There will be additional costs for 33rd Street that will be a local responsibility.

## Project Risks:

No remaining risks.

## Schedule:

Environmental Approval Date: 02/17/2009  
 Municipal Consent Approval Date: NA  
 Geometric Layout Approval Date: 12/7/2011  
 Construction Limits Established Date: Unknown  
 Original Letting Date: 09/15/2012  
 Current Letting Date: 11/15/2013  
 Construction Season: 2014  
 Estimated Substantial Completion: 2014



Minnesota Department of Transportation  
 District 3  
 7694 Industrial Boulevard  
 (218) 828-5700

**District Engineer:** Dan Anderson  
**Project Manager:** Terry Humbert

**Revised Date:** 12/15/2015
