

PROJECT SUMMARY


Hwy 60
 Hwy 60 from Hwy 52 to Hwy 63
 State Project No. 7902-25



Primary Purpose:

Performance-based Need: Pavement Condition

Investment Category:

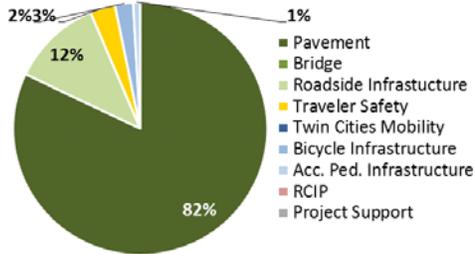

Project Description:

The project consists of a bituminous mill and overlay, hydraulic improvements, and ADA improvements.

Recent Changes and Updates

No recent significant changes.

Project History:

This project will preserve existing roadway structure, extend pavement life, and improve ride quality. ADA facilities will be brought into compliance.

Total Project Cost Estimate (millions)

Date in which the project entered into the STIP: 2015

	<u>Baseline Est.</u>	<u>Current Est.</u>
Construction Letting:	\$ 5.2	\$ 6.3
Other Construction Elements:	\$ 0.0	\$ 0.0
Engineering:	\$ 1.0	\$ 1.0
Right of Way:	\$ 0.0	\$ 0.0
Total:	\$ 6.2	\$ 7.3

Construction cost estimates are adjusted to the mid-year of construction, using inflation rates provided by OTSM.

Key Cost Estimate Assumptions:

20% engineering was used to arrive at total cost estimate.

Project Risks:

Competitive bid may be higher or lower than expected.

Schedule:

Environmental Approval Date: Not Needed
 Municipal Consent Approval Date: Not Needed
 Geometric Layout Approval Date: Not Needed
 Construction Limits Established Date: 06/07/2015
 Original Letting Date: 11/17/2017
 Current Letting Date: 11/17/2017
 Construction Season: 2018
 Estimated Substantial Completion: 11/2018



Minnesota Department of Transportation
 District 6
 2900 48th Street NW
 (507) 286-7500

District Engineer: Jeff Vlamincik
Project Manager: Heather Lukes

Revised Date: 12/15/2015
