


PROJECT SUMMARY

Hwy 61
Hwy 19 to Hwy 316
State Project No. 2514-119


Substantially Complete

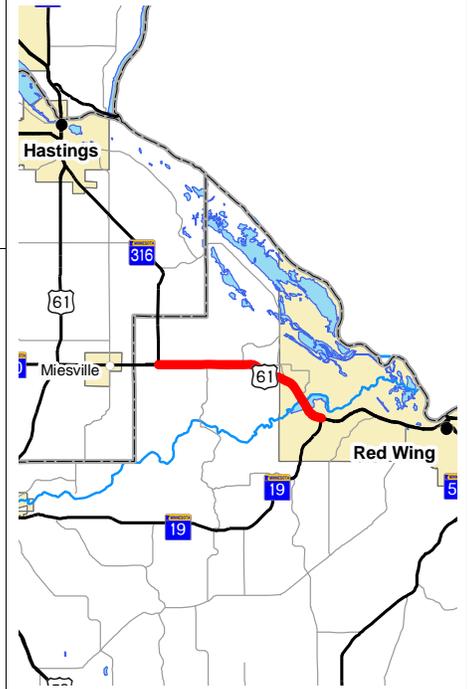

Primary Purpose:

Performance-based Need: Pavement Condition

Investment Category:



Project Description:

This project resurfaces 8.5 miles of both the northbound and the southbound lanes on Hwy 61 from Hwy 19 to Hwy 316. The project will also include traffic safety improvements.

Recent Changes and Updates

This project includes traffic safety improvements, such as a northbound right turn lane at CR 18, and northbound and southbound left turn lanes at Hwy 19. The traffic safety improvements are funded by FHWA Highway Safety Improvement Program funds. Costs exceeded estimates.

Project History:

The four-lane section from Hwy 19 to CR 18 was graded in 1994. The remaining northbound four-lane section from CR 18 to Hwy 316 was graded in 1996 and the southbound was graded in 1997. This section of Hwy 61 is in fair condition, but with significant cracking. As of 2011, the northbound and southbound Ride Quality Index (RQI) was rated as fair and has seen increasing deterioration since then.

Total Project Cost Estimate (millions)

Date in which the project entered into the STIP: 2011

	<u>Baseline Est.</u>	<u>Current Est.</u>
Construction Letting:	\$ 4.4	\$ 4.8
Other Construction Elements:	\$ 0.4	\$ 0.4
Engineering:	\$ 0.8	\$ 1.0
Right of Way:	\$ 0.0	\$ 0.0
Total:	\$ 5.6	\$ 6.1

Construction cost estimates are adjusted to the mid-year of construction, using inflation rates provided by OTSM.

Key Cost Estimate Assumptions:

No right of way was required. No environmental mitigation was needed.

Project Risks:

no project risks remain

Schedule:

Environmental Approval Date: Unknown
Municipal Consent Approval Date: Need Unknown
Geometric Layout Approval Date: Unknown
Construction Limits Established Date: Unknown
Original Letting Date: 11/22/2013
Current Letting Date: 12/20/2013
Construction Season: 2014
Estimated Substantial Completion: 11/2014



Minnesota Department of Transportation
District 6
2900 48th Street NW
(507) 286-7500

District Engineer: Jeff Vlamincik
Project Manager: Jacob Gasper

Revised Date: 12/15/2015
