

# PROJECT SUMMARY


Hwy 61  
Hwy 42 to just north of Lake City limits  
State Project No. 7906-96



## Primary Purpose:

Performance Based Need: Pavement Condition

## Investment Category:

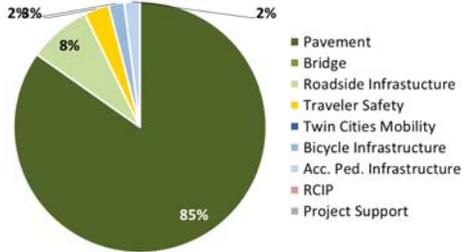

## Project Description:

This is a mill and overlay of northbound and southbound lanes of Hwy 61 from Hwy 42 to the north of Lake City.

## Recent Changes and Updates

Project Scoping Report 3/3/15. No other recent changes.

## Project History:

For this section of roadway, the Ride Quality Index (RQI) ranges from 3.4 to 2.8. This project is needed to improve pavement and shoulder ride quality and extend pavement life. The project will include rehabilitation and replacement of deficient storm sewers and culverts. The project will also include low cost safety improvements, reconstruction of curb ramps, sidewalks and crosswalks, and median improvements along the north segment of Lake City.

## Total Project Cost Estimate (millions)

Date in which the project entered into the STIP: 2015

	<u>Baseline Est.</u>	<u>Current Est.</u>
Construction Letting:	\$ 11.5	\$ 13.3
Other Construction Elements:	\$ 1.5	\$ 1.0
Engineering:	\$ 1.2	\$ 2.4
Right of Way:	\$ 0.0	\$ 0.1
<b>Total:</b>	<b>\$ 14.2</b>	<b>\$ 16.8</b>

*Construction cost estimates are adjusted to the mid-year of construction, using inflation rates provided by OTSM.*

## Key Cost Estimate Assumptions:

The cost estimates are from the project charter report of 6/25/14. The current cost estimate is from the final project scoping report dated 3/3/15.

## Project Risks:

Competitive bid may be higher or lower than expected.

## Schedule:

Environmental Approval Date: Need Unknown  
Municipal Consent Approval Date: Need Unknown  
Geometric Layout Approval Date: Need Unknown  
Construction Limits Established Date: Need Unknown  
Original Letting Date: 10/19/2018  
Current Letting Date: 10/19/2018  
Construction Season: 2019  
Estimated Substantial Completion: November 2019



Minnesota Department of Transportation  
District 6  
2900 48th Street NW  
(507) 286-7500

**District Engineer:** Jeff Vlamnick  
**Project Manager:** Kjersti Anderson

**Revised Date:** 12/15/2015
