

PROJECT SUMMARY

Hwy 16

Hwy 16 from I-90 to Tracy Road Spring Valley


State Project No. 5003-17



Primary Purpose:

Performance Based Need: Pavement Condition

Investment Category:

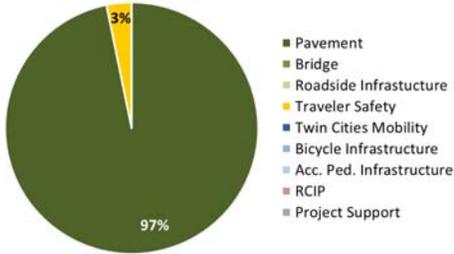

Project Description:

This project is a mill and overlay from I-90 to Spring Valley, which is about 16 miles.

Recent Changes and Updates

Project scoping report, 7/16/15. No other recent changes.

Project History:

This segment of Hwy 16 is a mostly rural 2-lane roadway. The pavement is beginning to deteriorate, which is expected to accelerate over the upcoming years. The project is needed to extend service life and improve ride quality. It includes safety and other improvements.

Total Project Cost Estimate (millions)

Date in which the project entered into the STIP: 2015

	<u>Baseline Est.</u>	<u>Current Est.</u>
Construction Letting:	\$ 7.0	\$ 7.0
Other Construction Elements:	\$ 0.6	\$ 0.6
Engineering:	\$ 0.9	\$ 0.9
Right of Way:	\$ 0.0	\$ 0.0
Total:	\$ 8.5	\$ 8.5

Construction cost estimates are adjusted to the mid-year of construction, using inflation rates provided by OTSM.

Key Cost Estimate Assumptions:

The cost estimates are from the project scoping report of 7/16/15.

Project Risks:

Competitive bids may be higher or lower than expected

Schedule:

Environmental Approval Date: TBD
 Municipal Consent Approval Date: NA
 Geometric Layout Approval Date: TBD
 Construction Limits Established Date: TBD
 Original Letting Date: 01/25/2019
 Current Letting Date: 01/25/2019
 Construction Season: 2019
 Estimated Substantial Completion: 11/2019



Minnesota Department of Transportation
 District 6
 2900 48th Street NW
 (507) 286-7500

District Engineer: Jeff Vlamnick
Project Manager: David Tsang

Revised Date: 12/15/2015
