

PROJECT SUMMARY


I-35

Washington, Anoka Counties

Bridge 82815, 02804, 02806

State Project No. 8280-47


<http://www.dot.state.mn.us/metro/projects/35linolakes/index.html>

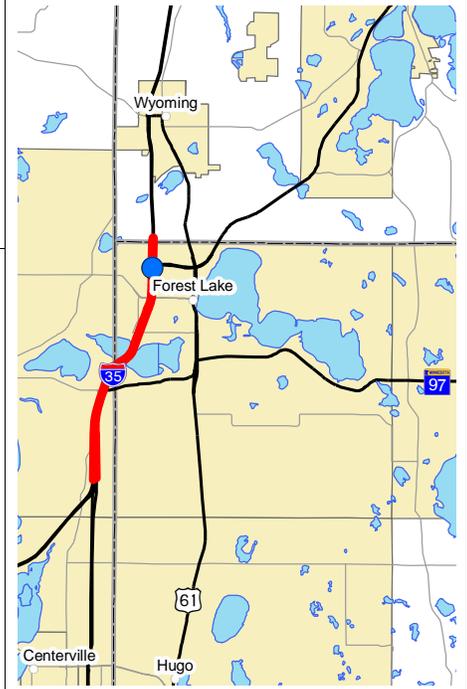

Primary Purpose:

Performance-based Need: Pavement Condition and Bridge Condition.

Investment Category:

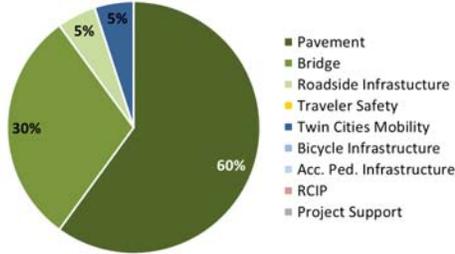

Project Description:

This project consists of an unbonded concrete overlay, and replacement of three bridges. Limits of the project are on I-35E from 80th St E to the junction of I-35/I-35W/I-35E & on I-35W from north of Main St. to the junction of I-35/I-35W/I-35E and on I-35 from the junction of I-35/I-35W/I-35E to north of Hwy 8. The three bridges are: northbound I-35W over southbound I-35E, Hwy 97 over I-35, and Hwy 8 over I-35.

Recent Changes and Updates

Current estimate reflected updated inflation (1/21/2015).

Project History:

This project first was included in the MHP in 2014. Pavement and bridge project to address poor pavement and bridge condition.

Total Project Cost Estimate (millions)

Date in which the project entered into the STIP: 2015

	<u>Baseline Est.</u>	<u>Current Est.</u>
Construction Letting:	\$ 39.6	\$ 38.9
Other Construction Elements:	\$ 0.0	\$ 0.0
Engineering:	\$ 6.4	\$ 6.9
Right of Way:	\$ 0.0	\$ 0.0
Total:	\$ 46.0	\$ 45.8

Construction cost estimates are adjusted to the mid-year of construction, using inflation rates provided by OTSM.

Key Cost Estimate Assumptions:

Standard practices were used to develop cost estimates for this project.

Project Risks:

Traffic impacts during construction. Anoka County leading an interchange study at I-35/Hwy 97.

Schedule:

Environmental Approval Date: 10/07/2015
 Municipal Consent Approval Date: 10/07/2015
 Geometric Layout Approval Date: pending
 Construction Limits Established Date: 01/16/2015
 Original Letting Date: 07/21/2017
 Current Letting Date: 04/28/2017
 Construction Season: 2017/2018
 Estimated Substantial Completion: 11/15/2018



Minnesota Department of Transportation
 District M
 1500 West County Road B2
 (651) 234-7500

District Engineer: Scott McBride
Project Manager: Ryan Coddington

Revised Date: 12/15/2015
