WELCOME



RED WING BRIDGE PROJECT

US 63 River Bridge and Approach Roadways


Open House

meeting is downstairs in the Foot Room



November 2016


Plum/3rd Street Traffic Control Change

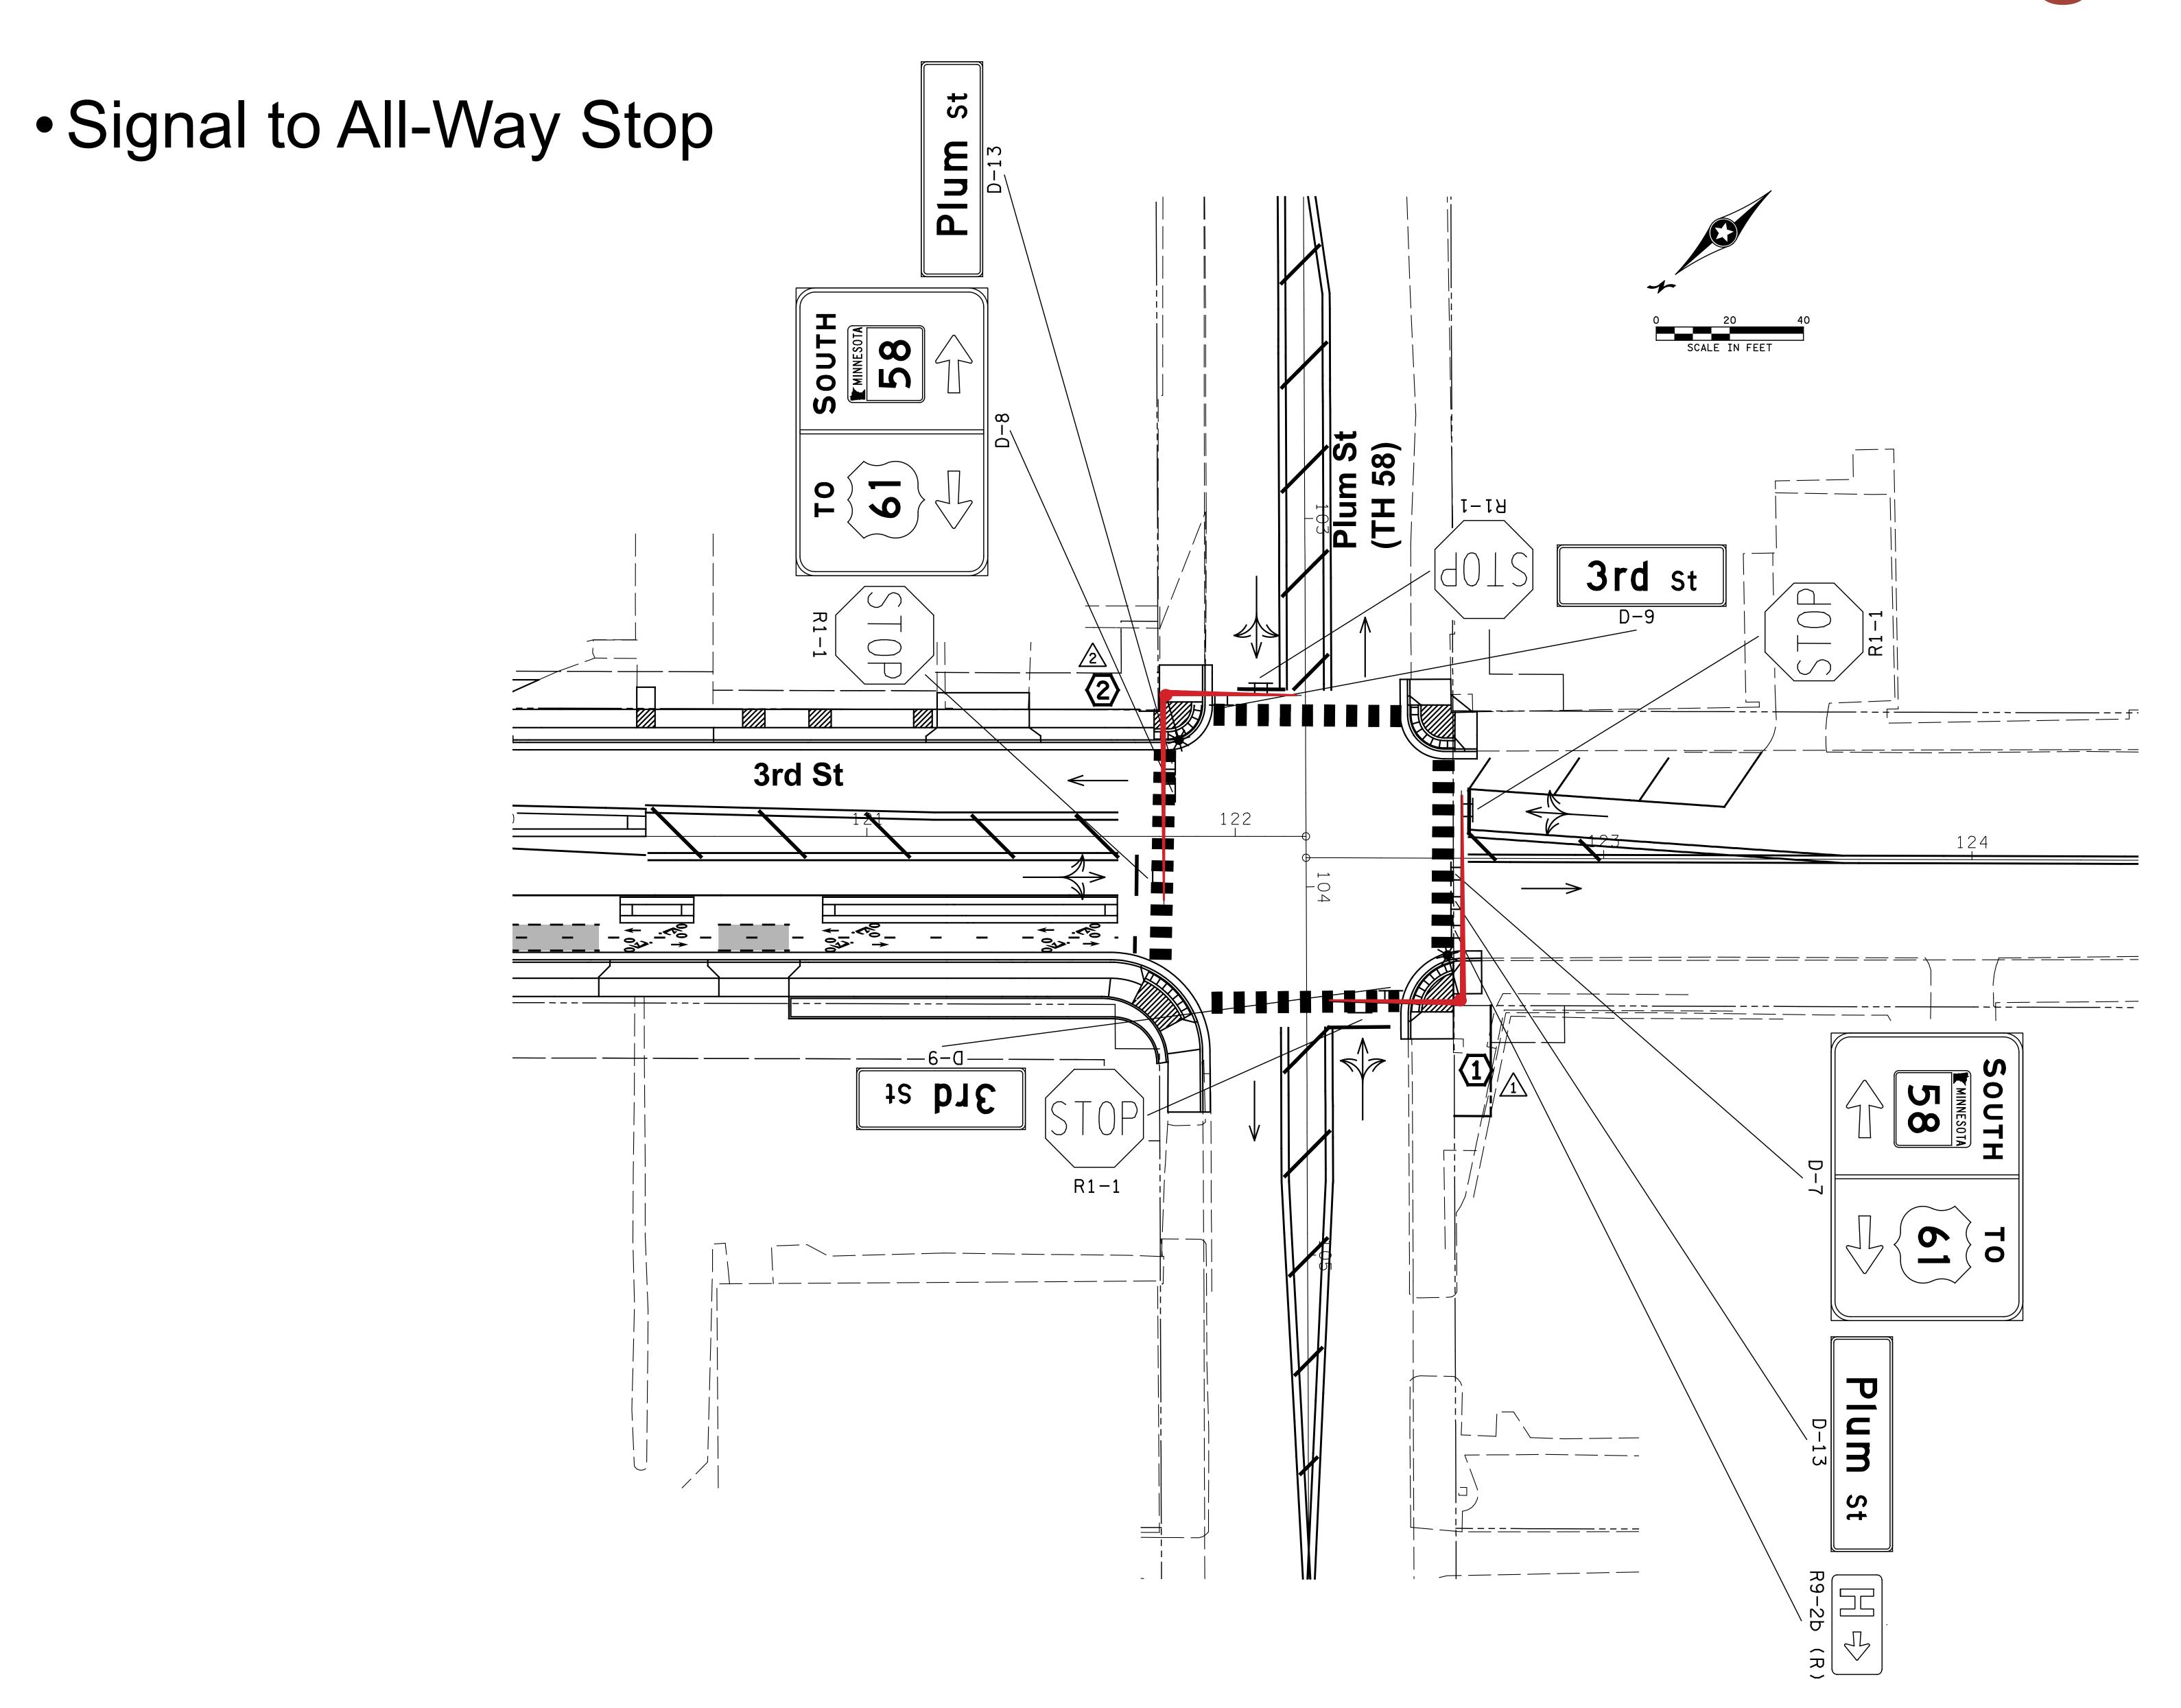

3rd Street Cycle Track



River Bridge Spire Signage

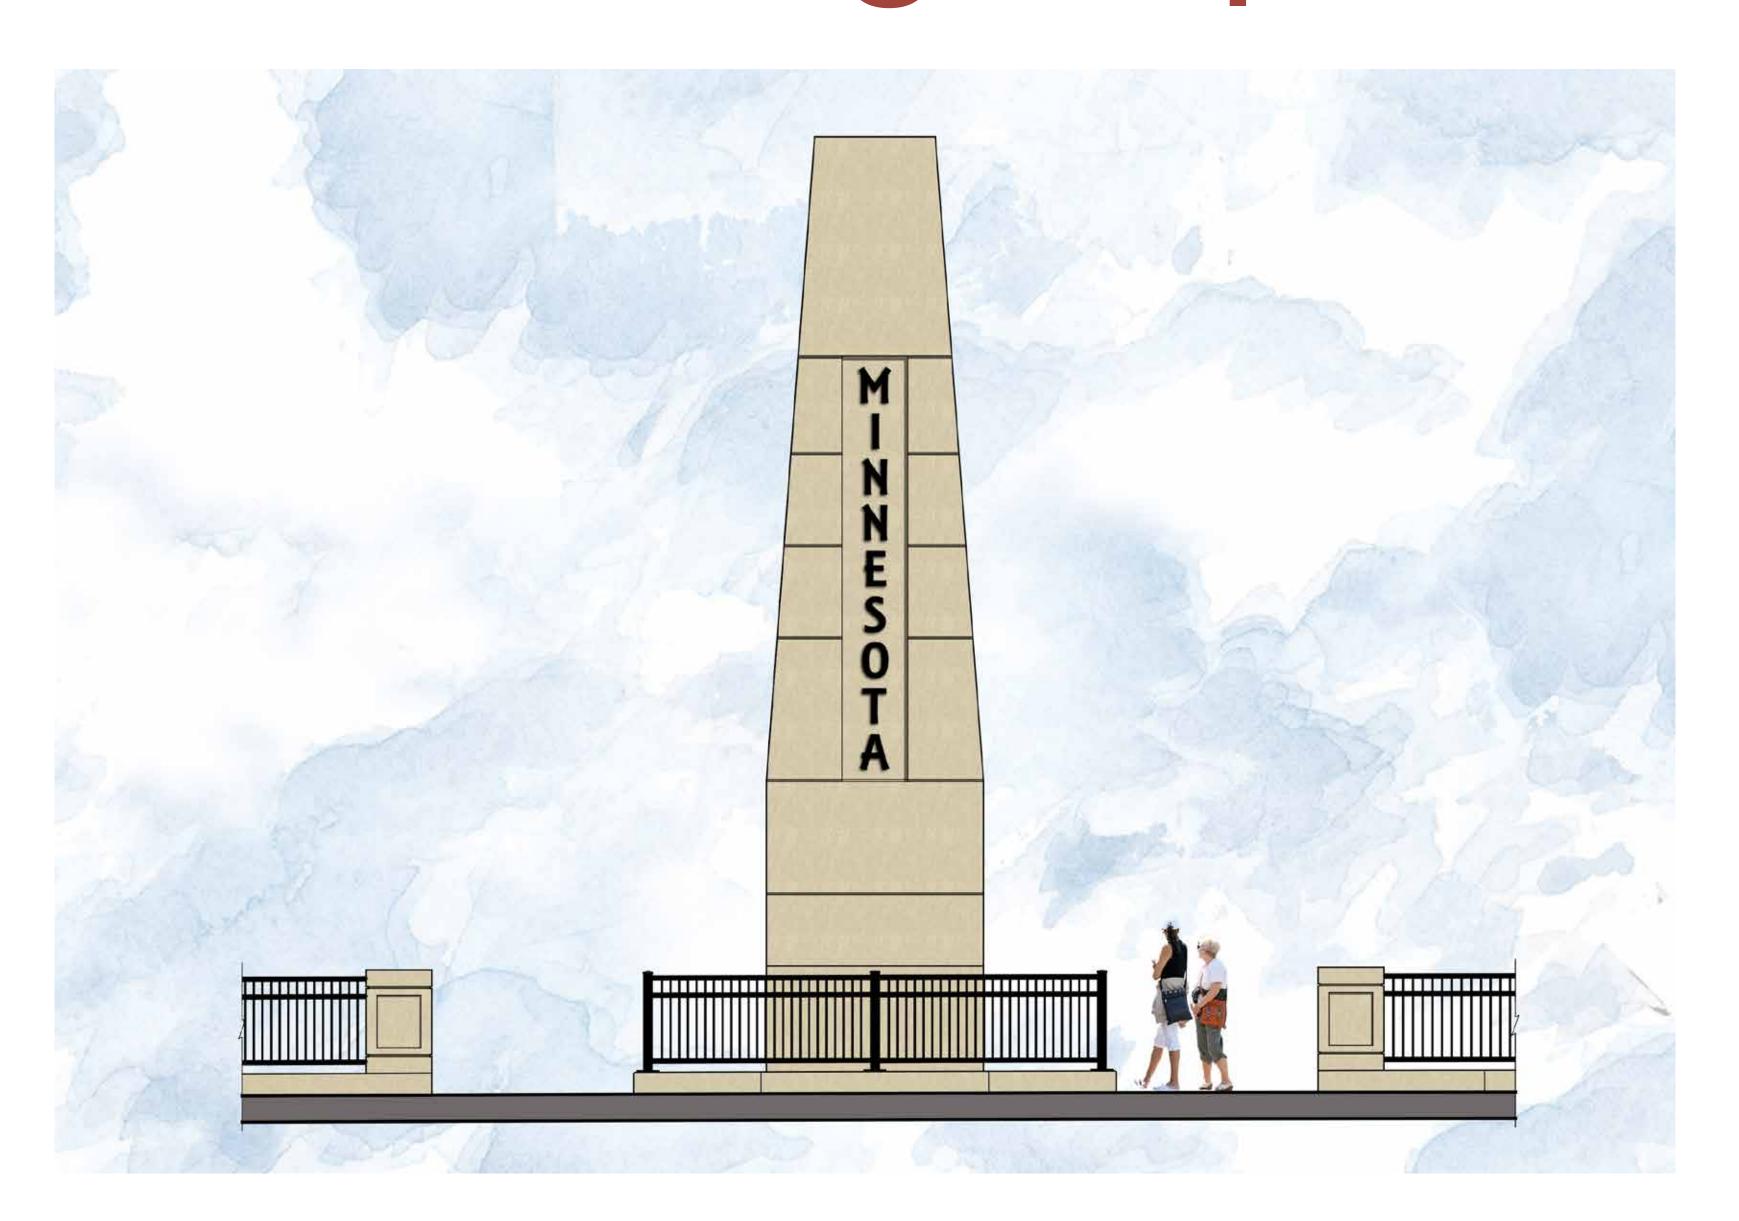

Daytime - Elevation View from Bridge Deck



Daytime - Elevation View from Bridge Deck




Nighttime - Elevation View from Bridge Deck



Nighttime - Elevation View from Bridge Deck

Landscape and Streetscape Design

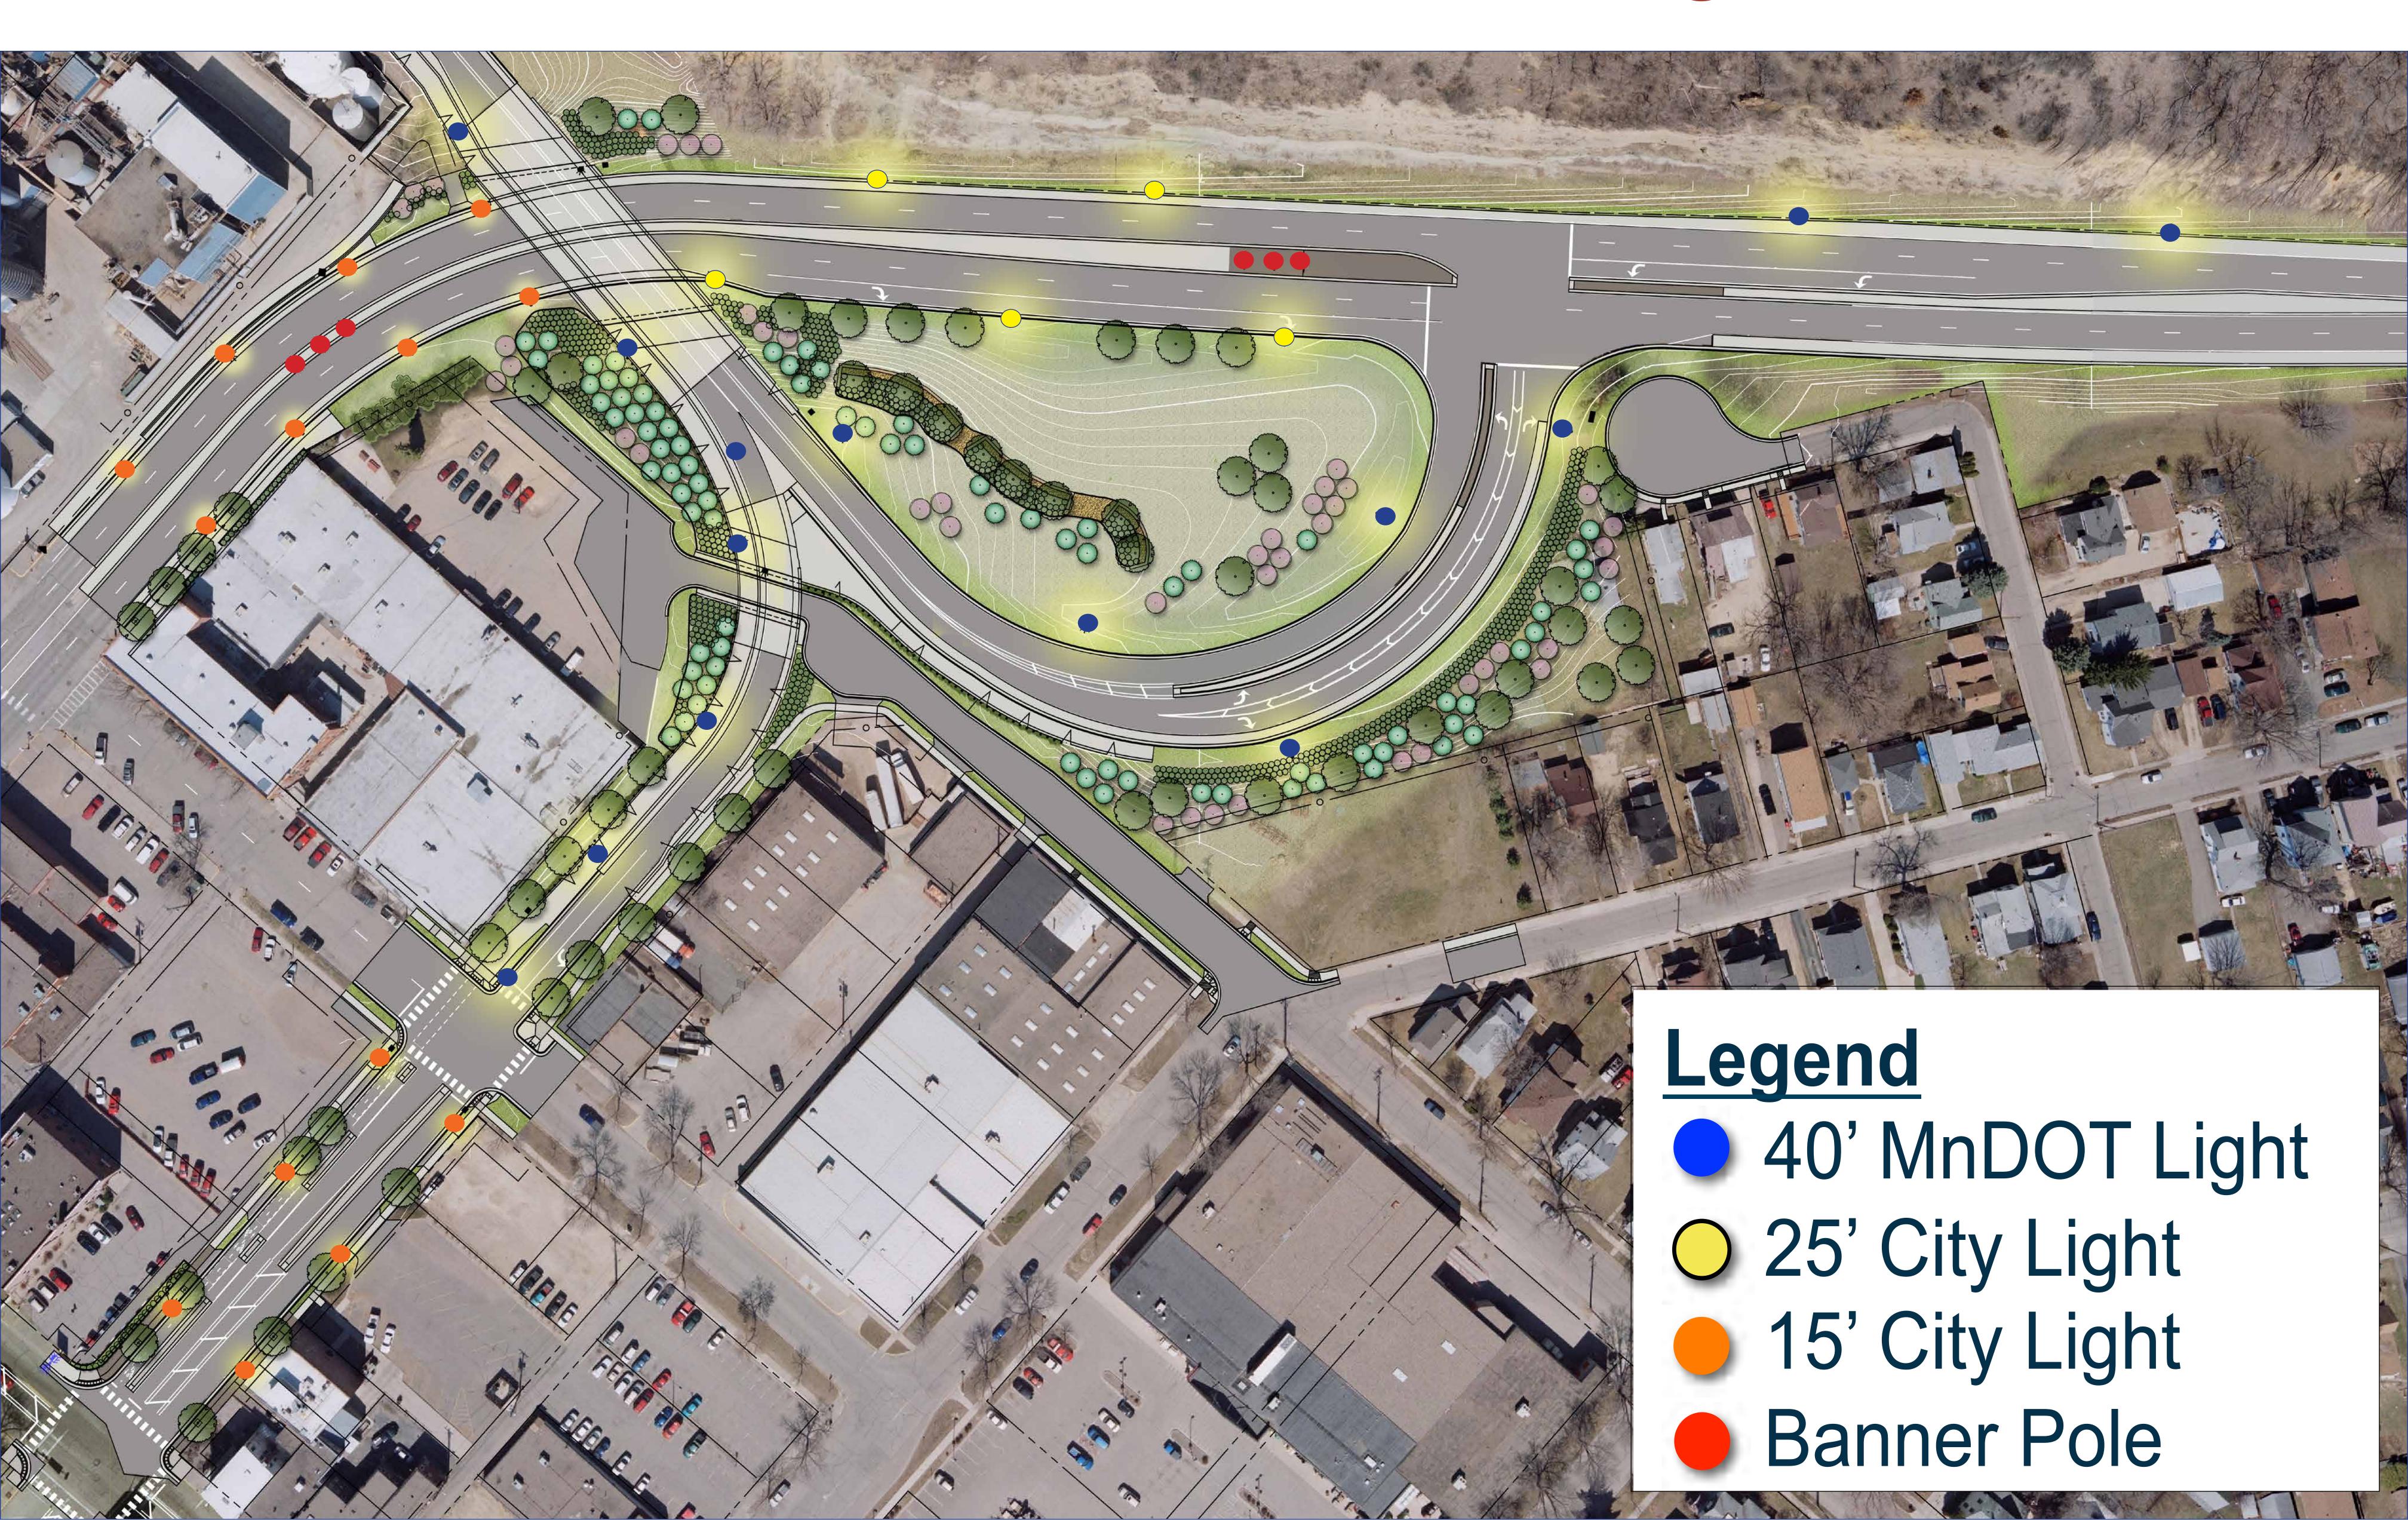


Landscape and Streetscape Design




Staging - 2017 — Stage 1A

Construction

- Begin construction of River Bridge
- Surcharge the poor soils for Wisconsin embankment
- Construct temporary bridge over Hwy 61
- Construct button-hook ramp
- Construct Hwy 61 north of the temporary bridge
- Construct cul-de-sac

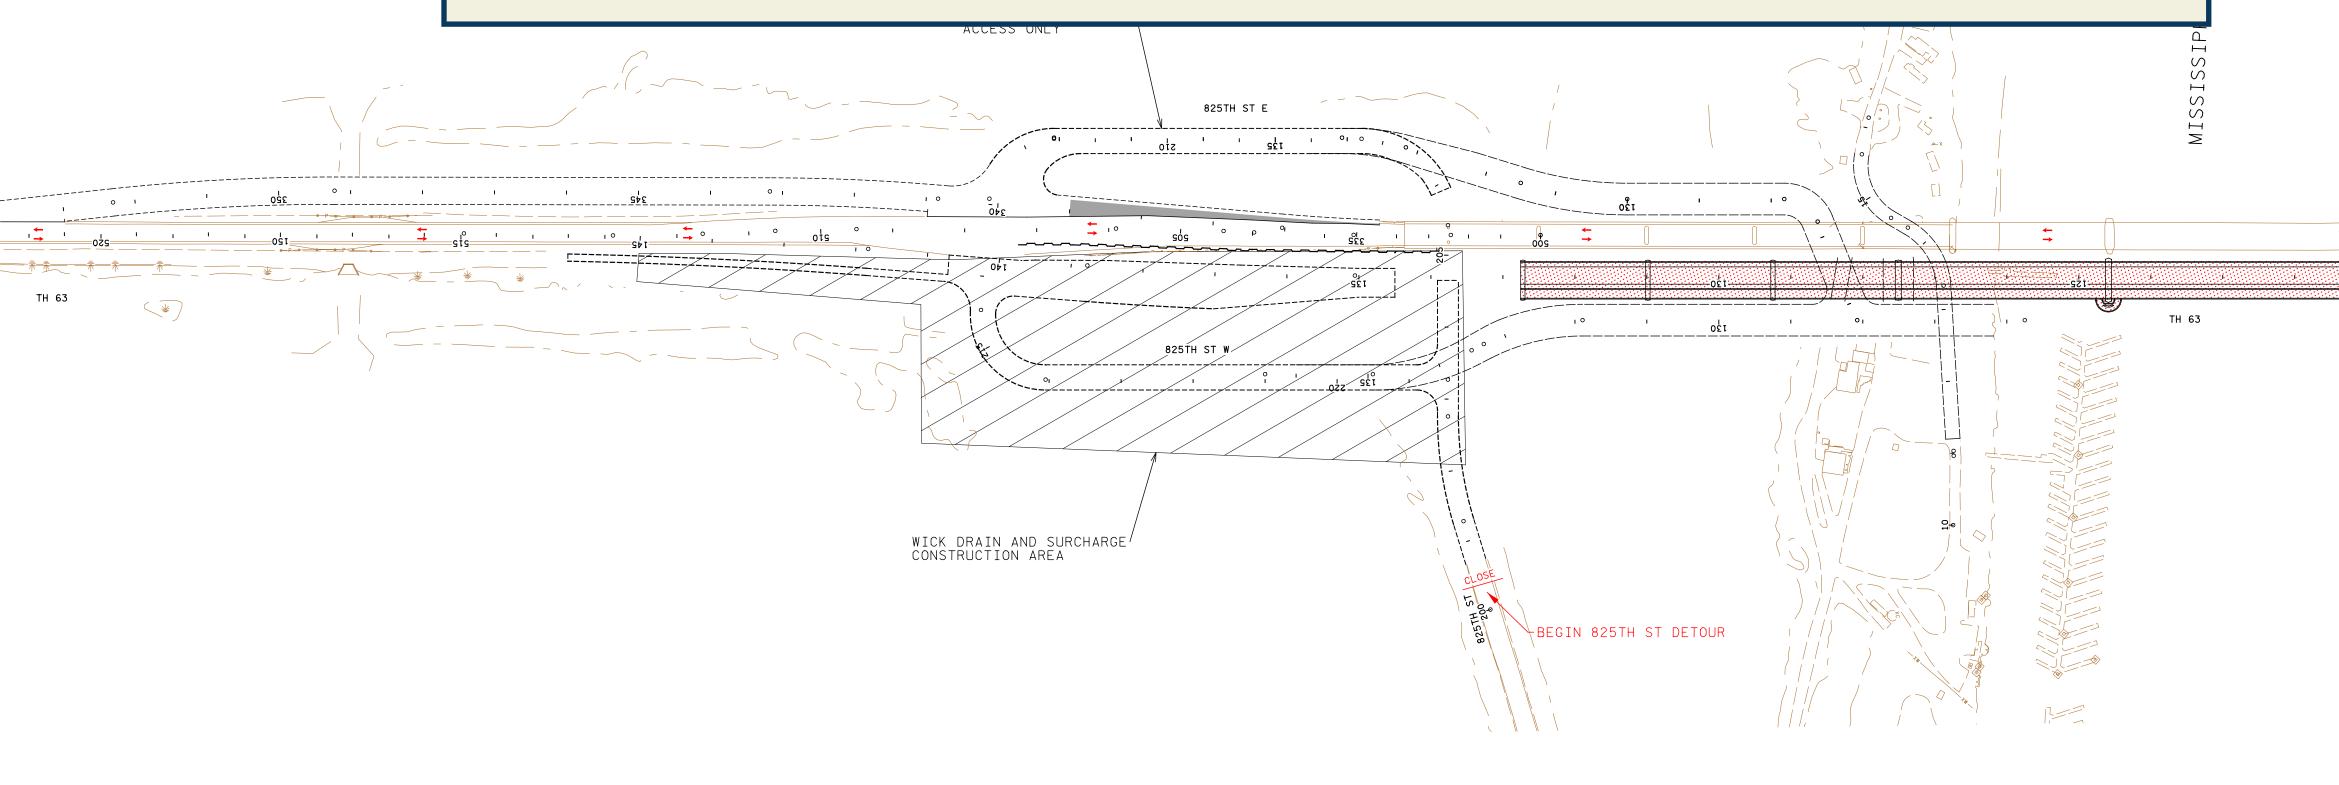


- •Hwy 63 traffic remains on existing River Bridge
- One lane traffic each way on Hwy 61
- •825th St closed at River Bridge and traffic detoured

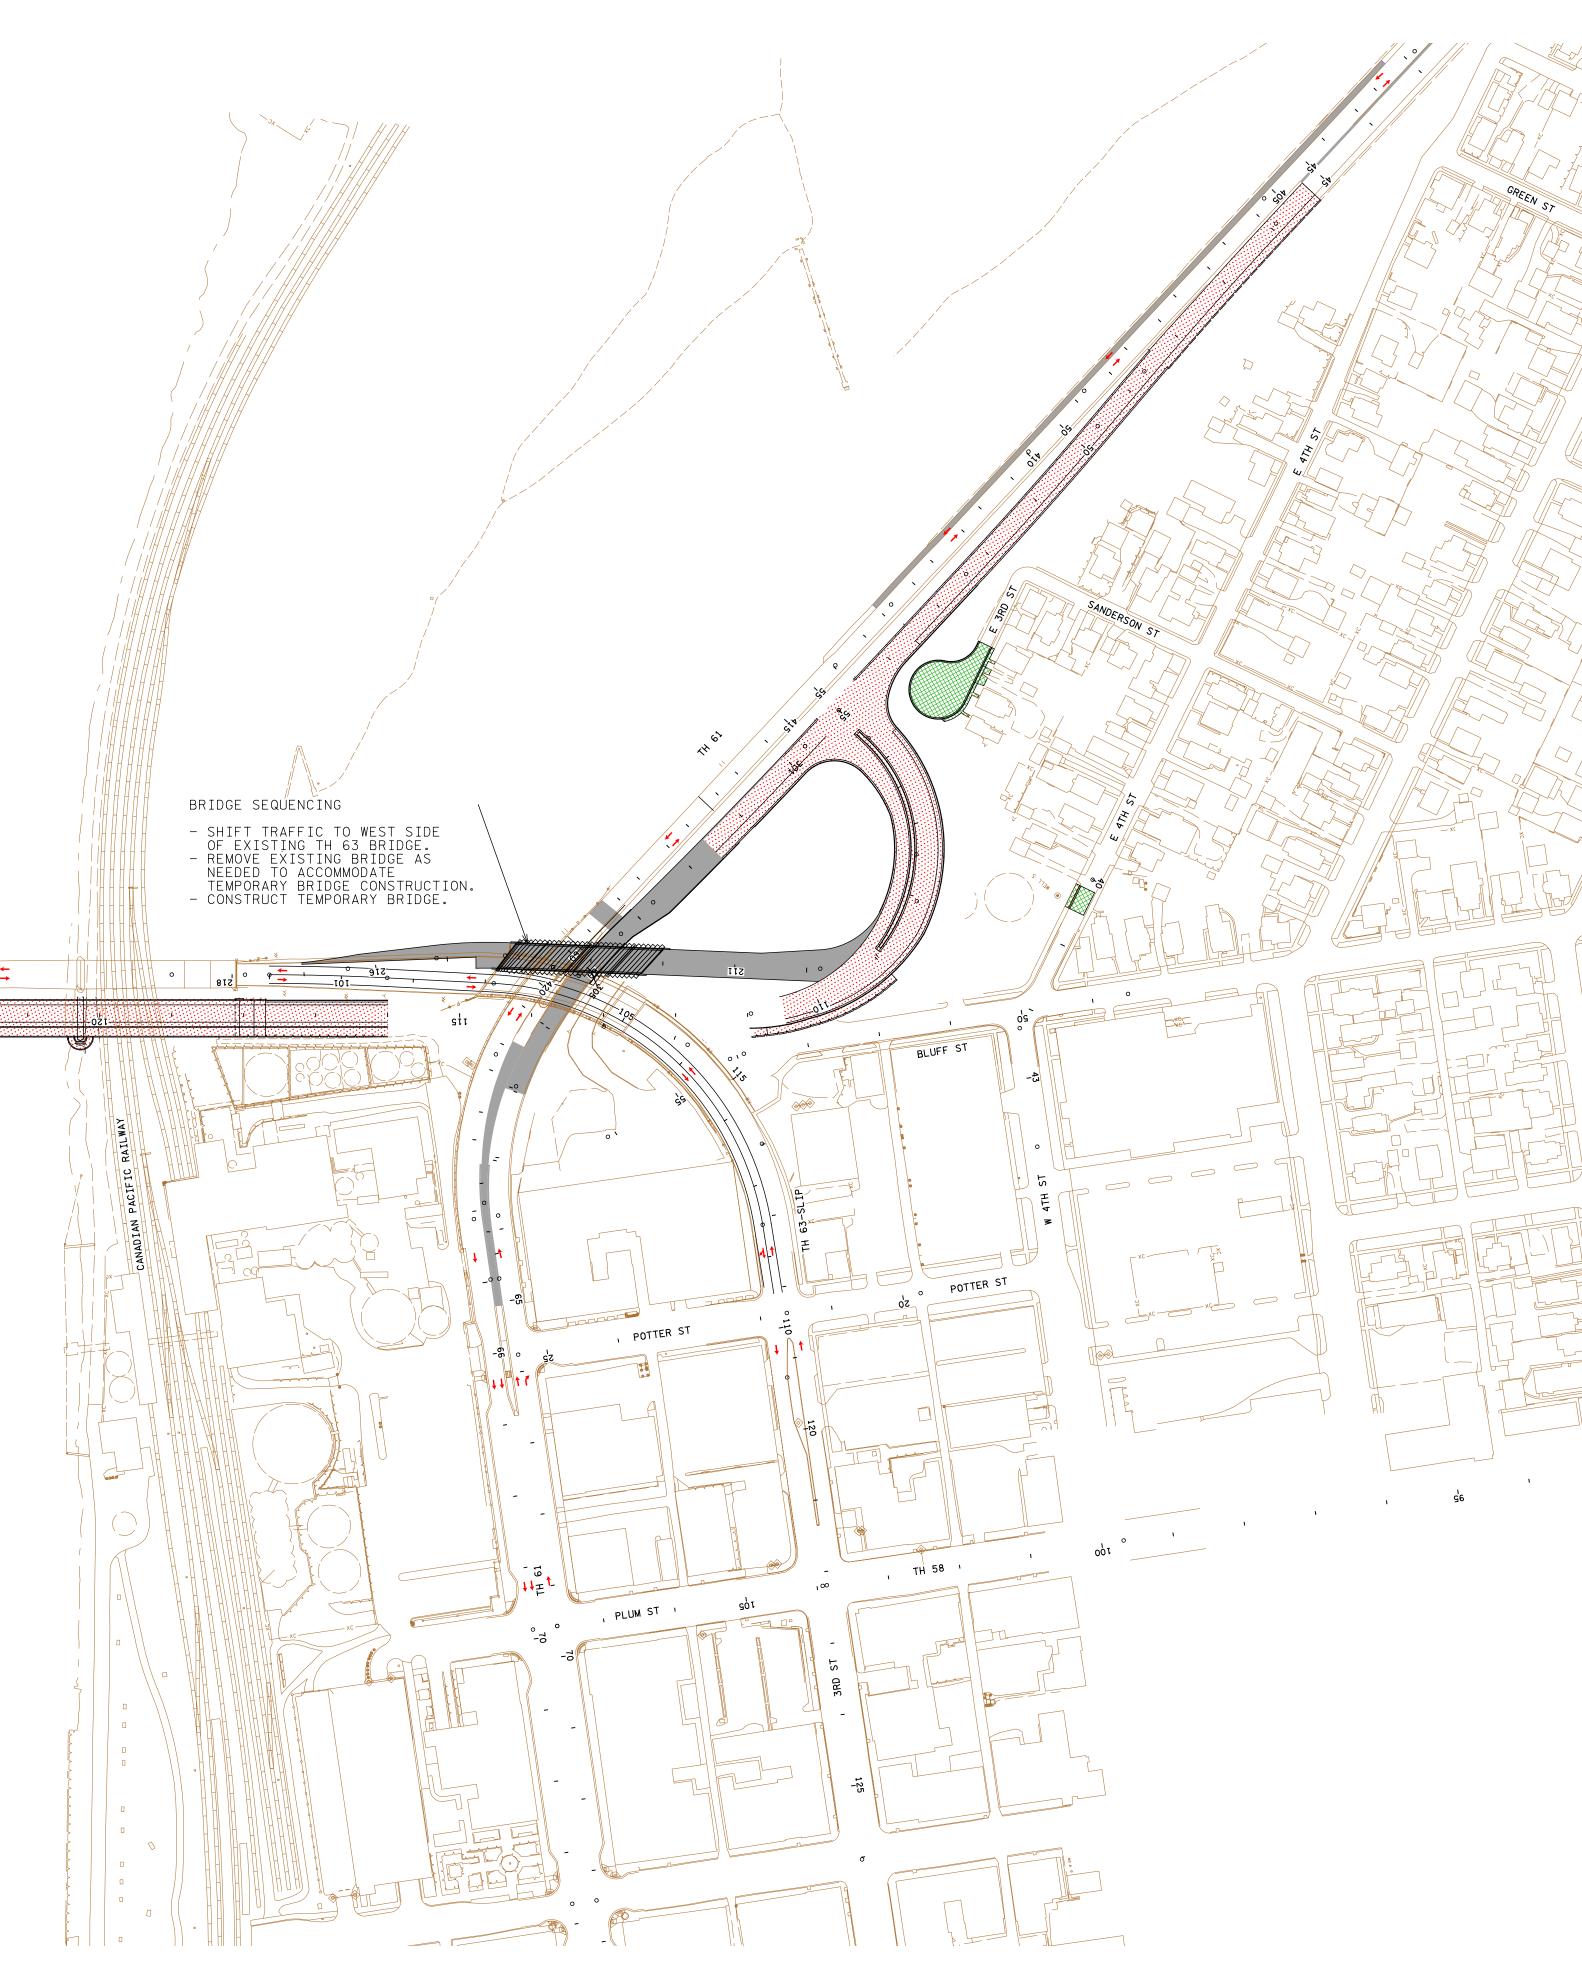


Staging - 2017 — Stage 1B

Construction

- Continue construction of River Bridge
- Surcharge the poor soils for Wisconsin embankment
- Continue construction of temporary bridge over Hwy
 61
- Construct Hwy 61 north of the temporary bridge

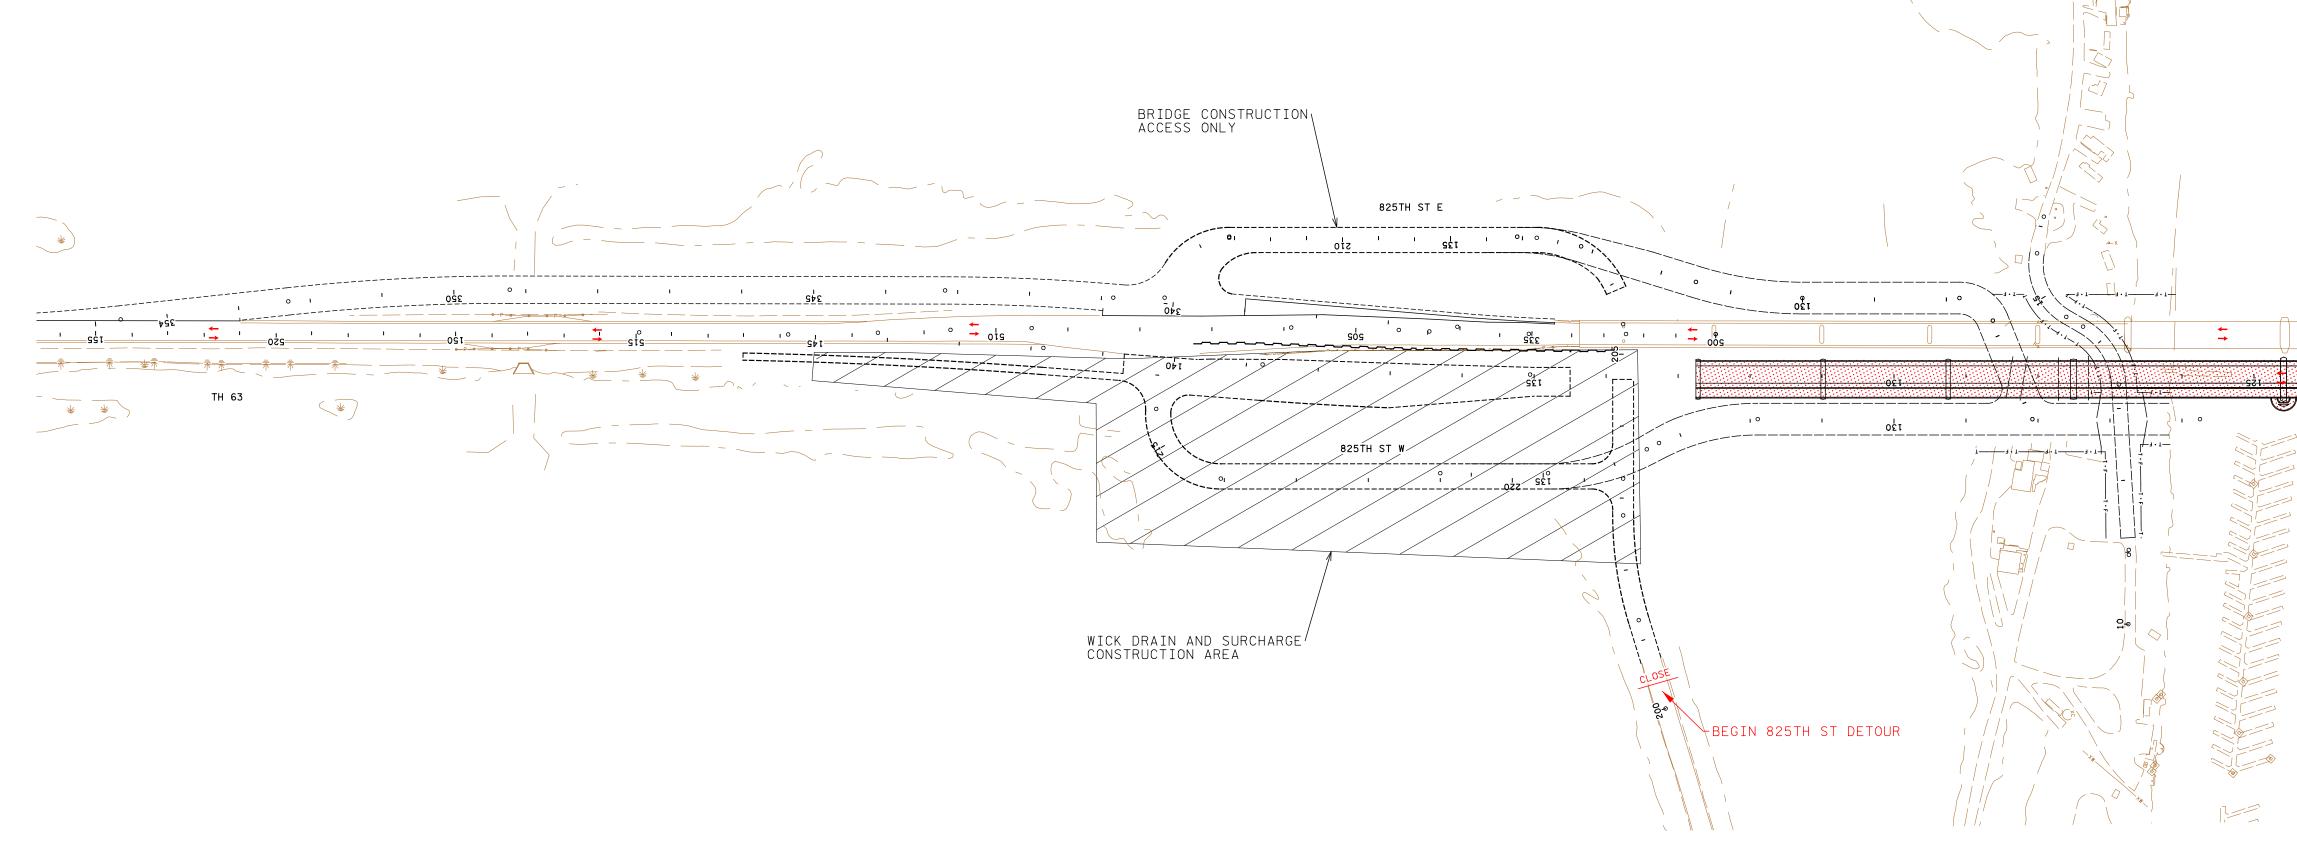


- •Hwy 63 traffic remains on existing River Bridge
- One lane traffic each way on Hwy 61
- •825th St closed at River Bridge and traffic detoured

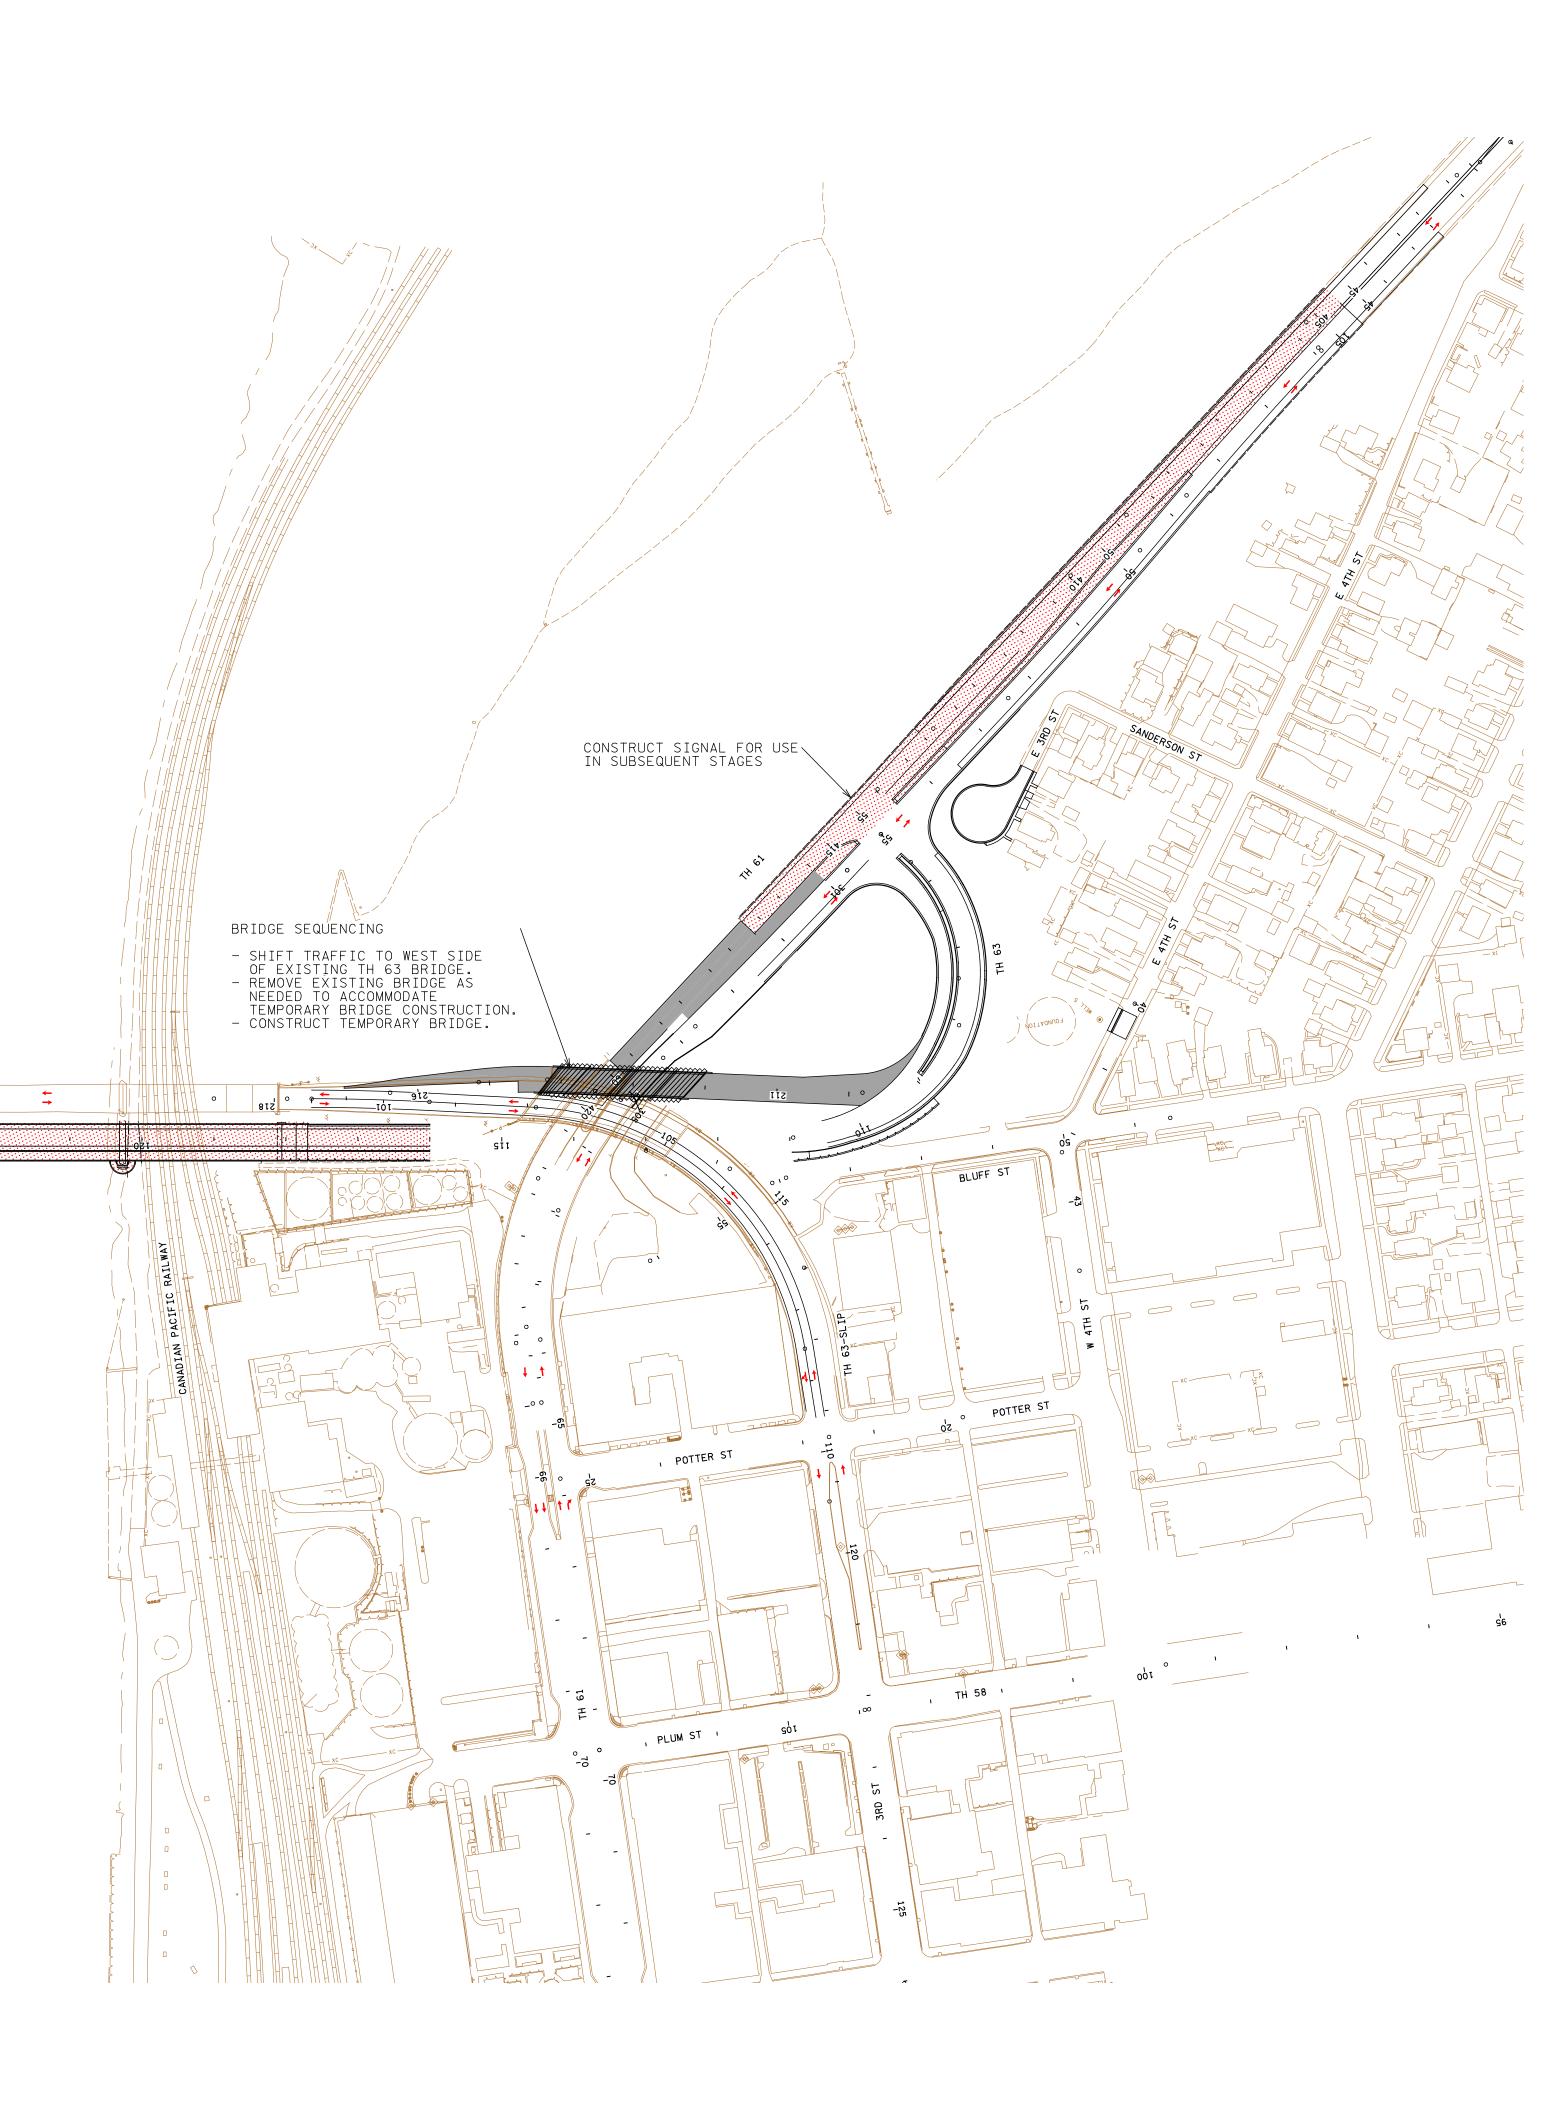

Staging - 2018 - Stage 2

Construction

- Continue construction of River Bridge
- •Construct new bridge over Hwy 61, slip ramp, slip ramp bridge, 3rd Street, and Bluff Street

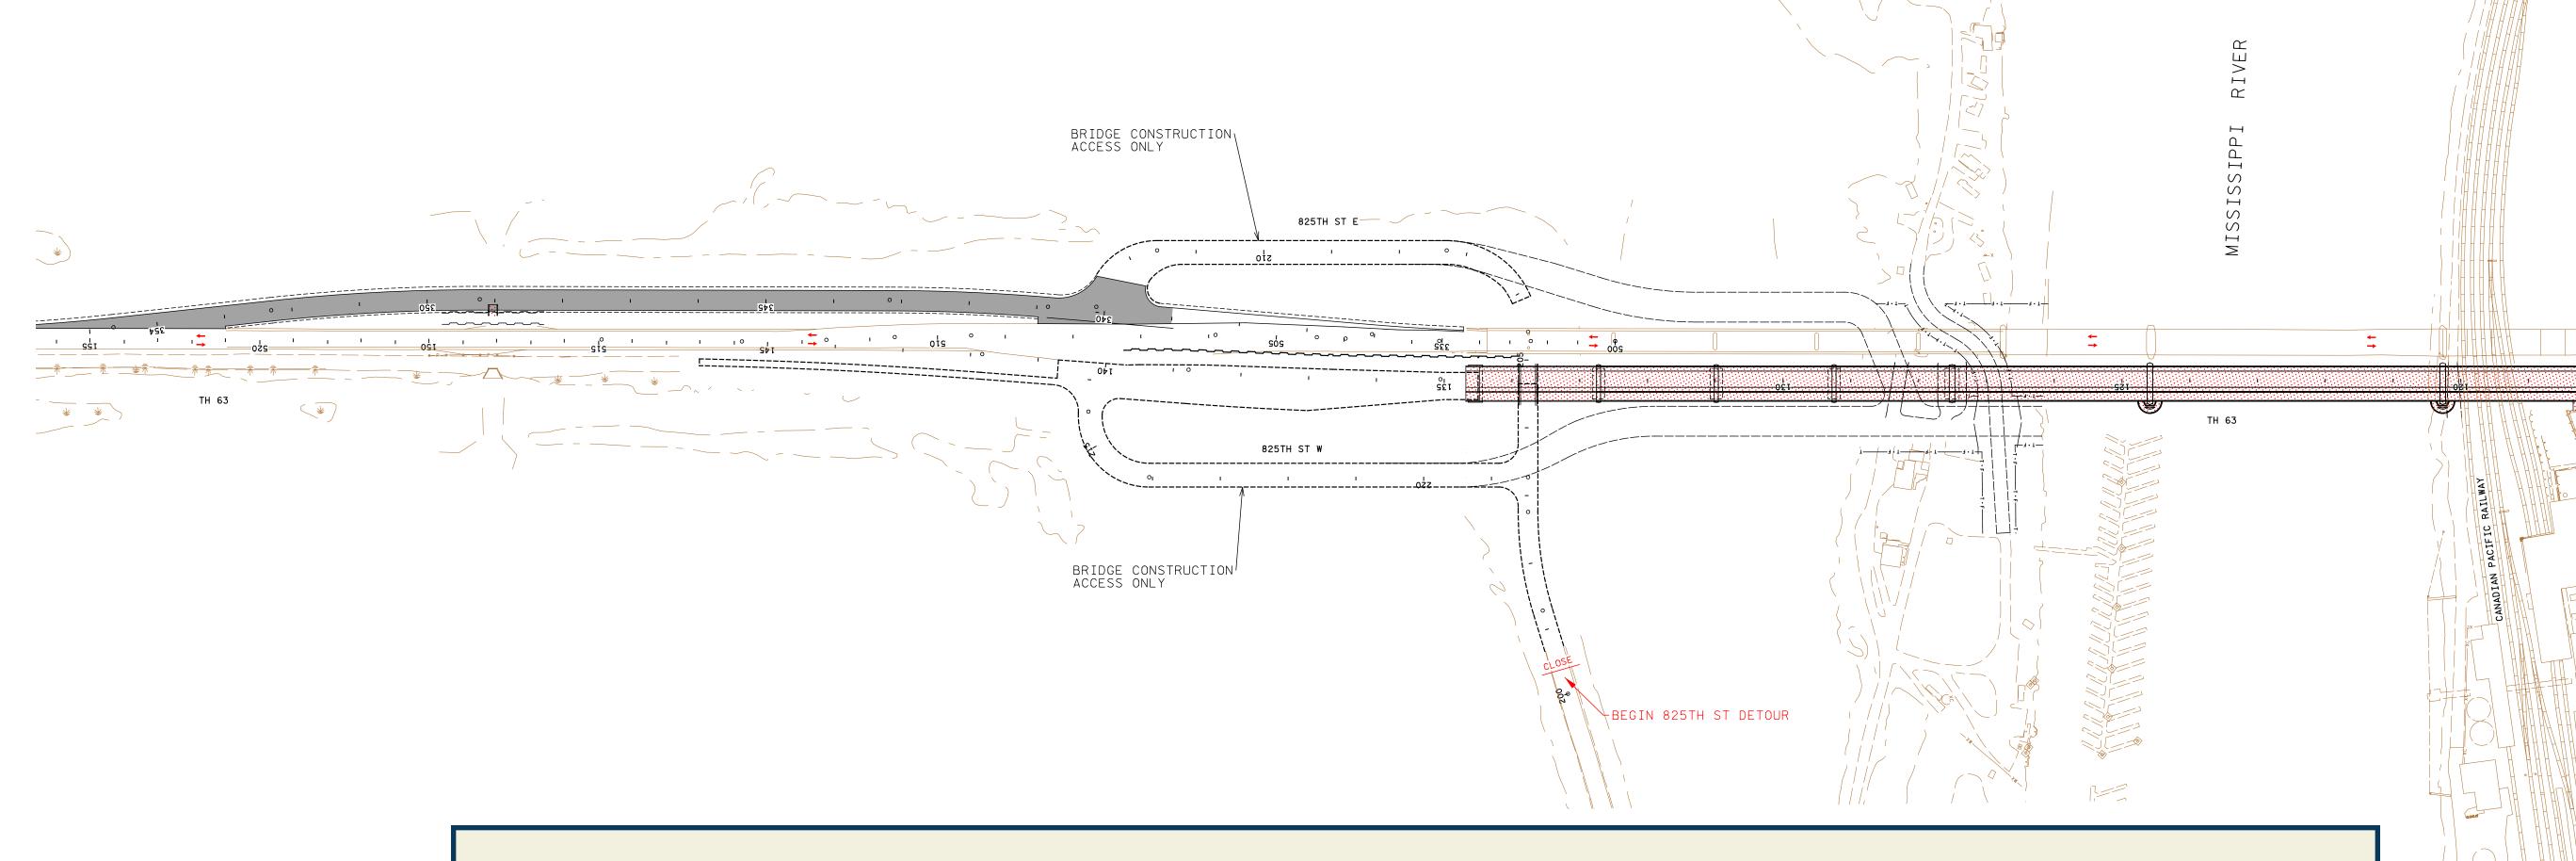


- •Hwy 63 traffic remains on existing River Bridge and routed onto temporary bridge and button-hook ramp to new signalized intersection with Hwy 61
- •825th St closed at River Bridge and traffic detoured
- •Plum/3rd Street intersection changed from traffic signal to all-way stop
- •3rd St closed, traffic allowed thru at Potter St for majority of Stage
- •4 week closure of 3rd/Potter St intersection

Staging - 2019 - Stage 3

Construction

- Continue construction of River Bridge
- Construct Hwy 63 in Wisconsin
- Construct Wisconsin box culvert
- Construct 825th St W

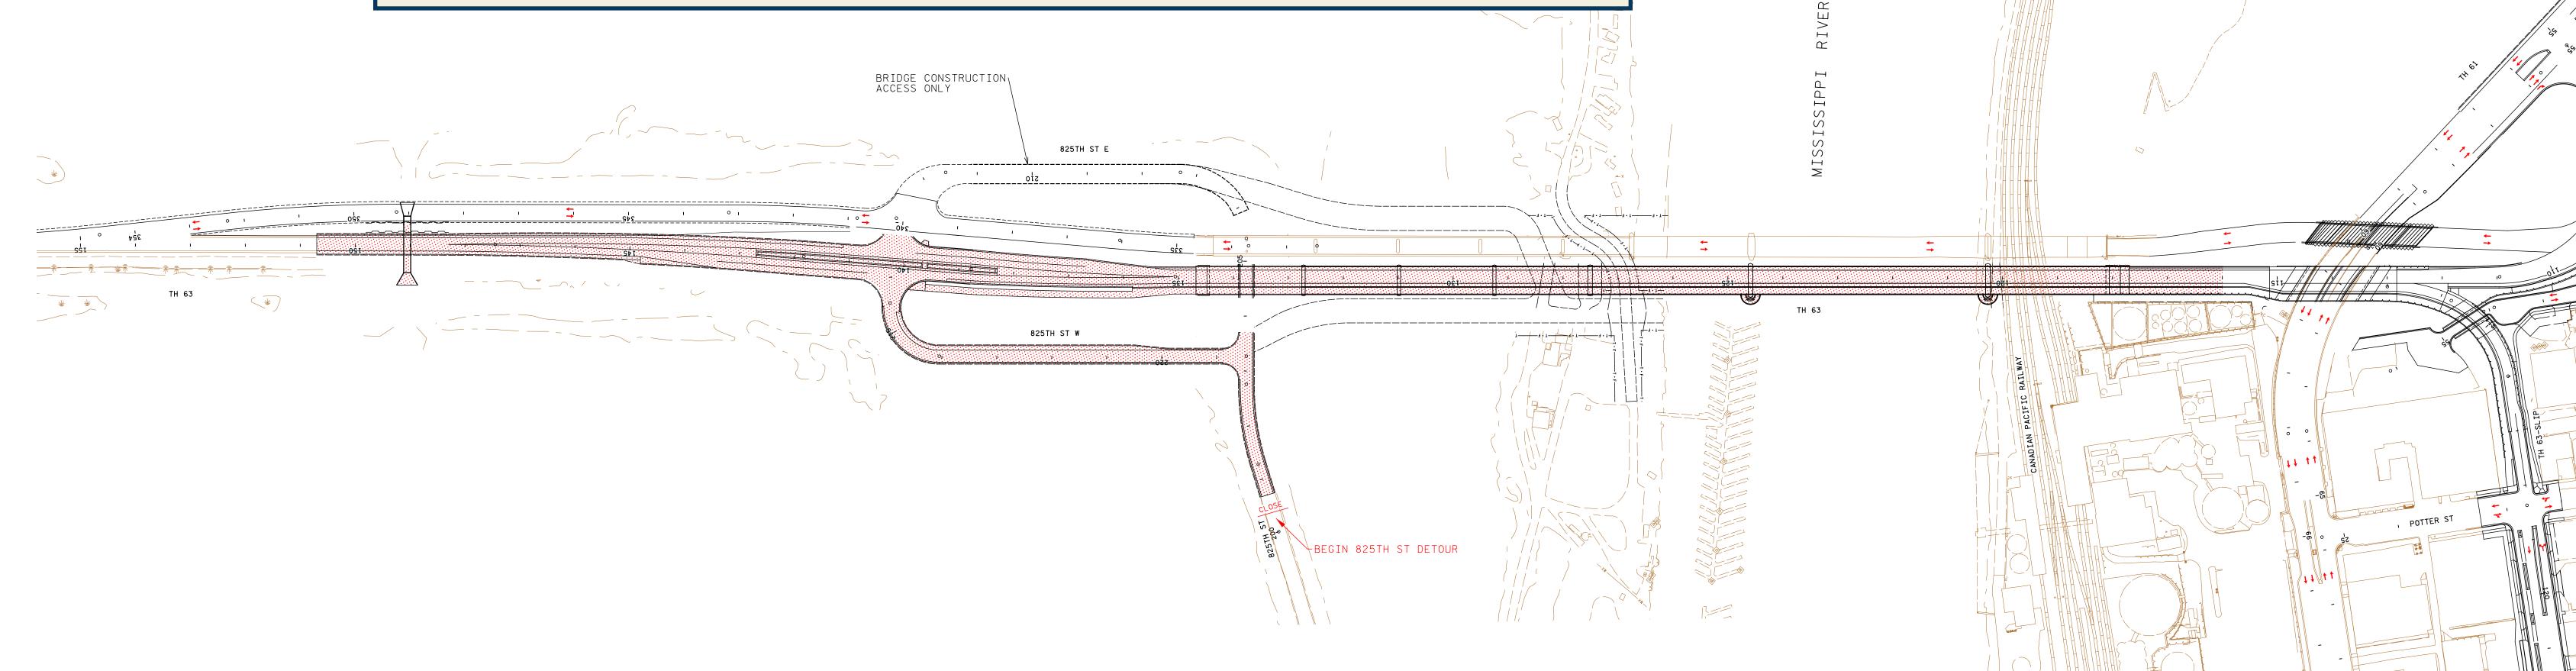

- •Hwy 63 traffic remains on existing River Bridge and routed onto temporary bridge and button-hook ramp to new signalized intersection with Hwy 61
- •Two lane traffic each way on Hwy 61
- •825th St closed at River Bridge and traffic detoured
- •3rd St and Bluff St open
- Slip ramp closed

Staging - 2020 - Stage 4A


Construction

- Construction of River Bridge complete, remove existing River Bridge
- •Construct Hwy 61 under Hwy 63 bridge
- Remove temporary bridge

only. All other traffic detoured.

slip ramp

•Highway 63 complete in Minnesota & Wisconsin, including

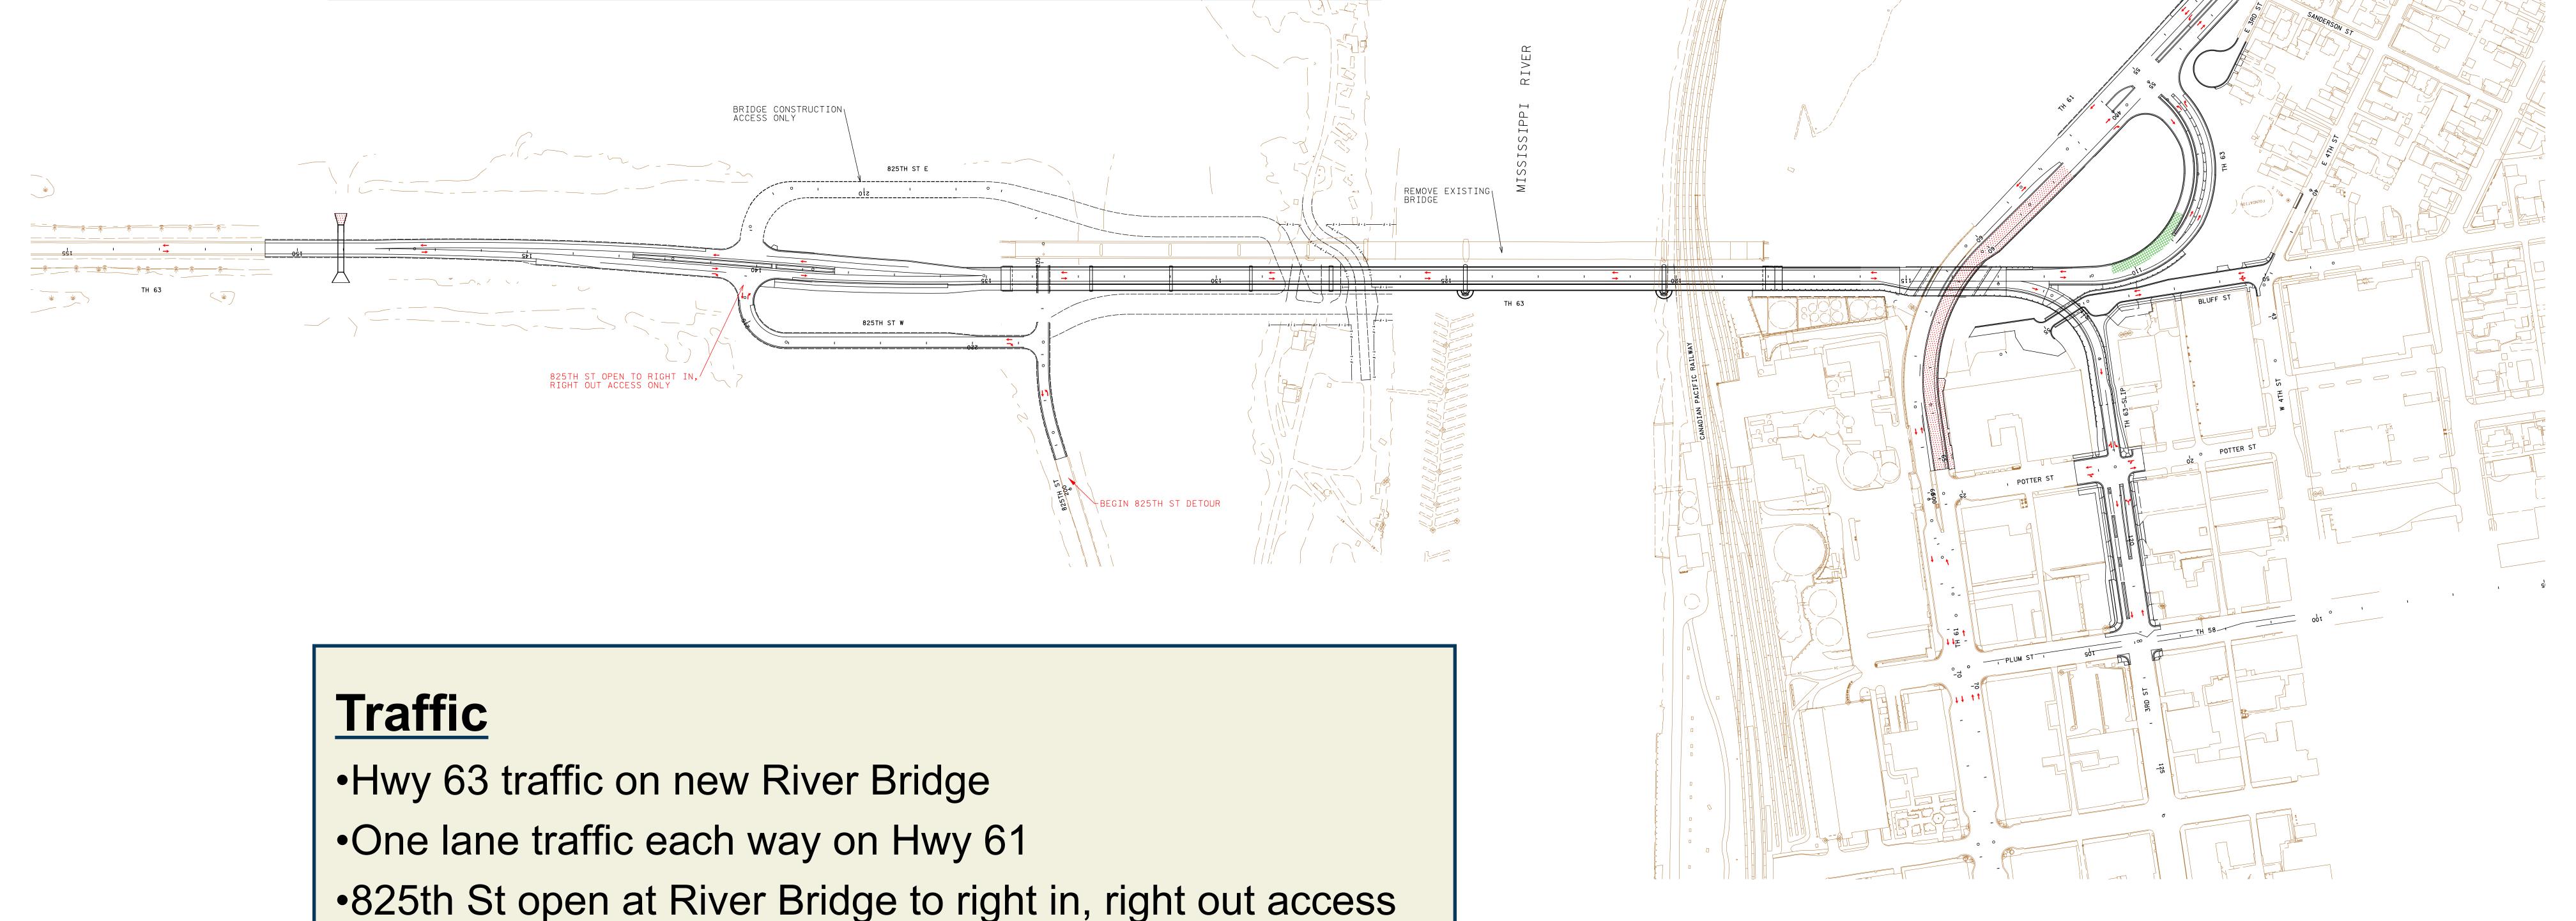

Staging - 2020 - Stage 4B


Construction

- •Construction of River Bridge complete, remove existing River Bridge
- Construct Hwy 61 under Hwy 63 bridge

access only. All other traffic detoured.

slip ramp

•Highway 63 complete in Minnesota & Wisconsin, including

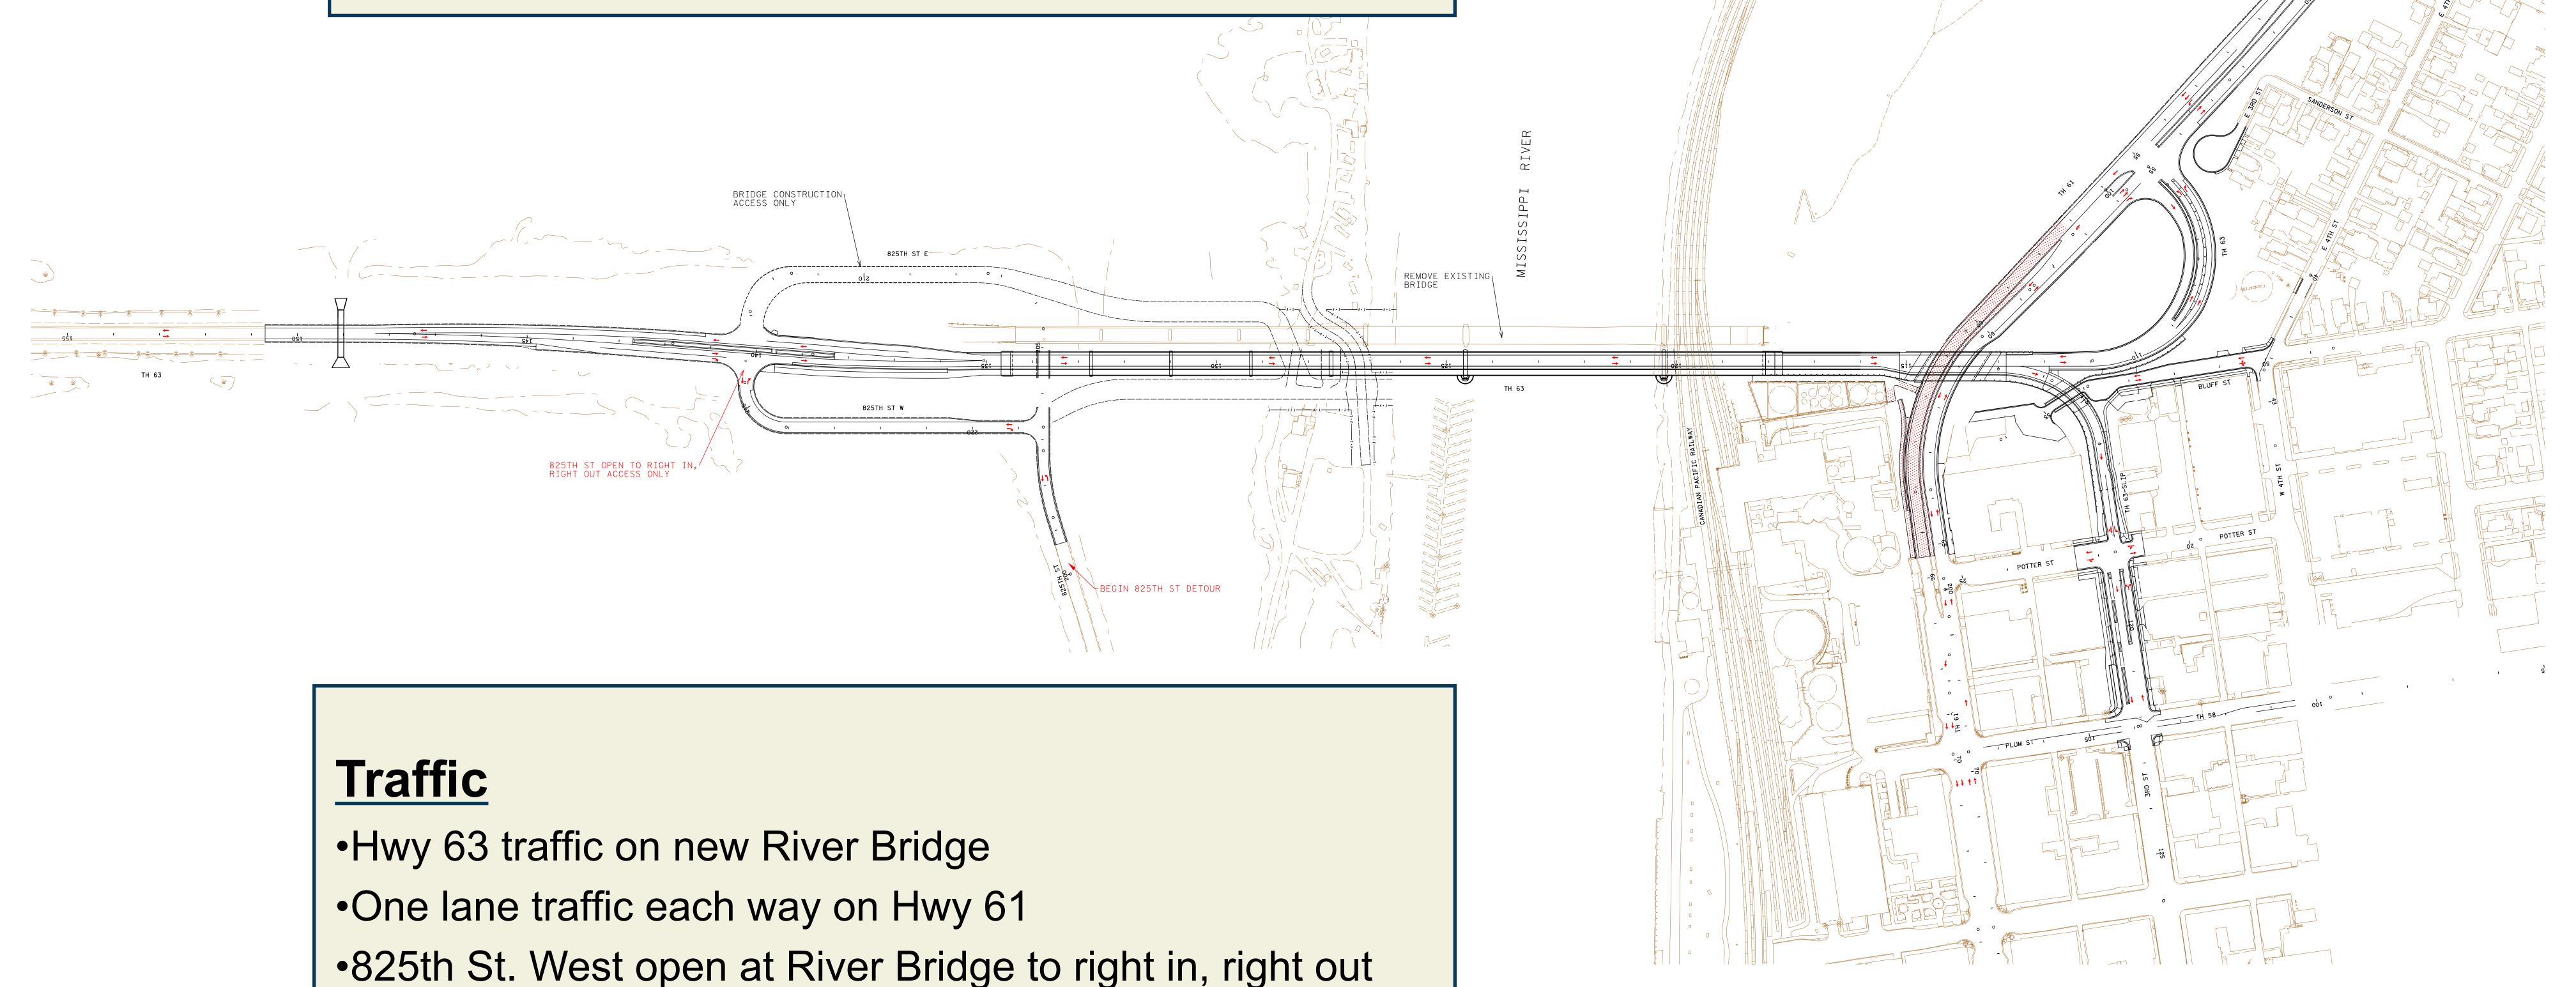

Staging - 2020 - Stage 5



 Construction of River Bridge complete, remove existing River Bridge

•825th St open at River Bridge to right in, right out access


•Highway 63 complete in Minnesota & Wisconsin, including

Construct median on Highway 61

only. All other traffic detoured.

slip ramp

•Construct 825th St E

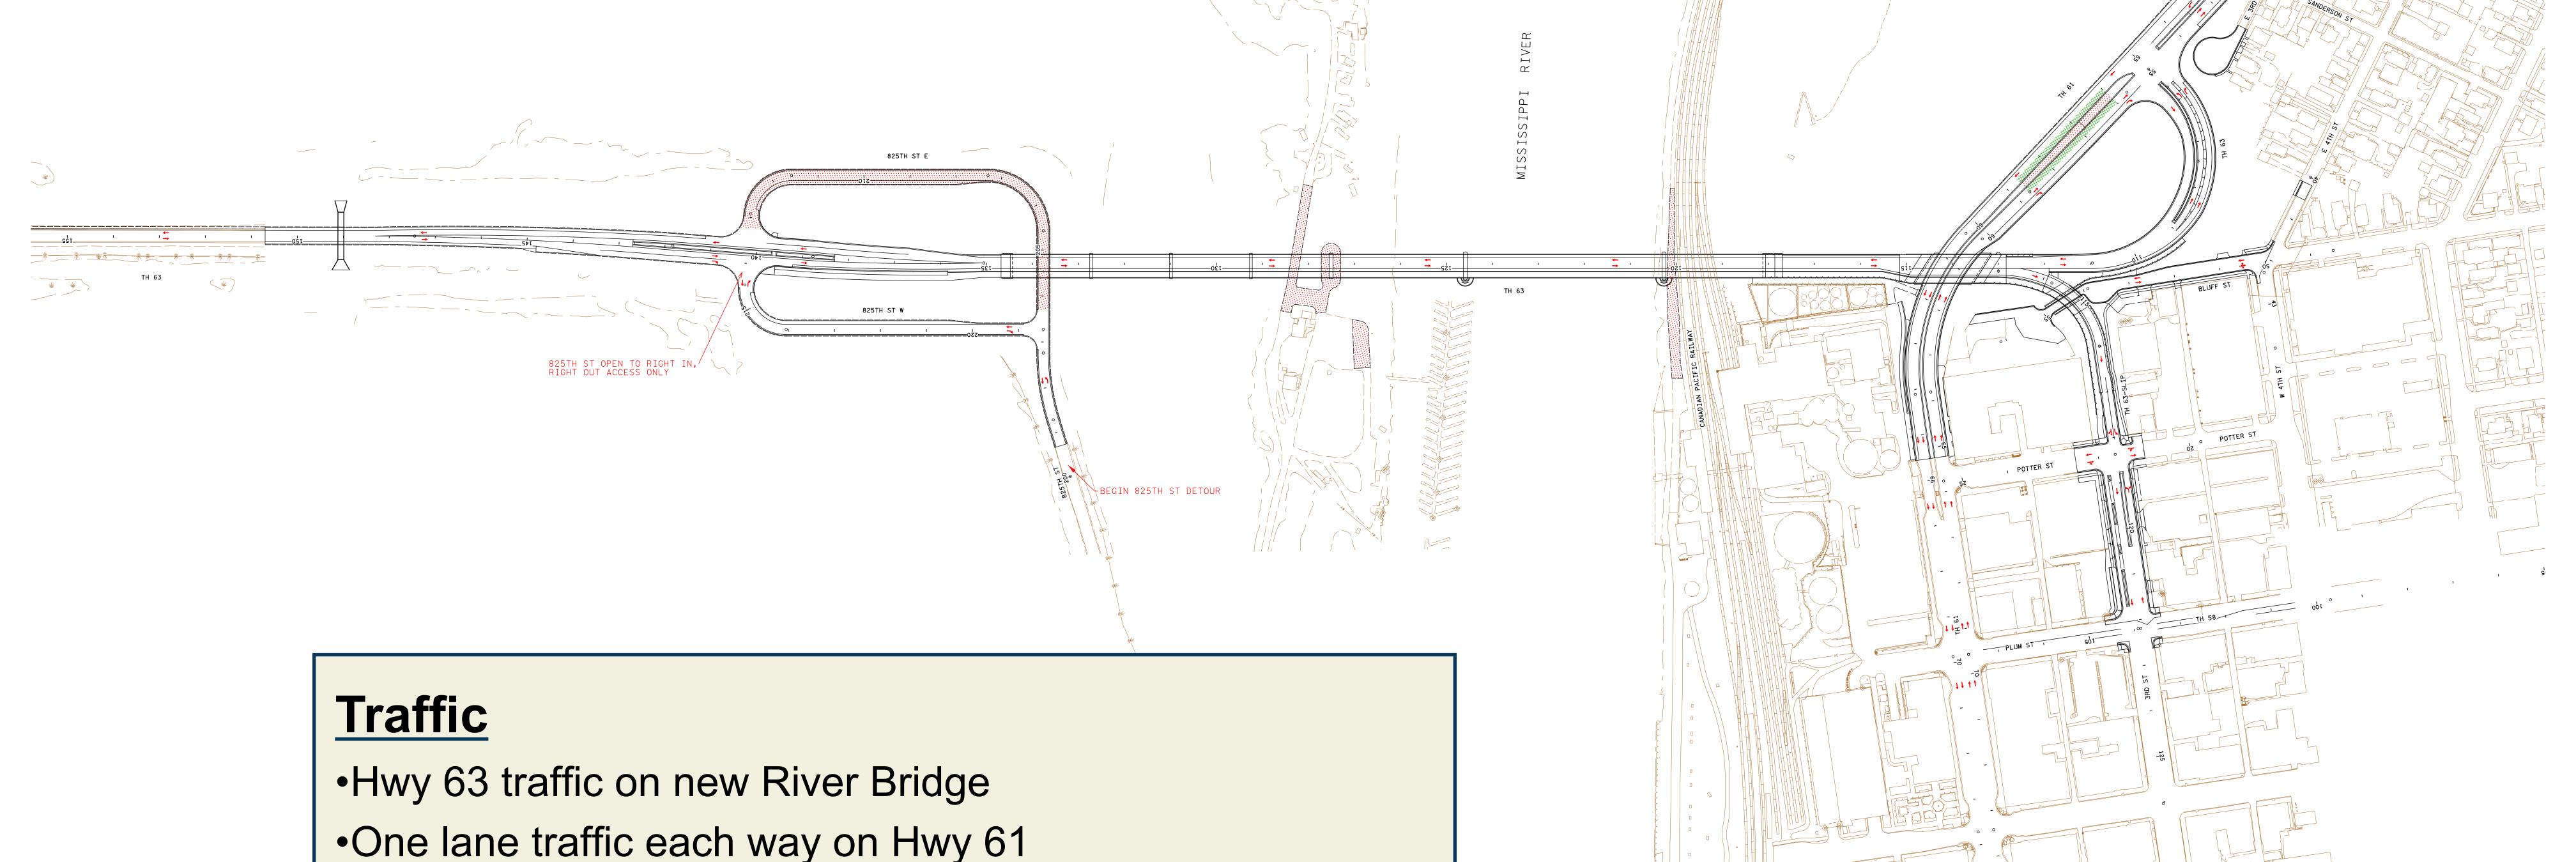

WELCOME



RED WING BRIDGE PROJECT

US 63 River Bridge and Approach Roadways

Open House



November 2016



BAND (

US 63 River Bridge and Approach Roadways



November 2016



US 63 River Bridge and Approach Roadways



November 2016
