


PROJECT SUMMARY

Hwy 25

From Foley to the Benton/Morrison County line


State Project No. 0508-13

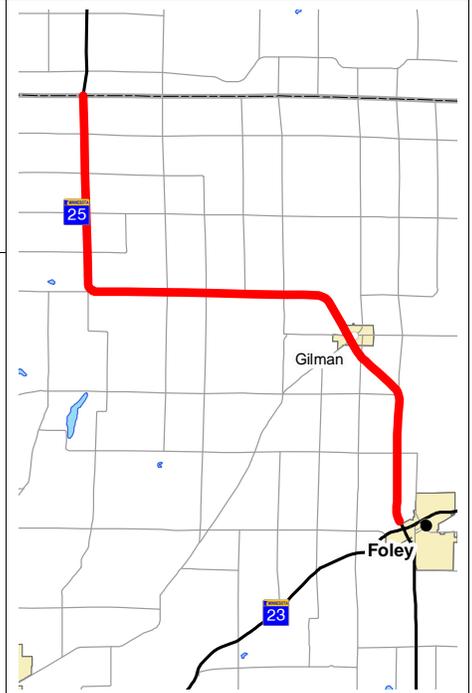

Primary Purpose:

Performance-based Need: Pavement Condition

Investment Category:

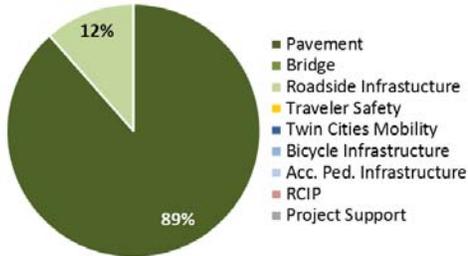

Project Description:

Resurfacing of the road from Foley to the Benton/Morrison County line.

Recent Changes and Updates

None.

Project History:

Deteriorating pavement condition requires resurfacing of this segment.

Total Project Cost Estimate (millions)

Date in which the project entered into the STIP: 2014

	<u>Baseline Est.</u>	<u>Current Est.</u>
Construction Letting:	\$ 6.6	\$ 6.6
Other Construction Elements:	\$ 0.0	\$ 0.0
Engineering:	\$ 1.3	\$ 1.3
Right of Way:	\$ 0.0	\$ 0.0
Total:	\$ 7.9	\$ 7.9

Construction cost estimates are adjusted to the mid-year of construction, using inflation rates provided by OTSM.

Key Cost Estimate Assumptions:

Estimate based on construction cost per mile of similar projects, adjusted for inflation.

Project Risks:

No significant risks are anticipated.

Schedule:

Environmental Approval Date: Not Started
 Municipal Consent Approval Date: Not Required
 Geometric Layout Approval Date: Not Required
 Construction Limits Established Date: Not Needed
 Original Letting Date: 10/27/2017
 Current Letting Date: 6/23/2017
 Construction Season: 2018
 Estimated Substantial Completion: Fall 2017



Minnesota Department of Transportation
 District 3
 7694 Industrial Boulevard
 (218) 828-5700

District Engineer: Dan Anderson
Project Manager: Claudia Dumont

Revised Date: 12/15/2015
