


PROJECT SUMMARY

Hwy 63
 County Road 16 interchange
 Bridge 55040
 State Project No. 5509-80


<http://www.co.olmsted.mn.us/planning/trnsprtng/plng/2015airportinterchange/Pa>

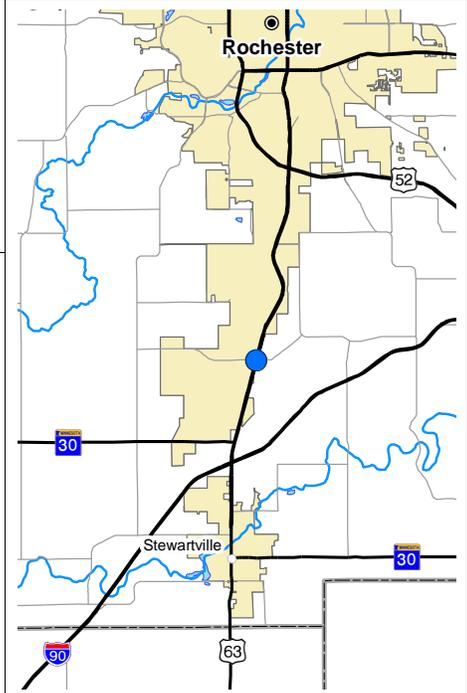

Primary Purpose:

Performance-based Need: District Safety Plan, TED Project

Investment Category:



Project Description:

This project will reconstruct the interchange of Hwy 16 and Hwy 63 in Olmsted county to address existing functional deficiencies. This design includes addressing inadequate sight distance, a narrow bridge deck, lack of turn lanes at ramp junctions, limited accommodation for non-motorized travel and poor access management within the interchange area.

The bridge reconstruction will also incorporate space for pedestrians and bicyclists to enhance safety on Hwy 16.

Recent Changes and Updates

The project was let on 6/2/15.
 Olmsted County is lead agency.

Project History:

The purpose of the project is to address existing functional deficiencies including: inadequate sight distance, a narrow bridge deck, lack of turn lanes at ramp junctions, limited accommodation for non-motorized travel and poor access management within the interchange area. Olmsted County was awarded a TED grant in July 2013 for \$2.224 million. Olmsted County will be the lead on this project, with oversight provided by MnDOT District 6 design staff. Project will be locally let.

Total Project Cost Estimate (millions)

Date in which the project entered into the STIP: 2013

	<u>Baseline Est.</u>	<u>Current Est.</u>
Construction Letting:	\$ 8.9	\$ 7.0
Other Construction Elements:	\$ 0.1	\$ 0.1
Engineering:	\$ 2.2	\$ 2.2
Right of Way:	\$ 0.4	\$ 0.4
Total:	\$ 11.6	\$ 9.7

Construction cost estimates are adjusted to the mid-year of construction, using inflation rates provided by OTSM.

Key Cost Estimate Assumptions:

The current estimate reflects the let amount.

Project Risks:

No further project risks are anticipated at this time

Schedule:

Environmental Approval Date: 09/09/2013
 Municipal Consent Approval Date: 1/5/15
 Geometric Layout Approval Date: 10/07/2014
 Construction Limits Established Date: 03/11/2014
 Original Letting Date: 02/16/2015
 Current Letting Date: 5/15/2015
 Construction Season: 2015/2016
 Estimated Substantial Completion: 11/2016



Minnesota Department of Transportation
 District 6
 2900 48th Street NW
 (507) 286-7500

District Engineer: Jeff Vlamincik
Project Manager: Jai Kalsy

Revised Date: 12/15/2015
