


## PROJECT SUMMARY


Hwy 250  
 Bridges on Hwy 250 in Lanesboro  
 Bridge 6975, 6977  
 State Project No. 2319-16  
[mndot.gov/d6/projects/hwy250-bridge/](http://mndot.gov/d6/projects/hwy250-bridge/)

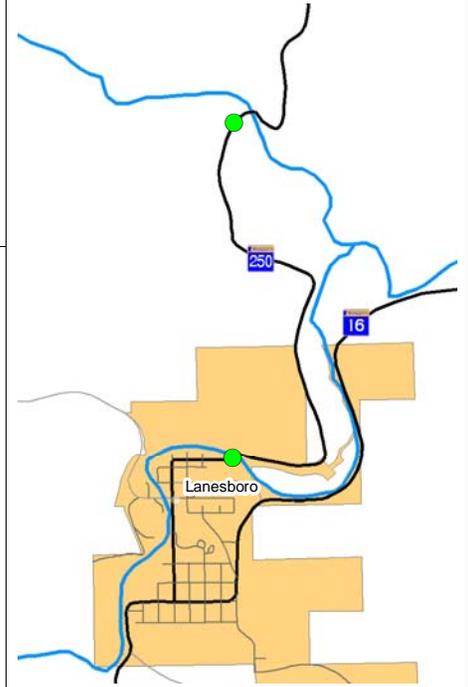

### Primary Purpose:

Performance-based Need: Bridge Condition

### Investment Category:



### Project Description:

The project replaces bridges over the north and south branches of the Root River in and to the north of Lanesboro.

### Recent Changes and Updates

The current estimate is based on updated information in the District 6 work plan (10 year HIP). Letting date changed based upon the optimized letting schedule.

### Project History:

Bridge #6975 was built in 1931 and bridge #6977 was built in 1924. Both structures are classified as functionally obsolete.

### Total Project Cost Estimate (millions)

Date in which the project entered into the STIP: 2013

	<u>Baseline Est.</u>	<u>Current Est.</u>
Construction Letting:	\$ 9.0	\$ 5.7
Other Construction Elements:	\$ 0.0	\$ 0.0
Engineering:	\$ 1.7	\$ 1.1
Right of Way:	\$ 0.3	\$ 0.3
<b>Total:</b>	<b>\$ 11.0</b>	<b>\$ 7.1</b>

*Construction cost estimates are adjusted to the mid-year of construction, using inflation rates provided by OTSM.*

### Key Cost Estimate Assumptions:

The environmental impacts of roadway approach work will not be significant. Traffic will be detoured during construction for bridge #6975.

### Project Risks:

The roadway approach work could lead to significant environmental issues. Right of way acquisition is on schedule.

### Schedule:

Environmental Approval Date: pending  
 Municipal Consent Approval Date: 8/3/15  
 Geometric Layout Approval Date: 05/14/2015  
 Construction Limits Established Date: 05/14/2015  
 Original Letting Date: 01/22/2016  
 Current Letting Date: 02/26/2016  
 Construction Season: 2016  
 Estimated Substantial Completion: 11/2016



Minnesota Department of Transportation  
 District 6  
 2900 48th Street NW  
 (507) 286-7500

**District Engineer:** Jeff Vlamincik  
**Project Manager:** Kjersti Anderson

**Revised Date:** 12/15/2015
