


PROJECT SUMMARY


Old Hwy 14
From west to east Waseca city limits
State Project No. 8103-115

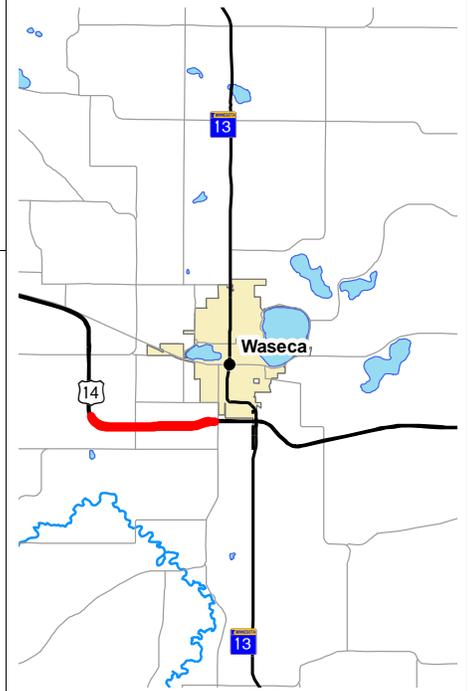

Primary Purpose:

Performance-based Need: Pavement Condition

Investment Category:

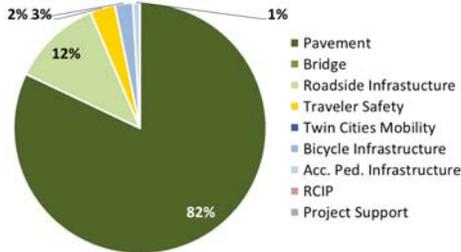

Project Description:

This project consists of the reconstruction of Old Hwy 14 through Waseca. The city will replace the utilities in conjunction with this project. A new concrete surface will be provided with the curb and gutter.

Recent Changes and Updates

The project is being designed at this time. The original baseline was incorrectly entered and has been corrected.

Project History:

The Legislature recently passed the law allowing for the construction of this project according to the Settlement Agreement. The turnback of Old Hwy 14 in Waseca and Steele counties was contested. A Settlement Agreement was created to define what was to be constructed.

Total Project Cost Estimate (millions)

Date in which the project entered into the STIP: 2014

	<u>Baseline Est.</u>	<u>Current Est.</u>
Construction Letting:	\$ 17.8	\$ 17.8
Other Construction Elements:	\$ 1.0	\$ 1.0
Engineering:	\$ 2.7	\$ 2.7
Right of Way:	\$ 0.0	\$ 0.0
Total:	\$ 21.5	\$ 21.5

Construction cost estimates are adjusted to the mid-year of construction, using inflation rates provided by OTSM.

Key Cost Estimate Assumptions:

The estimates for the turnback were performed early in the process. Only a certain amount of money was made available for the entire program on Old Hwy 14, so there is a need to make sure there is enough money for the projects that will come in subsequent years.

Project Risks:

The Settlement Agreement was very prescriptive in some areas and vague in others.

Schedule:

Environmental Approval Date: Pending Approval
Municipal Consent Approval Date: Not Needed
Geometric Layout Approval Date: Not Needed
Construction Limits Established Date: Not Needed
Original Letting Date: 04/15/2016
Current Letting Date: 03/15/2016
Construction Season: May 2016 / Nov 2017
Estimated Substantial Completion: 11/01/2017



Minnesota Department of Transportation
District 7
2151 Bassett Drive
(507) 304-6100

District Engineer: Greg Ous
Project Manager: Matt Rottermond

Revised Date: 12/15/2015
