


PROJECT SUMMARY

Hwy 73


Various locations on Highway 73 and Highway 2 that include the City of Cromwell and the City of Floodwood
State Project No. 6928-28

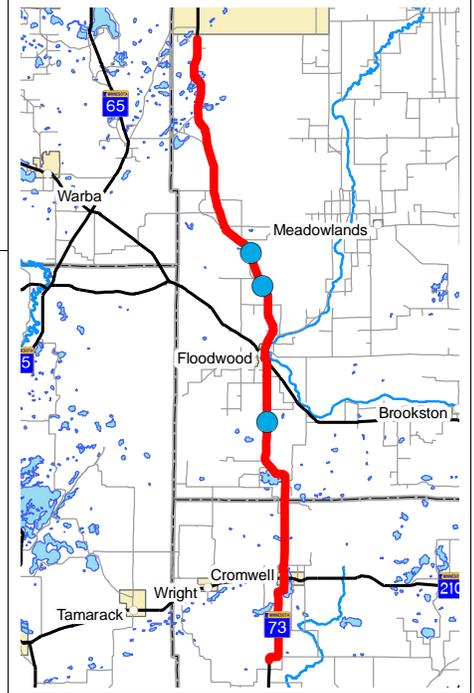

Primary Purpose:

Performance-based Need: Pavement Condition

Investment Category:

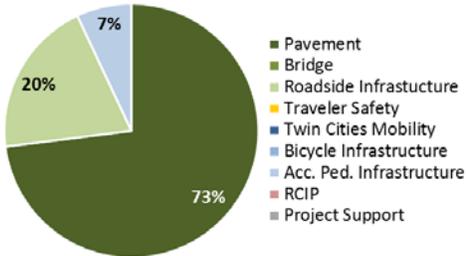

Project Description:

This project is 30 miles long, at several locations along Highway 73 and Highway 2 including the City of Cromwell and the City of Floodwood. Project improvements include: pavement resurfacing, curb ramp construction and sidewalk improvements.

Recent Changes and Updates

The project scoping was completed in August 2015.

Project History:

The need for this project is driven by deteriorating pavement resulting in a rough ride, high maintenance costs, and reduced load carrying capacity.

Total Project Cost Estimate (millions)

Date in which the project entered into the STIP: 2014

	<u>Baseline Est.</u>	<u>Current Est.</u>
Construction Letting:	\$ 8.5	\$ 8.5
Other Construction Elements:	\$ 0.8	\$ 0.8
Engineering:	\$ 1.6	\$ 1.6
Right of Way:	\$ 0.0	\$ 0.0
Total:	\$ 10.9	\$ 10.9

Construction cost estimates are adjusted to the mid-year of construction, using inflation rates provided by OTSM.

Key Cost Estimate Assumptions:

The baseline estimate was prepared in January of 2014 and includes costs for pavement resurfacing and drainage improvements.

Project Risks:

The final pavement recommendation is not complete. The amount of sidewalk replacement needed in Floodwood is not known.

Schedule:

Environmental Approval Date: Pending Approval
Municipal Consent Approval Date: Not Needed
Geometric Layout Approval Date: Not Needed
Construction Limits Established Date: Not Known
Original Letting Date: 01/01/2018
Current Letting Date: 2/23/2018
Construction Season: 2018
Estimated Substantial Completion: 11/01/2018



Minnesota Department of Transportation
District 1
1123 Mesaba Ave
(218) 725-2700

District Engineer: Duane Hill
Project Manager: Michael Kalnbach

Revised Date: 12/15/2015
