


## PROJECT SUMMARY


Hwy 25  
Buffalo  
State Project No. 8604-37

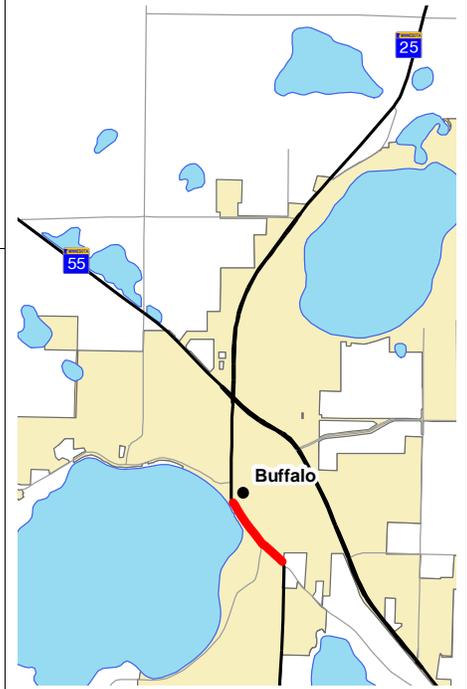

### Primary Purpose:

Performance-based Need: Pavement Condition

### Investment Category:

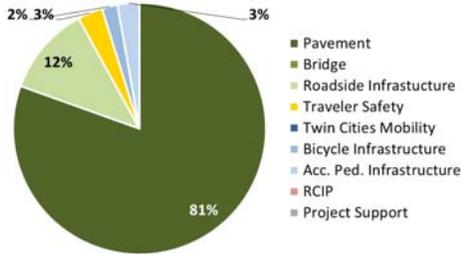

### Project Description:

Reconstruction of the roadway south of 1st St to north of Wright CR 147 in Buffalo, including pedestrian improvements, lighting, and curb and gutter.

### Recent Changes and Updates

New Project

### Project History:

The project was programmed to address deteriorating pavement.

### Total Project Cost Estimate (millions)

Date in which the project entered into the STIP: 2015

	<u>Baseline Est.</u>	<u>Current Est.</u>
Construction Letting:	\$ 5.3	\$ 5.3
Other Construction Elements:	\$ 0.0	\$ 0.0
Engineering:	\$ 1.1	\$ 1.1
Right of Way:	\$ 0.0	\$ 0.0
<b>Total:</b>	<b>\$ 6.4</b>	<b>\$ 6.4</b>

*Construction cost estimates are adjusted to the mid-year of construction, using inflation rates provided by OTSM.*

### Key Cost Estimate Assumptions:

The baseline estimate used estimated quantities and average bid prices.

### Project Risks:

The City of Buffalo has plans for replacement of underground utilities which needs to be coordinated with the project development and construction plans. Addressing pedestrian accessibility needs could result in additional right of way needs and impacts to properties.

### Schedule:

Environmental Approval Date: Need Unknown  
Municipal Consent Approval Date: Need Unknown  
Geometric Layout Approval Date: Need Unknown  
Construction Limits Established Date: Need Unknown  
Original Letting Date: 12/21/2018  
Current Letting Date: 12/21/2018  
Construction Season: 2019  
Estimated Substantial Completion: 2019



Minnesota Department of Transportation  
District 3  
7694 Industrial Boulevard  
(218) 828-5700

**District Engineer:** Dan Anderson  
**Project Manager:** Claudia Dumont

**Revised Date:** 12/15/2015
