


PROJECT SUMMARY


Hwy 55
Annandale to Buffalo
State Project No. 8606-60

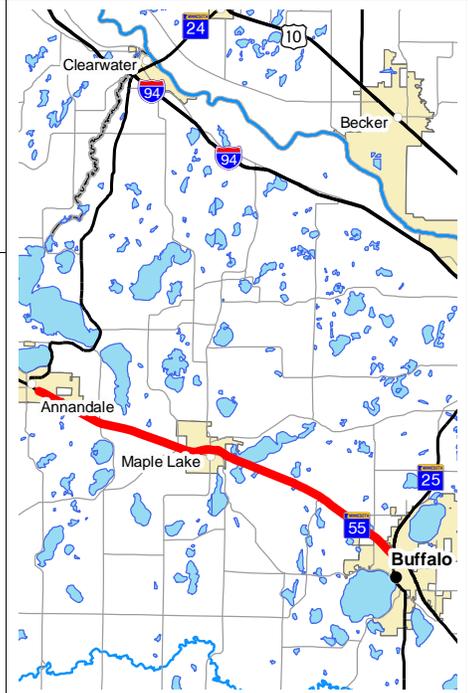

Primary Purpose:

Performance-based Need: Pavement Condition

Investment Category:

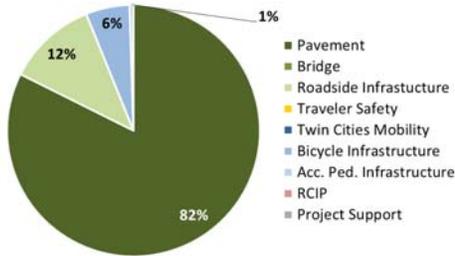

Project Description:

Resurfacing from Poplar Street in Annandale to the Hwy 55 junction in Buffalo, and includes paving the shoulders.

Recent Changes and Updates

New Project

Project History:

The project was programmed to address deteriorating pavement.

Total Project Cost Estimate (millions)

Date in which the project entered into the STIP: 2015

	<u>Baseline Est.</u>	<u>Current Est.</u>
Construction Letting:	\$ 5.6	\$ 5.6
Other Construction Elements:	\$ 0.0	\$ 0.0
Engineering:	\$ 1.1	\$ 1.1
Right of Way:	\$ 0.0	\$ 0.0
Total:	\$ 6.7	\$ 6.7

Construction cost estimates are adjusted to the mid-year of construction, using inflation rates provided by OTSM.

Key Cost Estimate Assumptions:

The baseline estimate used estimated quantities and average bid prices.

Project Risks:

This is a routine rural resurfacing project, so no significant risks are anticipated.

Schedule:

Environmental Approval Date: Not Needed
Municipal Consent Approval Date: Not Needed
Geometric Layout Approval Date: Not Needed
Construction Limits Established Date: Not Needed
Original Letting Date: 10/19/2018
Current Letting Date: 10/19/2018
Construction Season: 2019
Estimated Substantial Completion: 2019



Minnesota Department of Transportation
District 3
7694 Industrial Boulevard
(218) 828-5700

District Engineer: Dan Anderson
Project Manager: Claudia Dumont

Revised Date: 12/15/2015
