


PROJECT SUMMARY


Hwy 52
 Hwy 52 from Hwy 7 to 2 miles south of Hwy 19
 State Project No. 2506-77

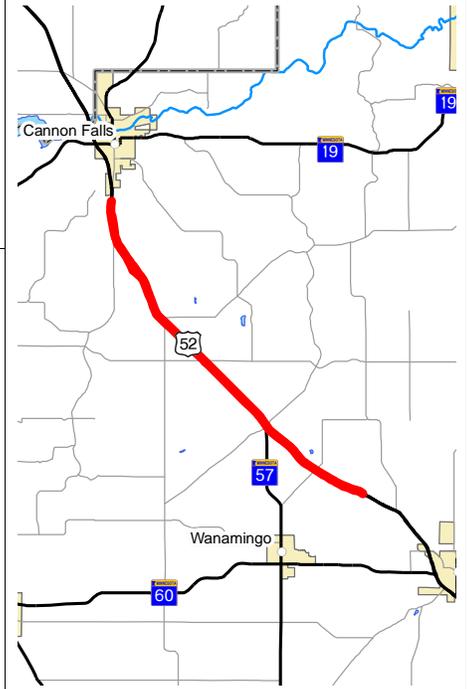

Primary Purpose:

Performance Based: Pavement Condition

Investment Category:

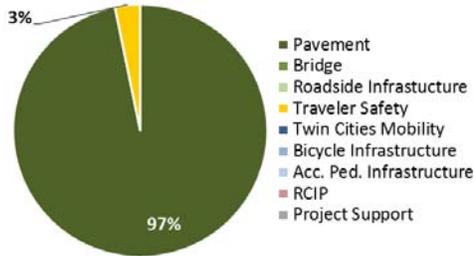

Project Description:

This is a bituminous overlay project in Goodhue county on the southbound lanes of Hwy 52.

Recent Changes and Updates

Project just entered STIP in 2014, so no updates or changes at this time.

Project History:

The purpose of this project is to preserve existing roadway structure, extend pavement life, and improve ride quality. This is a high priority interregional corridor on the National Highway System.

Total Project Cost Estimate (millions)

Date in which the project entered into the STIP: 2015

	<u>Baseline Est.</u>	<u>Current Est.</u>
Construction Letting:	\$ 5.7	\$ 5.7
Other Construction Elements:	\$ 0.4	\$ 0.4
Engineering:	\$ 0.8	\$ 0.8
Right of Way:	\$ 0.0	\$ 0.0
Total:	\$ 6.9	\$ 6.9

Construction cost estimates are adjusted to the mid-year of construction, using inflation rates provided by OTSM.

Key Cost Estimate Assumptions:

Cost estimates are based on the most recent District 6 work plan.

Project Risks:

Competitive bids may be higher or lower than expected.

Schedule:

Environmental Approval Date: TBD
 Municipal Consent Approval Date: TBD
 Geometric Layout Approval Date: TBD
 Construction Limits Established Date: TBD
 Original Letting Date: 10/27/2017
 Current Letting Date: 10/27/2017
 Construction Season: 2018
 Estimated Substantial Completion: 11/2018



Minnesota Department of Transportation
 District 6
 2900 48th Street NW
 (507) 286-7500

District Engineer: Jeff Vlamincik
Project Manager: David Tsang

Revised Date: 12/15/2015
