


PROJECT SUMMARY

Hwy 56


Hwy 56 from Maple St. in Taopi to Hwy 46 Mower County
State Project No. 5005-62

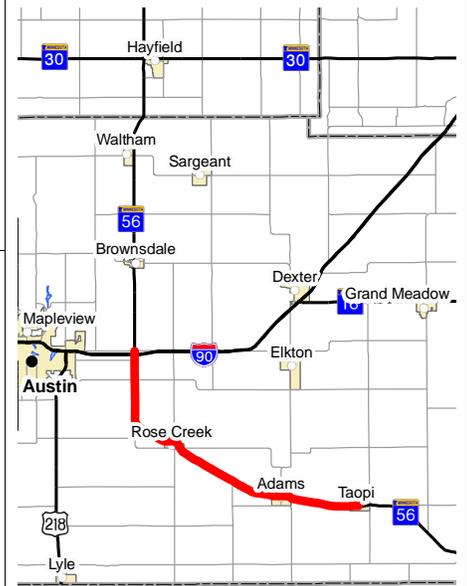

Primary Purpose:

Performance-based Need: Pavement Condition

Investment Category:



Project Description:

This is a bituminous mill and overlay project on Hwy 56 in Taopi to Hwy 46.

Recent Changes and Updates

Project prioritization factors delayed this project for several years. This project was originally proposed to be let in 2013.

Project History:

The purpose of this project is to preserve existing roadway structure, extend pavement life, and improve ride quality.

Total Project Cost Estimate (millions)

Date in which the project entered into the STIP: 2015

	<u>Baseline Est.</u>	<u>Current Est.</u>
Construction Letting:	\$ 5.7	\$ 6.2
Other Construction Elements:	\$ 0.3	\$ 0.3
Engineering:	\$ 1.0	\$ 1.0
Right of Way:	\$ 0.0	\$ 0.0
Total:	\$ 7.0	\$ 7.5

Construction cost estimates are adjusted to the mid-year of construction, using inflation rates provided by OTSM.

Key Cost Estimate Assumptions:

20 percent engineering cost estimated. Standard practices were used to develop cost estimate.

Project Risks:

Competitive bid may be higher or lower than expected. Soil conditions are unknown. Contaminated soil assessment currently being conducted in the city of Adams

Schedule:

Environmental Approval Date: Not Needed
Municipal Consent Approval Date: Unknown
Geometric Layout Approval Date: Unknown
Construction Limits Established Date: 05/07/2015
Original Letting Date: 01/25/2013
Current Letting Date: 01/27/2017
Construction Season: 2017
Estimated Substantial Completion: 11/2017



Minnesota Department of Transportation
District 6
2900 48th Street NW
(507) 286-7500

District Engineer: Jeffrey L Vlamincik
Project Manager: David Tsang

Revised Date: 12/15/2015
