


PROJECT SUMMARY


Hwy 58
Hwy 58 Bridge over Hwy 52 in Zumbrota
Bridge 9661
State Project No. 2510-50
<http://www.dot.state.mn.us/d6/projects/hwy58-bridge/index.html>

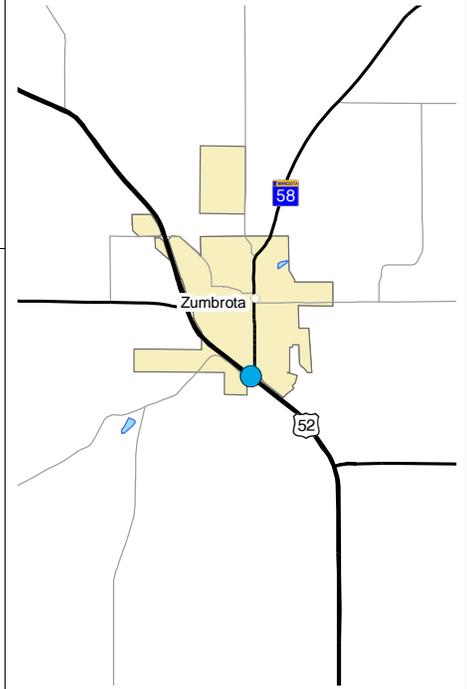

Primary Purpose:

Performance Based Need: Bridge Condition

Investment Category:

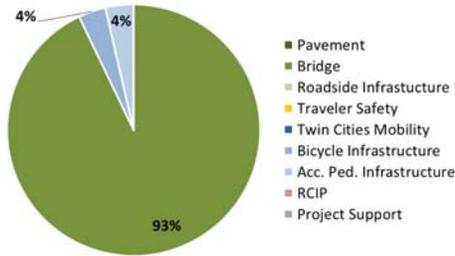

Project Description:

This project will replace the Hwy 58 bridge, #9661, over Hwy 52 in Zumbrota and several approaches.

Recent Changes and Updates

Funds added to project are reflected in the current STIP.

Project History:

The bridge #9661, a pre-stressed beam span bridge, was constructed in 1960 and is in need of replacement. The bridge has substandard railings and sight distance is limited at the interchange ramp intersections. Replacement is recommended. The project calls for replacement due to the bridges' condition and safety issues. The project would also reconstruct the approaches north and south of the bridge.

Total Project Cost Estimate (millions)

Date in which the project entered into the STIP: 2013

	<u>Baseline Est.</u>	<u>Current Est.</u>
Construction Letting:	\$ 4.8	\$ 6.5
Other Construction Elements:	\$ 0.3	\$ 0.3
Engineering:	\$ 0.8	\$ 0.8
Right of Way:	\$ 0.0	\$ 0.0
Total:	\$ 5.9	\$ 7.4

Construction cost estimates are adjusted to the mid-year of construction, using inflation rates provided by OTSM.

Key Cost Estimate Assumptions:

Funds added into the new STIP from District and other sources.

Project Risks:

Competitive bids may be higher or lower than expected.

Schedule:

Environmental Approval Date: pending
Municipal Consent Approval Date: need unknown
Geometric Layout Approval Date: pending
Construction Limits Established Date: pending
Original Letting Date: 01/27/2017
Current Letting Date: 01/27/2017
Construction Season: 2017
Estimated Substantial Completion: 2018



Minnesota Department of Transportation
District 6
2900 48th Street NW
(507) 286-7500

District Engineer: Jeff Vlamincik
Project Manager: Jai Kalsy

Revised Date: 12/15/2015
