

PROJECT SUMMARY


Hwy 61
Hwy 61 in Red Wing
Bridge 6483, &, 6482
State Project No. 2514-121



Primary Purpose:

Performance-based Need: Bridge Condition

Investment Category:

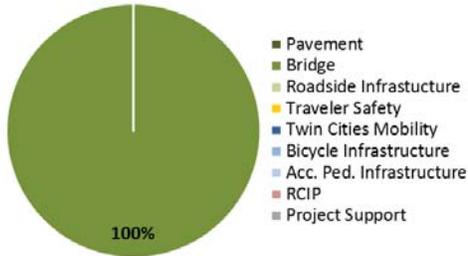

Project Description:

This project replaces bridge #6483 over the abandoned C&NW Railroad on Hwy 61 and plugs bridge #6482 in Red Wing.

Recent Changes and Updates

The District 6 work plan indicates that the current construction estimate is 7.5M, .8M less than the baseline estimate. The project was scoped and moved to FY 2025, (per 2016-2025 HIP dated 8/10/15).

Project History:

The project calls for the replacement of bridge #6483 because of its age and condition, along with reconstruction of the approaches to the bridge. It also plugs bridge #6482 in Red Wing.

Total Project Cost Estimate (millions)

Date in which the project entered into the STIP: 2014

	<u>Baseline Est.</u>	<u>Current Est.</u>
Construction Letting:	\$ 8.3	\$ 7.5
Other Construction Elements:	\$ 0.4	\$ 0.4
Engineering:	\$ 1.7	\$ 1.5
Right of Way:	\$ 0.0	\$ 0.0
Total:	\$ 10.4	\$ 9.4

Construction cost estimates are adjusted to the mid-year of construction, using inflation rates provided by OTSM.

Key Cost Estimate Assumptions:

No right of way costs will be required.

Project Risks:

Competitive bids may be higher or lower than expected.

Schedule:

Environmental Approval Date: Not Needed
Municipal Consent Approval Date: pending
Geometric Layout Approval Date: pending
Construction Limits Established Date: 10/11/2013
Original Letting Date: 01/27/2017
Current Letting Date: 01/27/2017
Construction Season: 2017
Estimated Substantial Completion: Pending



Minnesota Department of Transportation
District 6
2900 48th Street NW
(507) 286-7500

District Engineer: Jeff Vlamincik
Project Manager: Kjersti Anderson

Revised Date: 12/15/2015
