


PROJECT SUMMARY

Hwy 61

Ready Mix entrance in Red Wing to Hwy 19


State Project No. 2514-120

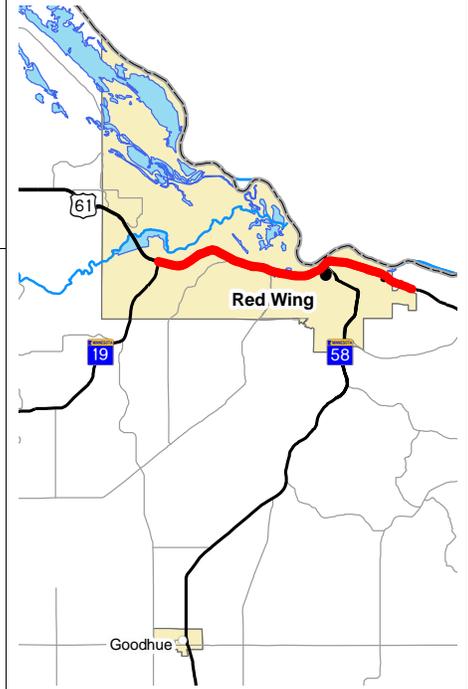

Primary Purpose:

Performance-based Need: Pavement Condition

Investment Category:



Project Description:

This project on Hwy 61 from the Ready Mix entrance in Red Wing to Hwy 19 is a bituminous mill and overlay in the rural sections and a mill and fill on the urban sections. The project will also include drainage and traffic safety improvements. Several mediums will be closed and an acceleration lane will be constructed on the north end of the project.

Recent Changes and Updates

No changes.

Project History:

The last bituminous overlay was placed in 1996 and followed up in 1998 with crack repair. As of 2011, the Ride Quality Index (RQI) was rated as fair, but has continued to deteriorate. The project was proposed in 2012.

Total Project Cost Estimate (millions)

Date in which the project entered into the STIP: 2012

	<u>Baseline Est.</u>	<u>Current Est.</u>
Construction Letting:	\$ 4.5	\$ 4.5
Other Construction Elements:	\$ 0.4	\$ 0.4
Engineering:	\$ 0.8	\$ 0.9
Right of Way:	\$ 0.0	\$ 0.0
Total:	\$ 5.7	\$ 5.7

Construction cost estimates are adjusted to the mid-year of construction, using inflation rates provided by OTSM.

Key Cost Estimate Assumptions:

No right of way will be required. No environmental mitigation will be needed.

Project Risks:

If right of way is needed the project schedule and cost would be affected.

Schedule:

Environmental Approval Date: 06/07/2015
 Municipal Consent Approval Date: NA
 Geometric Layout Approval Date: 2014
 Construction Limits Established Date: 06/07/2015
 Original Letting Date: 12/19/2014
 Current Letting Date: 12/19/2014
 Construction Season: 2015
 Estimated Substantial Completion: 11/2015



Minnesota Department of Transportation
 District 6
 2900 48th Street NW
 (507) 286-7500

District Engineer: Jeff Vlamincik
Project Manager: Chad Hanson

Revised Date: 12/15/2015
