


PROJECT SUMMARY


Hwy 63
Hwy 63 from Hwy 14 to Hwy 78
Bridge 8831, &, 8313
State Project No. 7908-35

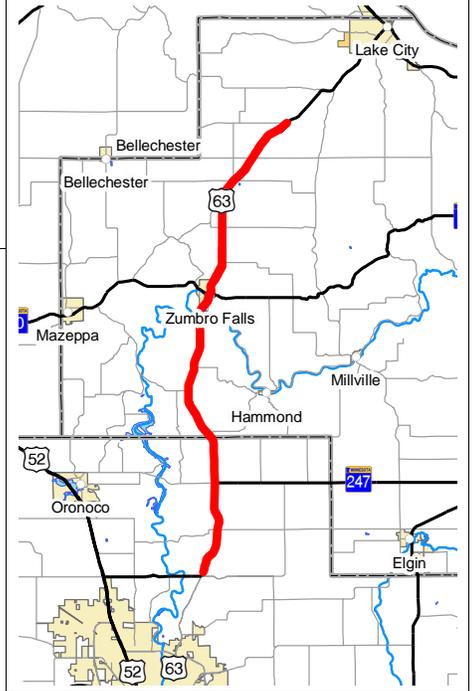

Primary Purpose:

Performance-based: Pavement Condition

Investment Category:

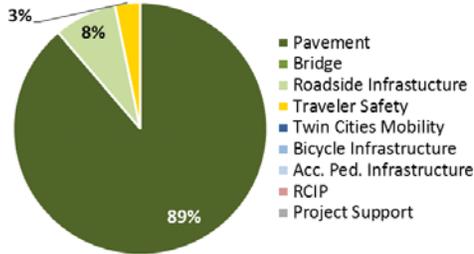

Project Description:

This project is a bituminous mill and overlay on Hwy 63 through Zumbro Falls from Hwy 14 to Hwy 78. The project includes replacing bridges #8831 and #8313.

Recent Changes and Updates

The project was scoped and entered the STIP. An environmental document is needed but has not yet been completed or turned in for approval.

Project History:

This section of Hwy 63 is a two lane rural highway. The ride quality index is low and starting to show signs of deterioration, which will be addressed to extend pavement life.

Total Project Cost Estimate (millions)

Date in which the project entered into the STIP: 2015

	<u>Baseline Est.</u>	<u>Current Est.</u>
Construction Letting:	\$ 8.6	\$ 10.3
Other Construction Elements:	\$ 0.0	\$ 0.0
Engineering:	\$ 1.7	\$ 1.7
Right of Way:	\$ 0.0	\$ 0.0
Total:	\$ 10.3	\$ 12.0

Construction cost estimates are adjusted to the mid-year of construction, using inflation rates provided by OTSM.

Key Cost Estimate Assumptions:

Standard practices were used to develop cost estimates.

Project Risks:

Competitive bids may be higher or lower than expected.

Schedule:

Environmental Approval Date: Need Unknown
Municipal Consent Approval Date: Not Needed
Geometric Layout Approval Date: not needed
Construction Limits Established Date: need unknown
Original Letting Date: 01/01/2018
Current Letting Date: 01/25/2018
Construction Season: 2018
Estimated Substantial Completion: 11/01/2018



Minnesota Department of Transportation
District 6
2900 48th Street NW
(507) 286-7500

District Engineer: Jeff Vlamincik
Project Manager: Kjersti Anderson

Revised Date: 12/15/2015
