


## PROJECT SUMMARY


Hwy 52  
Hwy 52 bridges over Little Cannon River  
Bridge 9485, &, 9486  
State Project No. 2506-79

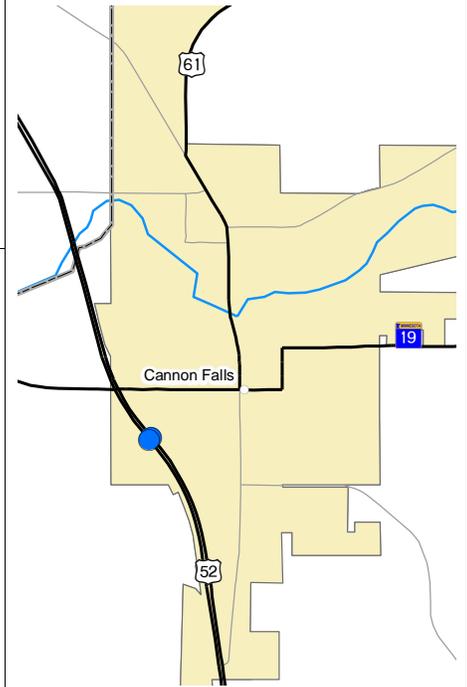

### Primary Purpose:

Performance-based Need: Bridge Condition

### Investment Category:

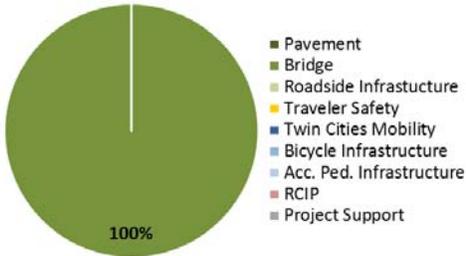

### Project Description:

The project replaces two bridges, 9485 & 9486, over the Little Cannon River on Hwy 52.

### Recent Changes and Updates

This project just entered the STIP in 2014. An environmental document is needed, but is not completed yet.

### Project History:

The bridge abutments have cracking, substandard bridge railings, and the overall deterioration is increasing.

### Total Project Cost Estimate (millions)

Date in which the project entered into the STIP: 2015

	<u>Baseline Est.</u>	<u>Current Est.</u>
Construction Letting:	\$ 5.2	\$ 4.9
Other Construction Elements:	\$ 0.2	\$ 0.2
Engineering:	\$ 1.0	\$ 1.0
Right of Way:	\$ 0.0	\$ 0.0
<b>Total:</b>	<b>\$ 6.4</b>	<b>\$ 6.1</b>

*Construction cost estimates are adjusted to the mid-year of construction, using inflation rates provided by OTSM.*

### Key Cost Estimate Assumptions:

No right of way cost.

### Project Risks:

Competitive bids may be higher or lower than expected.

### Schedule:

Environmental Approval Date: Need Unknown  
Municipal Consent Approval Date: Not Needed  
Geometric Layout Approval Date: pending  
Construction Limits Established Date: pending  
Original Letting Date: 02/01/2018  
Current Letting Date: 2/24/2017  
Construction Season: 2017  
Estimated Substantial Completion: November 2017



Minnesota Department of Transportation  
District 6  
2900 48th Street NW  
(507) 286-7500

**District Engineer:** Jeff Vlamincik  
**Project Manager:** Kjersti Anderson

**Revised Date:** 12/15/2015
