


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD


CONTROL SECTION 4511
TRUNK HIGHWAY 220
COUNTY Marshall
DISTRICT 28

LIMITS: S. Co. Line - E. Jct. T.H. in Alvarado

Ref. Pt. 044+00.557 - 046+00.069



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N° DIST
		TYPE	WIDTH	THICKNESS	
					No Record of Const. Added in 1949 50' L.T.
C	1951 4511-02	Br. 6971	28'		95' L.T. 1651
C	1952 4511-03	Grading Soil Cement Base Plant Mix Bit.	26' 22'	6" 1 1/2"	(A.F.E. 26 covers gravel surf. of X-roads & approaches) 1751
C	1954 A.F.E. 821	Guard Rail			912' of Br. 6971
M	1955 A.F.E. 820	Shoulder Repair			
C	1960	Plant Mix Bit.	22'		AC-1, 89 Tons by Maint. Dist. RS-2K, 2615 Gal. Agg. 113 C.Y. 1460
M	1964 C	Light Bit. Seal	23'		
C	1971 4511-06	Grading & Base Plant Mix Bit.	44' 40'	22" 3"	
C	1973 4511-26	Bit. Overlay Gravel Shoulders	28' 2'	3 1/2"	
C	1974 6000-02	PLATE BEAM GUARD RAIL FOR BR 6971			338 LIN. FT. 1774
C	1979 4511-10	Grading, Surfacing & Br. 45002	44' 40'	22" 3"	
M	1985 M4153	Bit. Overlay	22'	1 1/2"	Spec. 2331
C	1992 4511-12	Bit. Overlay	28'	1 1/2"	Spec. 2341
M	1995 M95278	Crack Repair			

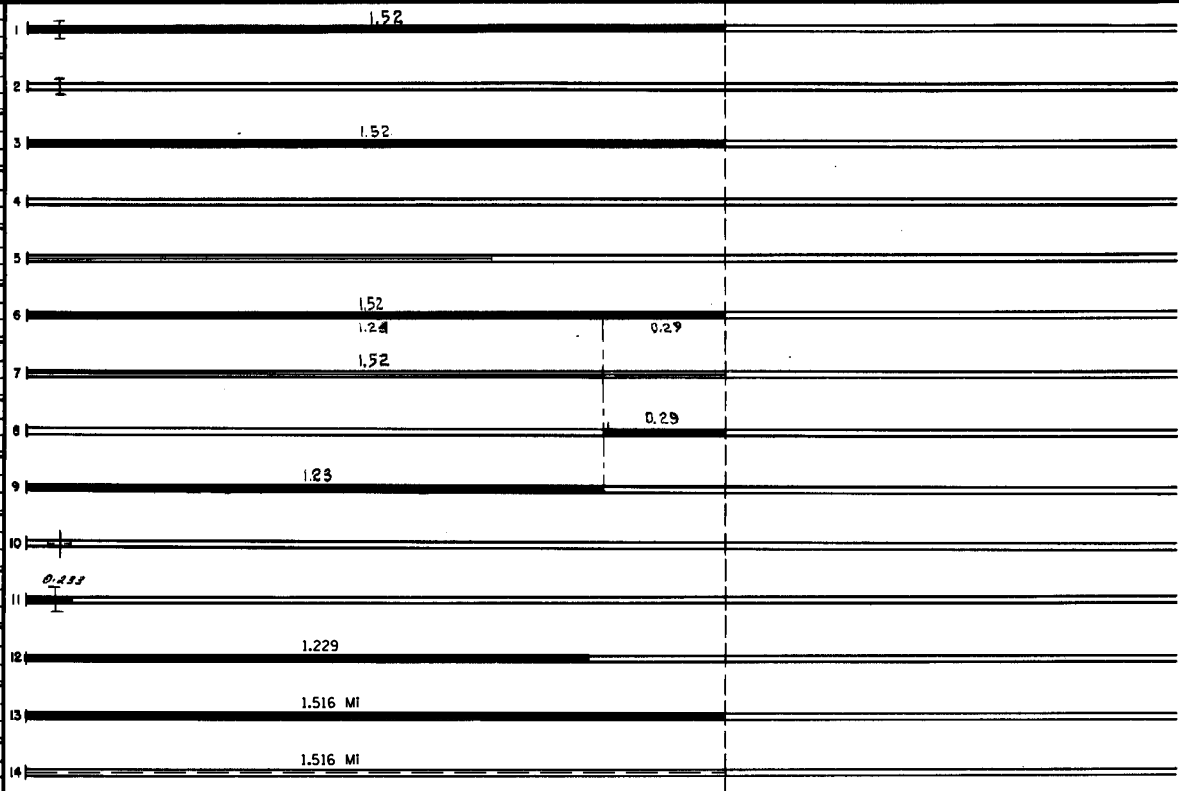

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1949	1950	1.52	0.93	0.01	0.52	0.00	1.51	0.01	0.00	0.00
1951	1960	1.52	0.98	0.02	0.52	0.00	1.50	0.02	0.00	0.00
1961		1.52	1.23	0.02	0.27	0.00	1.50	0.02	0.00	0.00

REMARKS: Layout is to scale as of 1949

FOR OTHER PROJECTS SEE DIST NO. 1360, 4069

