


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 5411
TRUNK HIGHWAY 200
COUNTY Norman
DISTRICT 28

LIMITS: E. End of Bridge (Red River) - Jct. T.H. 75 in Halstad
Ref. Pt. 000+00.142 - 000+00.910



YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o DIST.
		TYPE	WIDTH	THICKNESS	
		Gravel	24'	1"	No Record of Const. Added in 1934.
C	1941 A.F.E. 36	Bit. Surf. Treat. (Blot)			SC 3,2812 Gal./Mi. Grav. 133 C.Y./Mi. Maint. Dept.
C	1945 A.F.E. 21	Bit. Resurfacing Bit. Surf. Treat.	24'	3/4"	SC 3,8980 Gal./Mi. Grav. 433 C.Y./Mi. Maint. Div.
C	1950 5411-02	Grading Gravel	32' 28'	1 1/2"	1000 C.Y./Mi. 950
		Gravel	32'		No Record of Const. Taken over from village in 1950
C	1951 A.F.E. 7	Seeding			
C	1952 5411-03	Concrete	2263	8979	952
C	1956 A.F.E. 817	Guard Rail			192 L.F.
C	1971 5411-05	PLATE BEAM GUARD RAIL FOR BR 5221			509 LIN. FT. (OVER RED R.) 471
C	1973 5411-06	RR CROSSING SIGNALS			(ON BRIDGE) 1173
M	1975 SF	GRAVEL SHLDR. REPAIR			500 C.Y. 2075
M	1979 SF	GRAVEL SHLDR. REPAIR			500 C.Y. 2779
S	2001 5411-14	SubCut, Grading Agg. Class 1&5 Concrete Doweled	42' 42' 27'	Var	Class 1& 5 Spec 2301
	2006 8822-61	Concrete Rehab.			

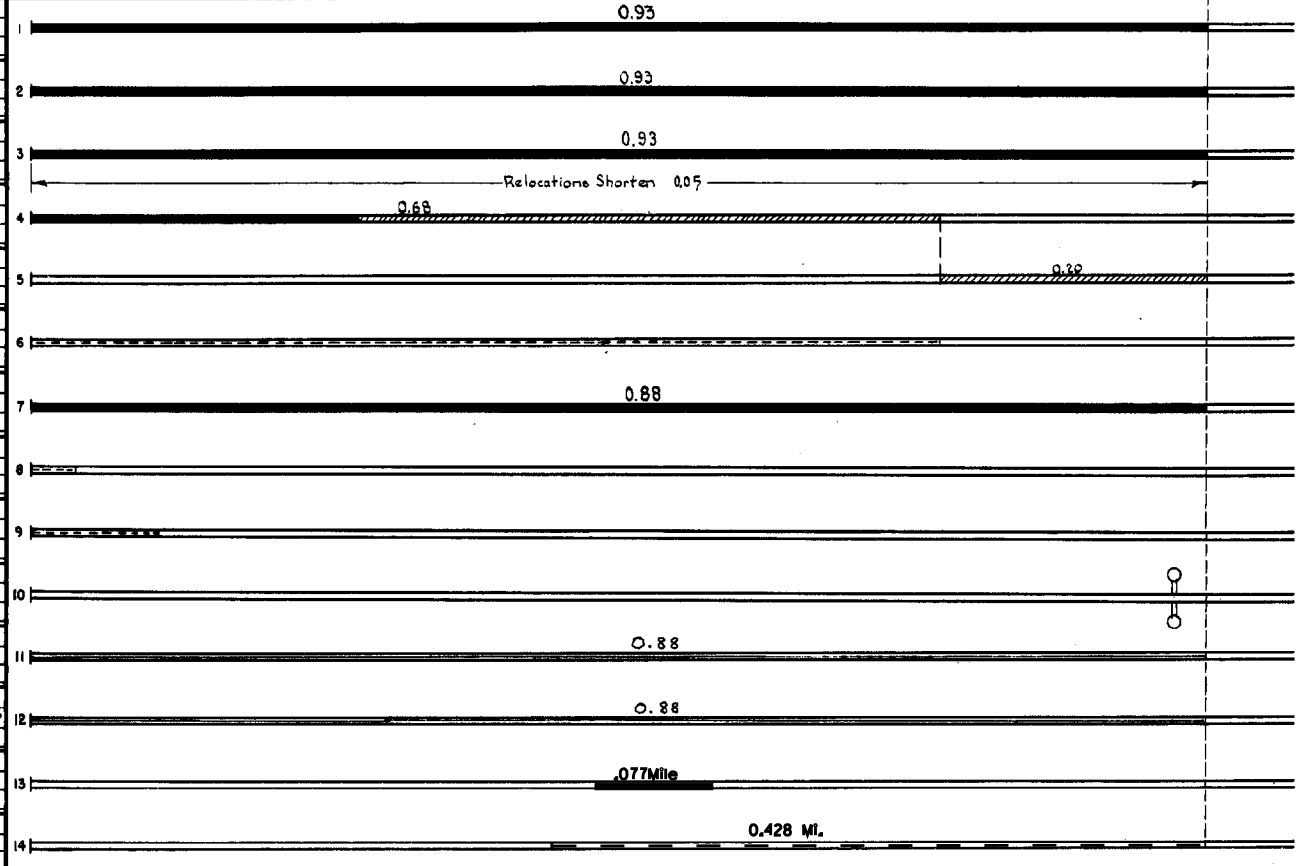

YEARS FROM	TOTAL MILES TO	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1949	0.93	0.67	0.00	0.26	0.00	0.93	0.00	0.00
1950	1956	0.88	0.65	0.00	0.23	0.00	0.88	0.00	0.00
1956		0.88	0.61	0.00	0.27	0.00	0.88	0.00	0.00

REMARKS: Layout is to scale as of 1934.
FOR OTHER PROJECTS SEE DIST. No. 4069
