


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 5611
TRUNK HIGHWAY 24
COUNTY Otter Tail
DISTRICT 4A

LIMITS: W. Co. Line - Jct T.H. 59
Ref. Pt. 011+00.758 - 018+00.862



YEAR BUILT	PROJECT N°	DESCRIPTION				CODE N°
		TYPE	WIDTH	THICK-NESS	REMARKS	
		Gravel	24'	1"	No Record of Constr.	
		Grading	24'		Added in 1934.	
1924		Gravel	24'	2 1/2"	Co. Job 2401 1200 C.Y./Mile Added in 1934.	
M	A.F.E. 32	Regraveling			Grav. & Clay 332 C.Y./Mi. Maint. Dept.	
M	A.F.E. 6	Regraveling & Consolidation			Grav. & Binder Soil 255 C.Y./Mi. Maint. Dept.	
M	A.F.E. 6	Grav. Resurfacing (Spots)			1835 Tons	
C	5611-04	Grading	32'			
1951	5611-04	Gravel	28'	1 1/2"	1200 C.Y./Mi. Ext. 2' H&B Culvs.	
C	5611-05	Gravel Base	28'	3-9"		
1952	5611-05	Mixed Bit	26'	1"		
M	A.F.E. 605	Light Bit. Seal	26'		AE RS-2, 16490 Gal. Agg. 540 C.Y.	
C	5611-06	Plant Mix Bit.	24'	1 1/2" added		
M	A.F.E. 605	Light Bit. Seal	25'		RC-2, 12287 Gal. Agg. 441 C.Y.	
M	1953	Spot Treat Bit. Surf. Repair	24'	1"	Bit. 2290 Gal. Agg. 219 Tons To Ex. 300 Gal.	
C	5611-09	Mix Bit. Surf.	24'	3"		
1977	5611-09	GRAY SHOULDERS	6'			
M	1990	Spot Overlay		1 1/2"	Spec. 2341	
C	1997	Milling Bit. Overlay	28'	2"	Spec. 2341	
			28'	Var.		

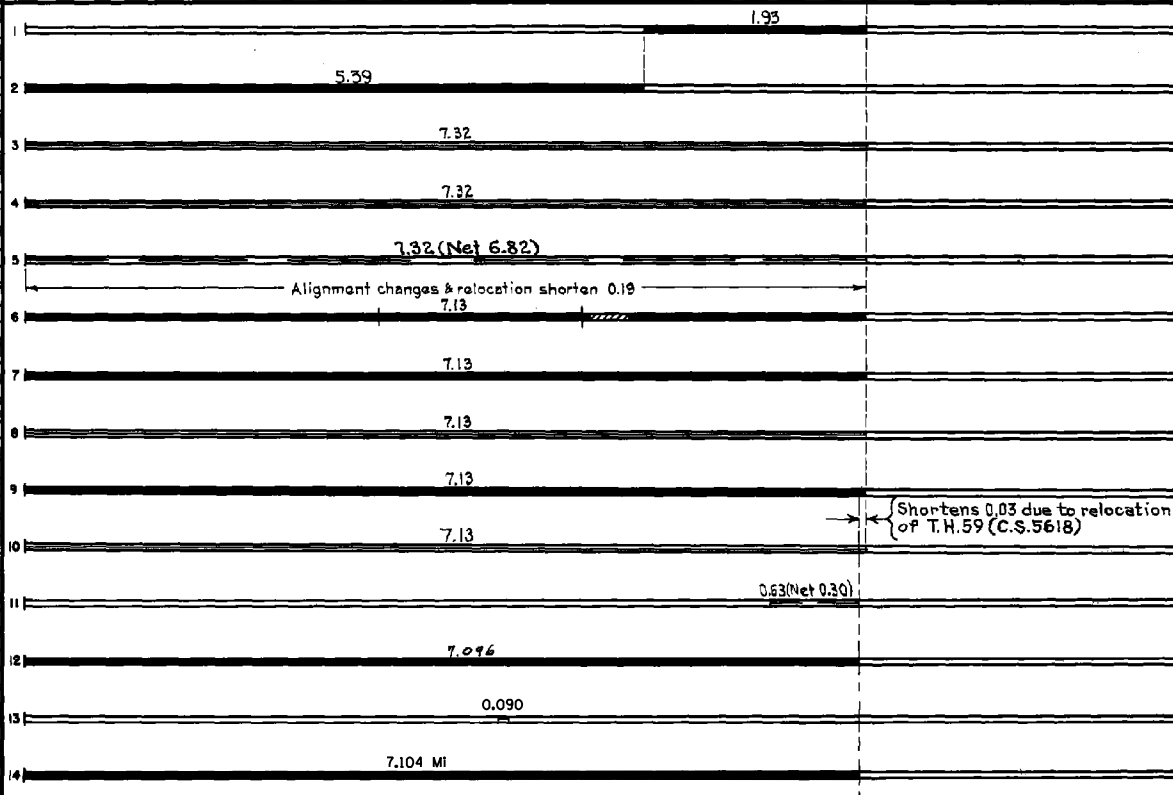

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED			INCORPORATED			RURAL		URBAN	
			RDWY. MI.	BR. MI.	BR. MI.	RDWY. MI.	BR. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1950	7.32	7.32	0.00	0.00	0.00	7.32	0.00	0.00	0.00		
1951	1966	7.13	0.00	0.00	0.00	0.00	7.13	0.00	0.00	0.00		
1967		7.10	7.10	0.00	0.00	0.00	7.10	0.00	0.00	0.00		

REMARKS: Layout is to scale as of 1934.

