


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 7096
TRUNK HIGHWAY 65
COUNTY Scott
DISTRICT 9A

LIMITS Jct. TH.35 - N. Co. Line



YEAR BUILT	PROJECT N°	DESCRIPTION				CODE N°
		TYPE	WIDTH	THICK-NESS	REMARKS	
1924		Gravel	24'	3 1/2"	Rice Co. Job 2407. 1600 C.Y./Mi. Added in 1934.	
M 1940	A.F.E. 11	Regraveling	26'		470 C.Y./Mi. Maint. Dept.	
C 1941	7006-09	Grading & Stab. Gravel	38'	1"	1200 C.Y./Mi.	
C 1948	7006-02	Grading Stab. Gravel C86x69	38' 30'	2"	1200 C.Y./Mi. Not in use until 1949	
C 1949	7006-04	Grading Br. 6409	43'		C66x30' S.S.-U.R.	
C 1949	7006-10	Bit. Stab. Base Plant Mix Bit.	32' 24'	4"-10" 1 1/2"		
M 1951	A.F.E. 23	Spot Base Repair Spot Treat. Bit. Surf. Repair	34' 24'	1"-10"	RT-6&M63, 12293 Gal. Agg. 250 C.Y.	
CEM 1952	7006-11 A.F.E. 36	Plant Mix Bit. Drainage Corr.	24'	2"-4" added	Mi. Pt. 1.00	
M 1956	A.F.E. 604 A.F.E. 605	Bit Surf. Repair* Light Bit. Seal(6.09Mi.)	24' 24'		MC-32 RC-2, 19852 Gal. Agg. 879 Tons & 368 C.Y. *Mi. Pt. 4.40-4.90	
M 1940		Bit. Surf. Repair	24'		MC-32 RC-2, 4745 Gal. Agg. 424 Tons	
M 1964	C S.F.	Light Bit. Seal Spot Treat. Bit. Surf. Repair	24'		RS-2K, 9722 Gal. Seal Agg. 280 C.Y. Pl. Mix Bit. 816 Tons	
C 1965	Maint.	Gravel Base Plant Mix Bit. Base Plant Mix Bit. Surf.	36' 26' 24'	6" 1 1/2" 3"	12" Sand-Gr Sub-base	

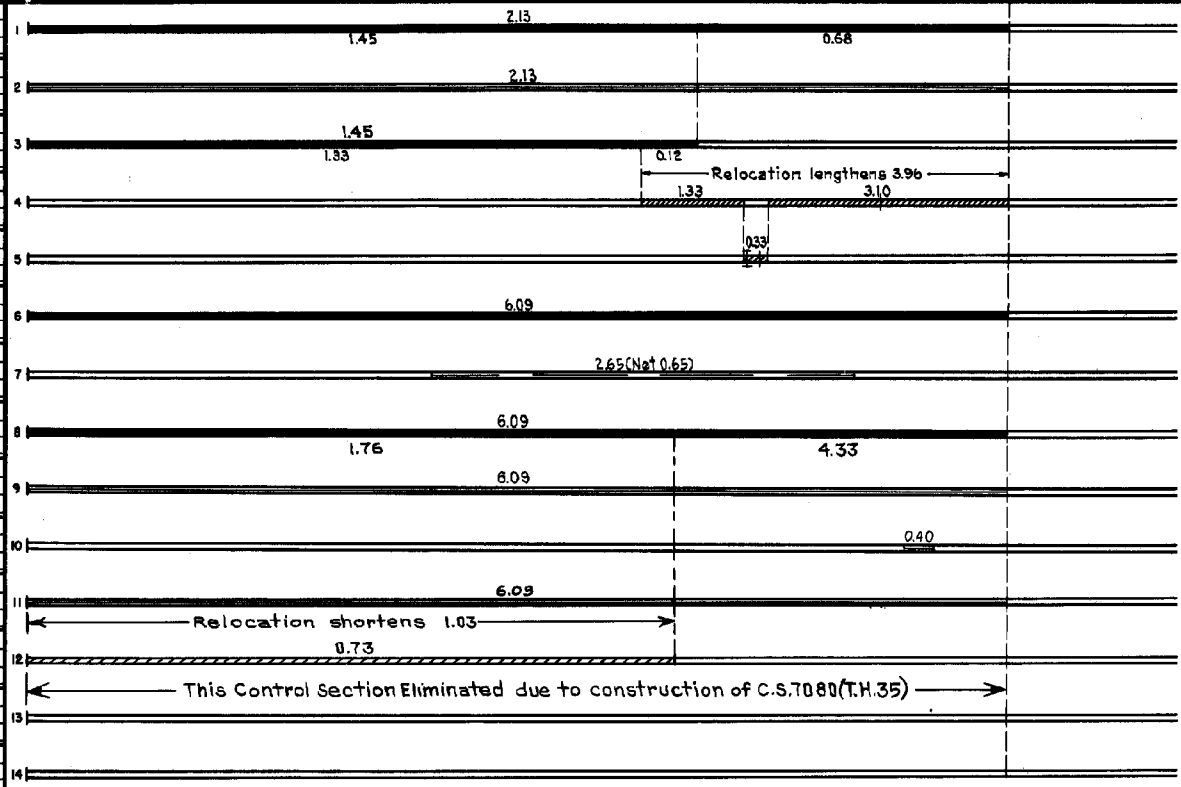

FROM	TO	TOTAL MILES	UNINCORPORATED			INCORPORATED			RURAL		URBAN	
			RDWY. MI.	BR. MI.		RDWY. MI.	BR. MI.		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1948	2.13	2.13	0.00	0.00	0.00	0.00	2.13	0.00	0.00	0.00	
1949	1964	6.09	6.09	0.00	0.00	0.00	0.00	6.09	0.00	0.00	0.00	
1965	1965	5.06	5.06	0.00	0.00	0.00	0.00	5.06	0.00	0.00	0.00	
1966		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	

REMARKS: Layout is to scale as of 1934 Plan revised for 1948 & 1949 relocation
(1) Contract not final but work substantially complete in 1949.
