


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 8302
TRUNK HIGHWAY 4
COUNTY Matonwan
DISTRICT 7B

LIMITS: E. Jct. T.H. 60 in St. James - No. Co. Line



YEAR BUILT	PROJECT N ^o	DESCRIPTION		REMARKS	CODE N ^o
		TYPE	WIDTH THICKNESS		
M 1952	A.F.E. 5	Bit. Fog Seal Coat	24'	RS-1, 6907 Gal. Agg. 101 C.Y.	1
M 1952	A.F.E. 6	Grav. Resurfacing	24'	4312 Tons	2
C 1953	8302-10	Sand-Grav. Subbase	32' 4"		3
C 1953	8302-11	Bit. Stab. Base	32' 4"		3
C 1954	A.F.E. 817	Plant Mix Bit.	24' 2"	Br. 8832 (C106T)	3
C 1954	A.F.E. 817	Rip Rap		At Br. 5076	4
M 1956	A.F.E. 605	Bit. Seal Coat	24'	RS-2, 9635 Gal. Agg. 300 C.Y.	5
C 1958	A.F.E. 818	Bit. Resurfacing	25' 1" added	MC3, 42063 Gal. Agg. 2810 Tons	6
M 1959	A.F.E. 605	Mixed Bit.	26'	RS-2, 7682 Gal. Agg. 280 C.Y.	7
M 1962		Spot Treat		Rd. Mix. 14195 Tons	8
M 1962		Bit. Surf. Repair	24'	MC3, RS-2, 35620 Gal. Agg. 488 C.Y.	8
M 1962		Light Bit. Seal	25'		8
C 1965	8302-13	Shoulder Grading		Rt. & Lt. of rdwy imp. Grading & Base not on entire project	9
C 1965		Bit. Base			9
C 1965		Plant Mix Bit Surf.	24' 3"		9
M 1966	SF	Bit. Surf. Repair	24' 1"	MC 250, 57175 Gal. Agg. 4351 Tons	10
M 1967	SF	Bit. Surf. Repair	24' 1"	MC 800-21, 373 Gal. CRS-1 10,080 Gal.	11
M 1967	C	Light Bit. Seal	24'		11
C 1978	8302-19	GRADING, Bit. SURFACING	2' 3"	TEMP. TH 4 E Jct TH 60 - IN PLACE TH 60 IN ST. JAMES	12
C 1978	RS 6101 (18)	Agg. Subbase, Curbs	16'	TRANSFERRED FROM CS. 8309 DUE TO RELOCATION OF TH 60	13
C 1978	8302-21	Bit. SURFACING	24' 2"	0.40 MI. TRANSFERRED FROM CS. 8309 IN PL. TH 60 - C.S.A.H. 14	14

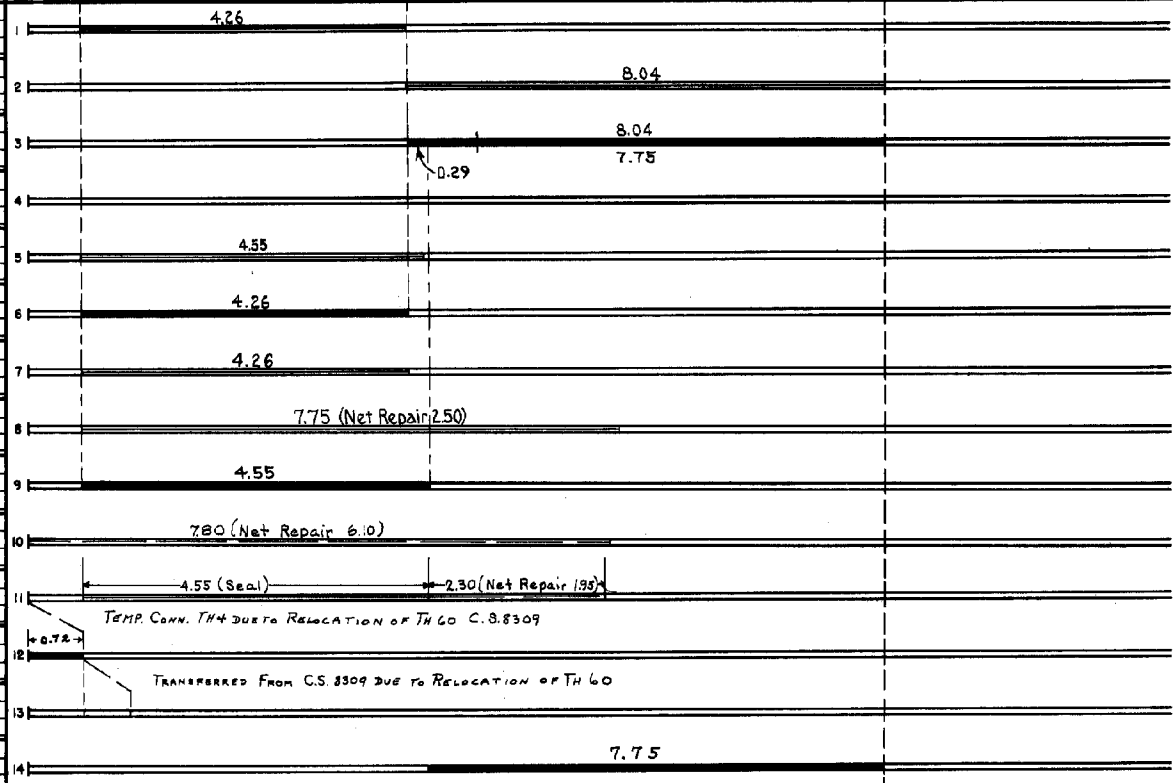

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.

REMARKS: See Sheet No. 1

