

PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 3310  
TRUNK HIGHWAY 70  
COUNTY Kanabec  
DISTRICT 1A

LIMITS: S. Jct. T.H. 107 - E. Co. Line

Ref. Pt. 010+00.446 - 011+00.224

YEAR BUILT	PROJECT N <sup>o</sup>	DESCRIPTION			CODE N <sup>o</sup>
		TYPE	WIDTH	THICKNESS	
1923		Gravel	25'	2 1/2"	
					Co. Job 2302. 1200 C.Y./Mile. Added in 1934.
M					
1940	A.F.E. 43	Regraveling			198 C.Y./Mile. Maint. Dept.
C					
1942	3310-01	Grading Sand-Grav. Base	30'	6"	
C					
1942	A.F.E. 7	Seeding			Seed supplied by R.S.D. (S.P. 3310-03) Maint. Dept.
1943					
C					
1948	3310-04	Bit. Stab. Grav. Base Mixed Bit	26'	2"-8"	
M					
1951	A.F.E. 4	Bit Fog Seal	24'		RCS-1, 1958 Gal. Agg. 56 C.Y.
M					
1956	A.F.E. 819	Spot Base Repair Bit. Surf. Repair	32'		MC-2, 3797 Gal. Agg. 353 Tons
M					
1959	A.F.E. 605	Bit. Seal Coat	25'		RC-2, 1431 Gal. Agg. 58 C.Y.
M					
1965	SF	Bit. Surf. Repair	24'		MC-250 Tack 237 Gal. Rd. Mix 309 Tons
C					
1977	3310-07 SF	Bit. SURFACING GRAVEL SURF. 2.3 YAR.	24'	3"	Bit. Spec. # 2331
C					
1999	3310-10	Bit. Overlay Gravel Surface	24'	1 1/2"	Spec. 2350
S					
2011	3310-11	Reclamation Milling Bit. Surfacing	24'	6" 4" var.	Spec. 2360

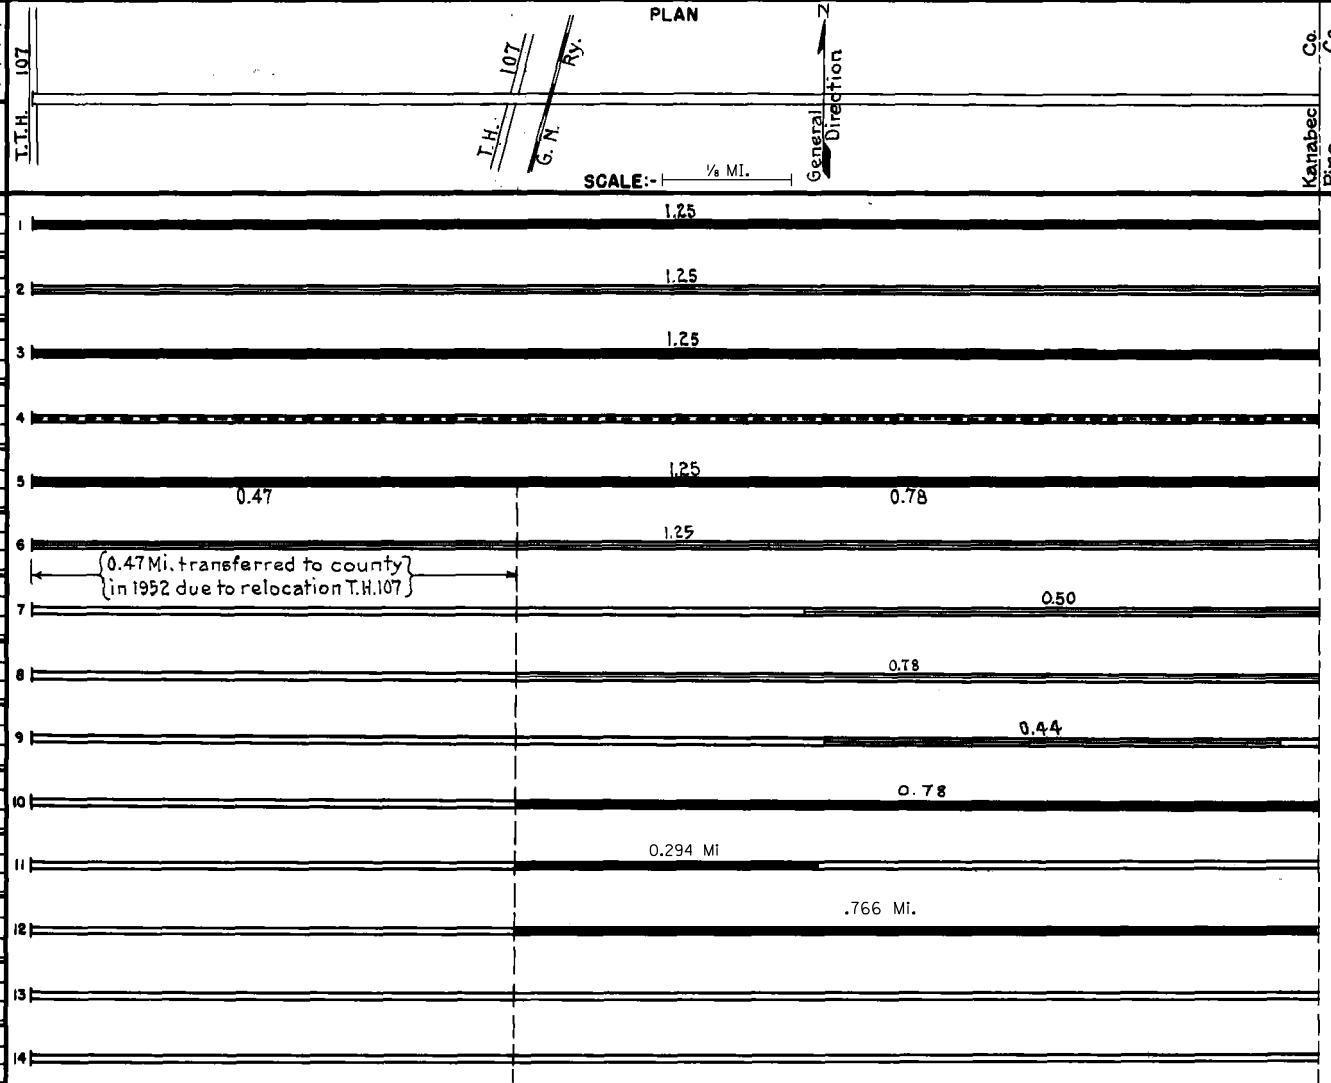

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1924	1951	1.25	0.00	0.00	0.00	1.25	0.00	0.00	0.00	
1952		0.78	0.78	0.00	0.00	0.78	0.00	0.00	0.00	

REMARKS: Layout is to scale as of 1934

Kanabec Co. Pine
