FORM R.L.-7 REV. 3-58

PREPARED BY
TRAFFIC AND PLANNING DIVISION
IN COOPERATION WITH
U.S. DEPARTMENT OF COMMERCE
BUREAU OF PUBLIC ROADS

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

SHEET 1 OF 1

CONTROL SECTION 1812
TRUNK HIGHWAY 309
COUNTY Crow Wing
DISTRICT 3A

LIMITS: E. Jct. T.H. 18 - W. Jct. T.H. 18
Brainerd State School and Hospital

Ref. Pt. 000+00.000 - 000+00.274

YEAR BUILT	PROJECT Nº	DESCRIPTION TYPE	WIDTH	THICKNESS	REMARKS
		Sub-base		12"	0.12 Mi. 72' Wide
1959	1812-01	Base		4"	0.07 Mi. 36' Wide
		Plant Mix Bit.		3"	0.16 Mi. 24' Wide
M					CRS-2 Bit. 3,185 Gal.
1967	C	Bit. Seal Coat	Var.		FA-3 Agg. 125 C.Y.
U	U10171	Mill & Bit. Overlay	36-	1.5"	Spec. 2350
2001	1812-13	(Larson Engr'ing, MN)	72'		

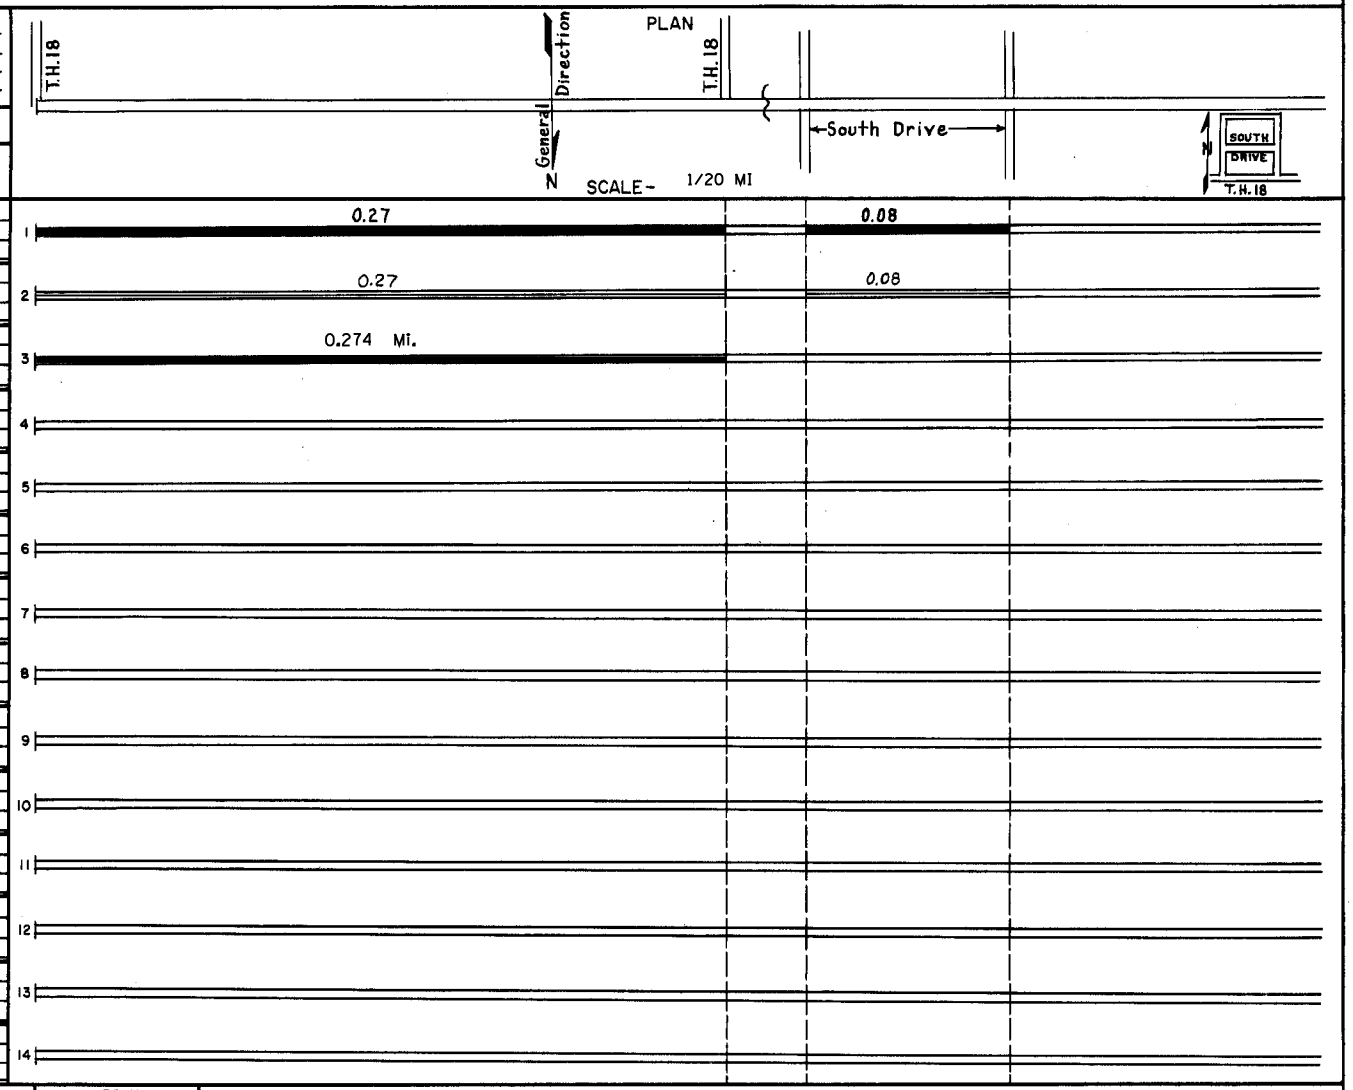

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.
1959		0.35	0.35	0.00	0.00	0.00	0.35	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1959.
