Mn/DOT 29450 (4-78)
FORM RL-7

PREPARED BY
BUREAU OF POLICY & PLANNING
IN COOPERATION WITH
U.S. DEPARTMENT OF TRANSPORTATION-FEDERAL HIGHWAY ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF TRANSPORTATION
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 1929
TRUNK HIGHWAY 77
COUNTY Dakota
DISTRICT Metro

LIMITS: Johnny Cake Ridge Rd. - Jct. ISTH - 35E

Ref. Pt. 000+00.000 - 002+00.846

YEAR BUILT	PROJECT NO	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS
C 1983	1929-03	Grading	140'		
C 1983	1929-63 I-35E-4(145)	Grading	140'		
C 1983	1929-05	Concrete Paving	2-24'-36'	8"	
		Bit. Shoulders	10'		
C 1983	1982-87 I-35E-4(160)	Concrete Paving	2-24'-36'	8"	
		Bit. Shoulders			
C 1983	1929-19082 M5049(8)	Br. 19082			215' Pre Conc. Bm. Sp.
C 1982	1982-48	Grading, Agg. Base	2-32'	5"	
		Concrete Surface	2-24'	9 1/2"	
		Bit. Shoulders	10', 3'		
C 1986	1929-04	Grading, Agg. Base	2-30'	5"	
		Concrete Surface	2-24'	8"	Br. 19081
		Bit. Shoulders	8'	7"	
S 2007	S07045 1925-44	Concrete Pavement Repair & TMS	72'	var.	Conc. Dowel bars
S 2012	1929-44	Conc. Rehabilitation	var.		36' SB
	1925-53	Bit. Mill & Overlay	var.	var.	Spec 2360 24' NB

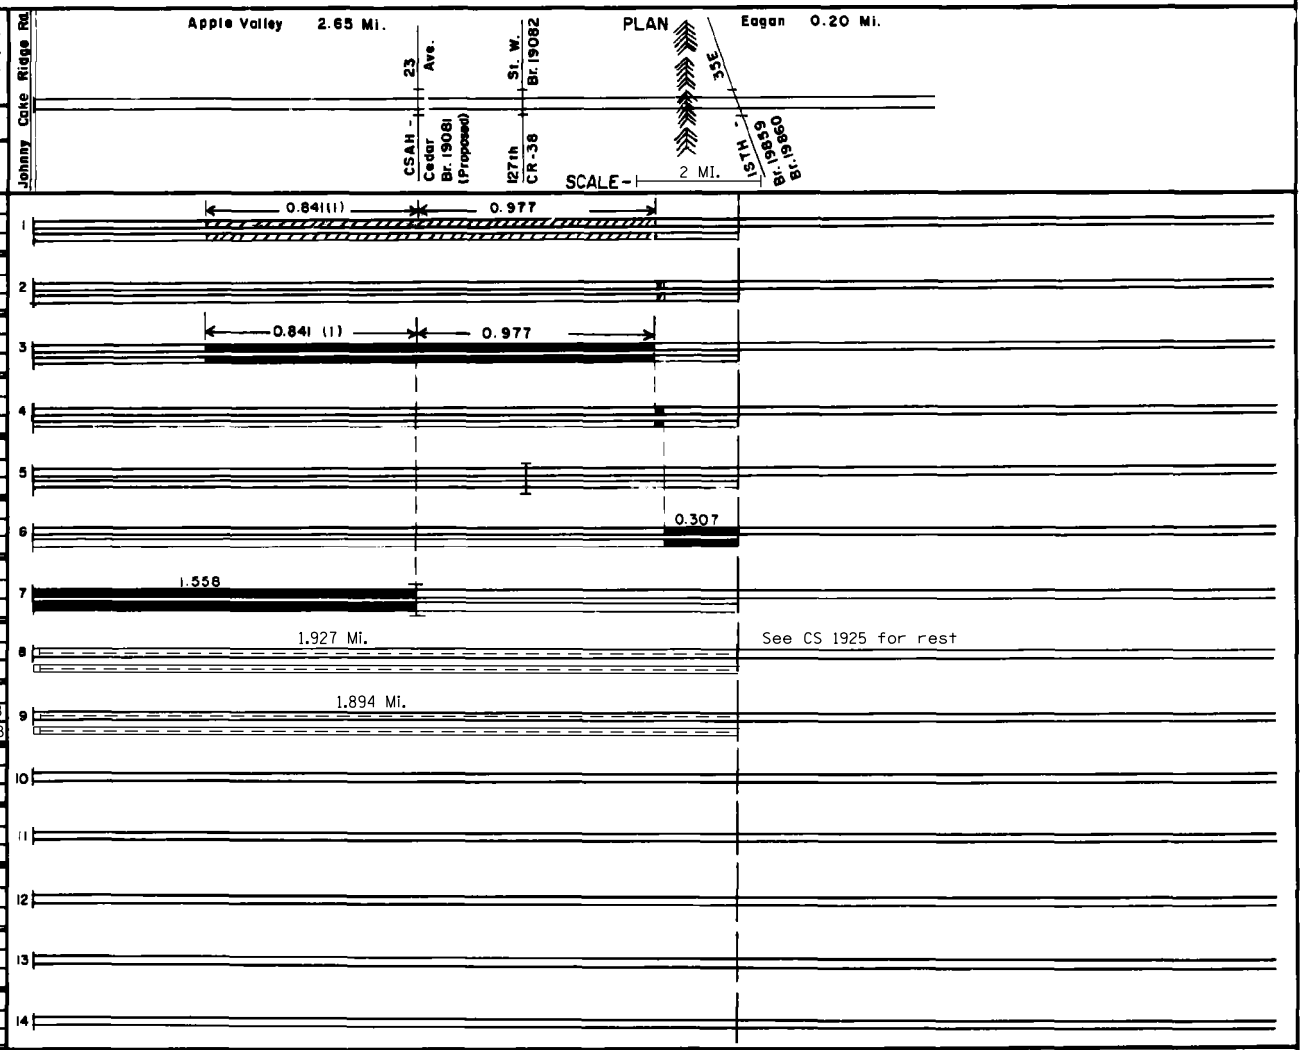

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.

REMARKS: (1) This portion of project is on Cedar Ave., not TH. 77 (0.841 Mi.)
