FORM R.L.-7 REV. 2-40

SHEET 1 OF 1

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 6101
TRUNK HIGHWAY 9
COUNTY Pope
DISTRICT 4B

LIMITS: S. Co. Line - W. Co. Line

Ref. Pt. 044+00.643 - 047+00.983

YEAR BUILT	PROJECT Nº	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS	CODE Nº
1921	9-10-22B	Grading	30'			
1922	9-10-22B	Gravel	24'	4¼"	2000 C.Y./Mile.	
1931	9-10-22B	Concrete	20'	9-7-9		
M 1971	SF	Gravel Shoulders Joint Seal			3,361 C.Y.	
C 1984	6101-01	Bit. Widening Bit. Surfacing Agg. Shoulders	3' 28' 4'	9" 4½" Var.	Lt. & Rt.	
M 1991	4460	Crack Repair				
C 2010	6101-03	Bit. Overlay	28'	var.	Spec. 2360	
M 2018	8824-153	Bit. Seal Coat	28'		Spec. 2356	

PLAN

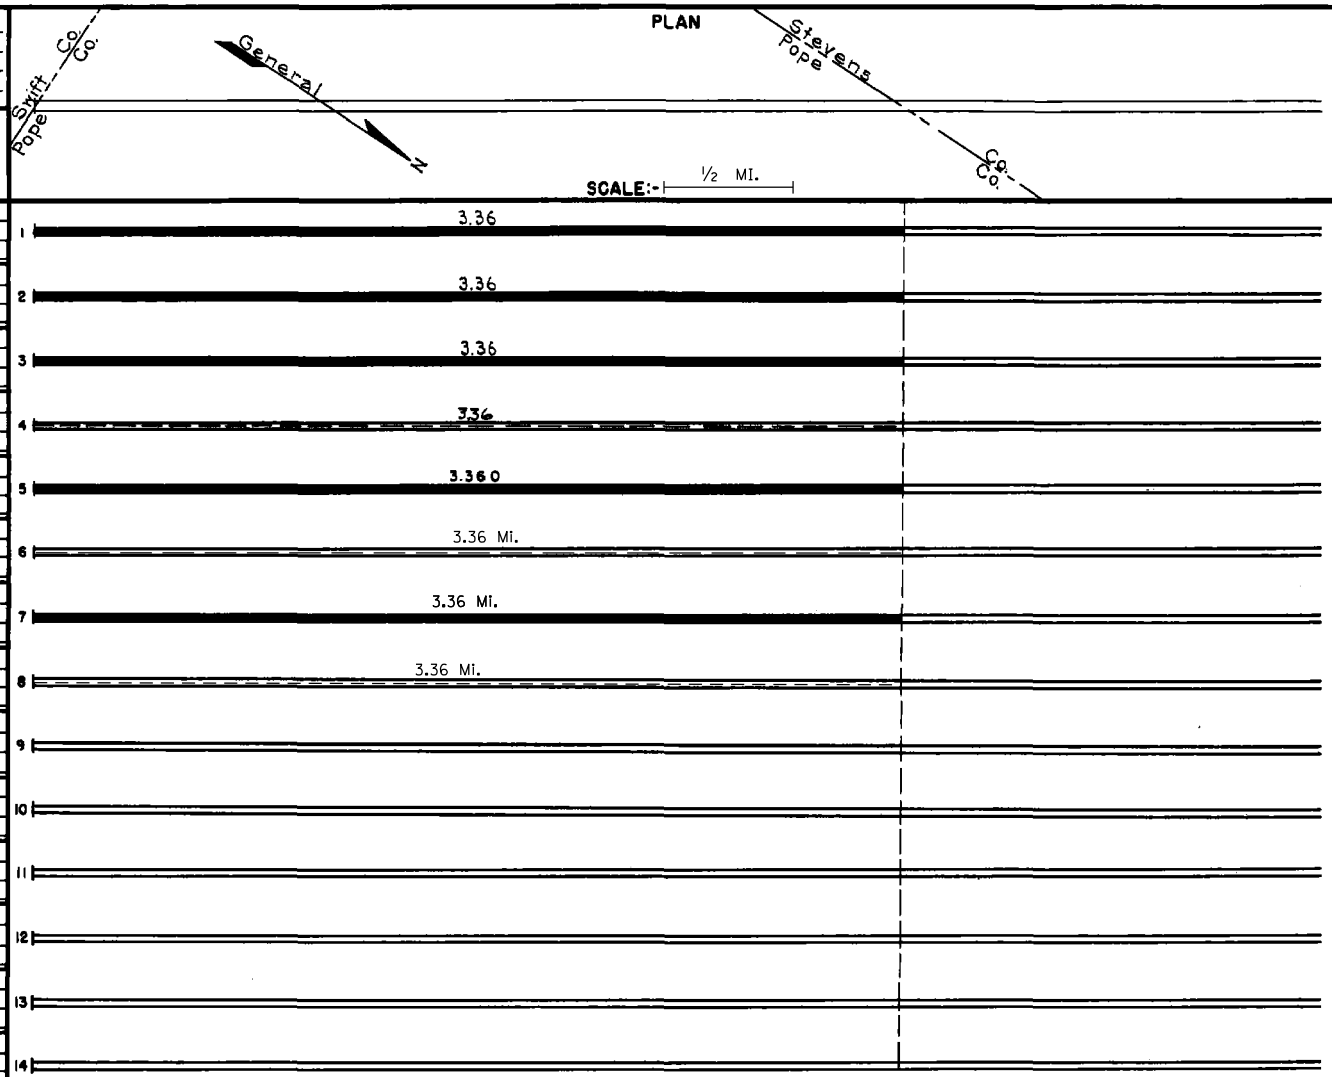

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.
1921		3.36	3.36	0.00	0.00	0.00	3.36	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1921
