FORM R.L.-7 REV. 2-40

SHEET 1 OF 1

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 6210
TRUNK HIGHWAY 12
COUNTY Ramsey
DISTRICT 9A

LIMITS: E. Corp. Limits of St. Paul (W. Limits of Maplewood) – E. Limits of Maplewood (Jct. T.H. 120) (E. Co. Line)

YEAR BUILT	PROJECT Nº	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS	CODE Nº
1922		Gravel	24'	2"		
					Maint. Dept.	
		Grading	40'			
1927	12=12-25A	Gravel	24'	1½"	618 C.Y./Mile.	
1928	12=12-25A	Concrete	20'	9-7-9		
C		Grading	36'		New Roadway –	
1940	6210-01	Concrete	22'	9-7-9	Divided Highway.	
C					New Roadway –	
1940	6210-02 A.F.E. 5	Seeding			Divided Highway. Maint. Dept.	
C						
1953	6210-08	Traffic Signals				
C		Grading	38'			
1954 (1)	6210-10	Concrete	24'	9"		
C						
1955	6210-13	Conc. Resurfacing	24'	5 min.		

PLAN

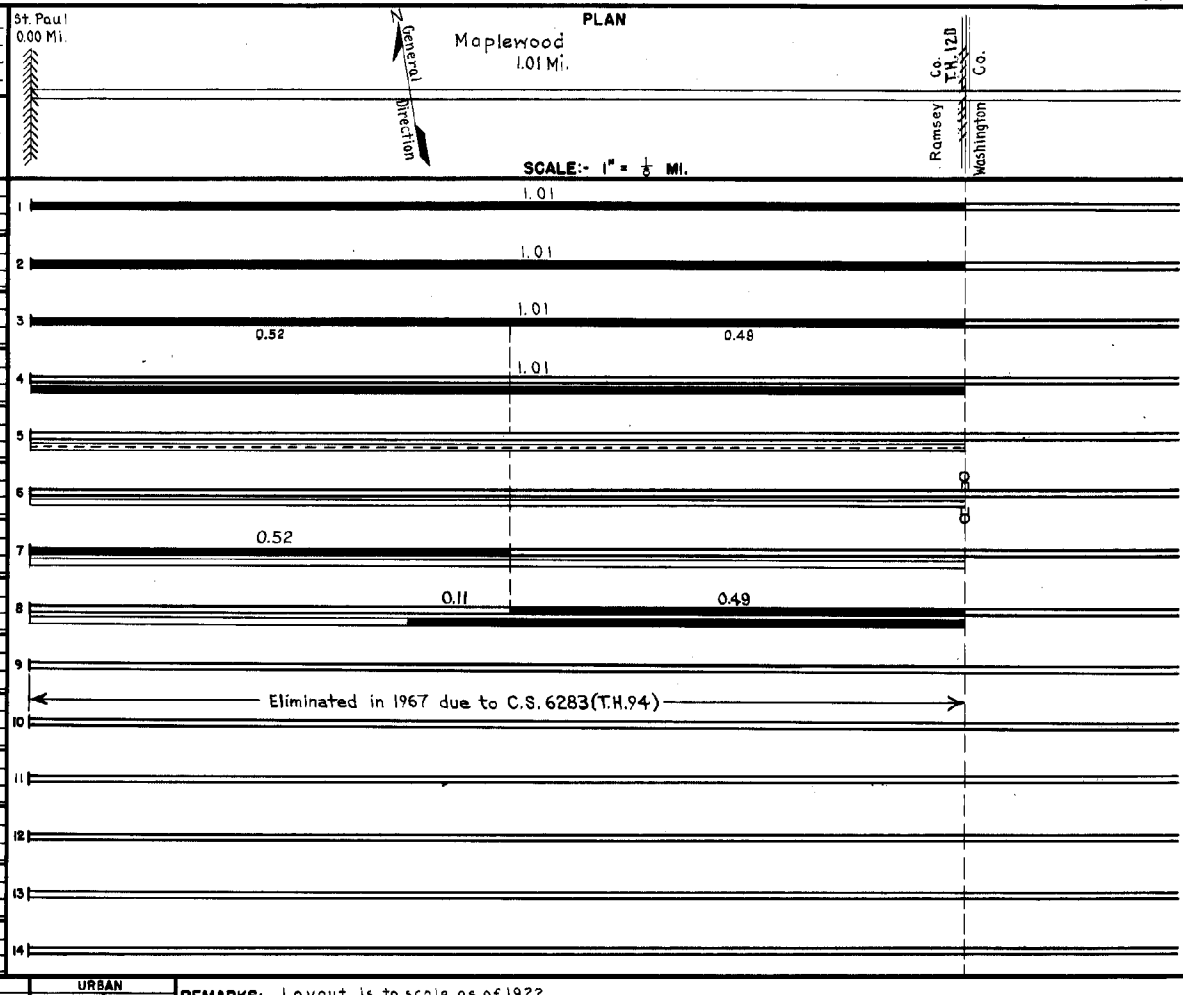

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.
1922	1956	1.01	1.01	0.00	0.00	0.00	1.01	0.00	0.00	0.00
1957	1966	1.01	0.00	0.00	1.01	0.00	0.00	0.00	1.01	0.00
1967		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1922
(1) Contract not final but work substantially complete
