FORM R.L.-7 REV. 2-40

SHEET 1 OF 3

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 8202
TRUNK HIGHWAY 10
COUNTY Washington
District 9A

LIMITS: Jct. T.H. 61 - W. End of Bridge (St. Croix River)



YEAR BUILT	PROJECT Nº	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS	CODE Nº	Length
					No Record of Constr		
		Oil Tr. Gravel	27'	3"			2.93
					Added in 1934.		
1936	10=94-21	Br. 5473	30'		B.S. Underpass.		2
M	A.F.E.4	Patching &			AE-1, 2788 Gal./Mi.		
1942	A.F.E.5	Bit. Seal Coat	24'		Sand, 72 C.Y./Mi.		2.93
					Maint. Dept.		
M		Gravel Lifts &			MC-3, 6749 Gal./Mi.		
1945	A.F.E. 18	Restore Bit. Mat					2.93
		(Spots)			Maint. Div.		
C		Bit. Resurfacing			SC-3, 24378 Gal.		
1946	A.F.E. 20	Mixed Bit.	26'	1"	Agg. 1598 C.Y.		2.93
				added			2.93
M					AE-1, 8607 Gal.		
1947	A.F.E. 5	Bit. Seal. Coat	24'		Agg. 245 C.Y.		2.93
M		Spot Treat.			MC-3 & RT-6, 7432 Gal.		
1950	A.F.E. 4	Bit. Surf. Repair	24'		Agg. 465 C.Y.		2.93 (Net 1.00)
M		Spot Treat.			MC-3, 9362 Gal.		
1951	A.F.E. 4	Bit. Surf. Repair	22'		Agg. 668 C.Y.		2.33 (Net 1.20)
M					RCS-2, 4592 Gal.		
1952	A.F.E. 5	Light Bit. Seal	24'		Agg. 136 C.Y.		2.93
C							
1952	A.F.E. 48	Guard Rail					
M		Spot Treat			MC-3, 8003 Gal.		
1953	A.F.E. 604	Bit. Surf. Repairs	22'		Agg. 605 Tons		2.93 (Net 0.90)
M		Spot Treat.			MC-3, 9653 Gal.		
1955	A.F.E. 604	Bit. Surf. Repair	24'		Agg. 802 Tons		2.93 (Net 0.85)
M					MC-3, 9129 Gal.		
1956	A.F.E. 604	Bit. Surf. Repair	24'		Agg. 868 Tons		1.10
M		Spot Treat			MC-3, 3289 Gal.		
1957	A.F.E. 604	Bit. Surf. Repair	24'		Agg. 330 Tons		2.93 (Net 0.40)

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.
1934		2.93	2.93	0.00	0.00	0.00	2.93	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1934.

FORM R.L.-7 REV. 3-58

PREPARED BY
TRAFFIC AND PLANNING DIVISION
IN COOPERATION WITH
U.S. DEPARTMENT OF COMMERCE
BUREAU OF PUBLIC ROADS

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 8202
TRUNK HIGHWAY 10
COUNTY Washington
DISTRICT Metro

LIMITS: Jct. T.H. 61 - W. End of Bridge (St Croix River)

Ref. Pt. 299+00.761 - 302+00.897

YEAR BUILT	PROJECT Nº	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS
M		Spot Treat			MC-3, 4541 Gal.
1959	A.F.E. 604	Bit. Surf. Repair	24'		Agg. 420 Tons
M					RC-2, 4526 Gal.
1960		Bit. Seal Coat	22'		Agg. 144 C.Y.
M		Spot Treat			Plant Mix 2267 Tons
1964	SF	Bit. Surf. Repair	V.W.		RC-2 Tack 1226 Gal.
		Spot Shouldering			Gravel 538 Tons
C					
1969	8202-07	Pl. Mix. Bit	24'	2½"	
		Gravel Shoulders	16'		8' Rt. & Lt.
C		Curve Realign &			
1980	8202-16	Reconstruction	24'	10¼"	
	GR 003-5(34)	Bit. Shoulders	8'	1½"	
C		Grading	47'		
1981	8202-20	Bit. Surfacing	24'	2¼"	Park & Ride Facility
	GR 003-5(39)	Bit. Shoulders	10'	Var.	
C					
1981	8202-13	Traffic Control Signals			At New Jct. TH-61
	GR 003-5(39)	Lighting System			
C					
1984	8202-22	Grading	24'	4"	Spec. 2331
		Bit. Surfacing		¾"	Spec. 2361
C					
1990	8202-26	Temp. Connection			Future TH-10
M					
1992	SF	Bit. Overlay	24'	1½"	
C					
1999	8202-24	Grading	Var	6"	MV 3 (MVNW35035B)
		Surfacing			LV 3 (LVNW35035B)
M					
2005	8825-155	Bit. Crack Repair			Spec. 2331
M					
2005	8202-27	Microsurfacing	24'		Spec. 2356
S					
2013	8825-470	Microsurfacing	24'		Spec. 2356 Type 2

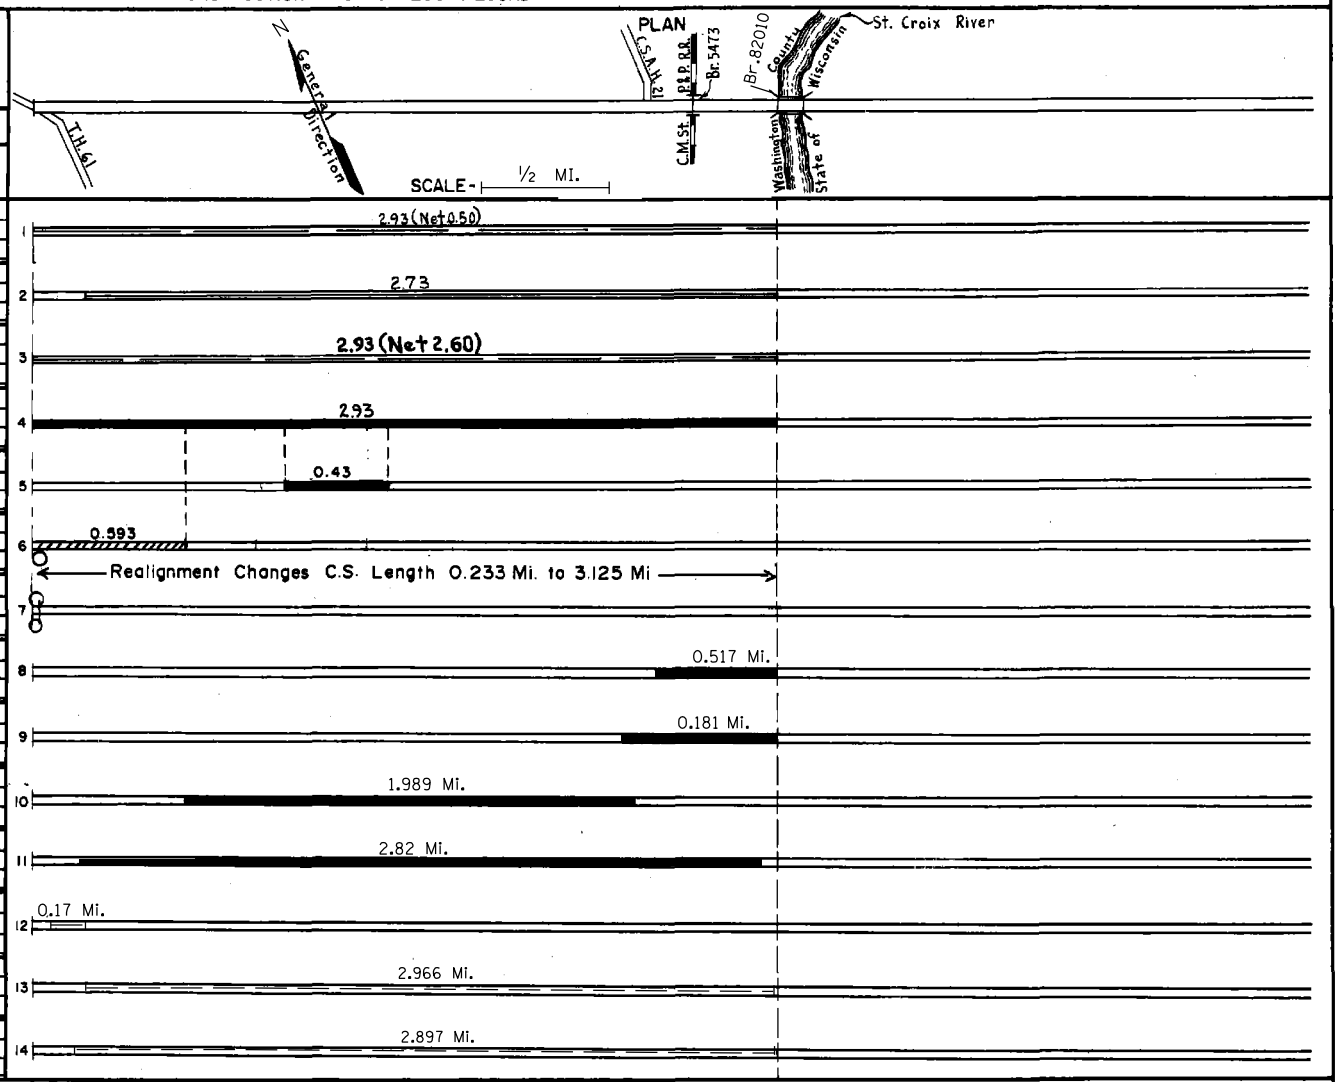

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.

REMARKS: See Sheet Nº 1

FORM RL-7

PREPARED BY
BUREAU OF POLICY & PLANNING
IN COOPERATION WITH
U. S. DEPARTMENT OF TRANSPORTATION - FEDERAL HIGHWAY ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF TRANSPORTATION
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 8202
TRUNK HIGHWAY 10
COUNTY Washington
DISTRICT Metro

LIMITS: Jct USTH-61 - W end Br.82010; St Croix River

Ref. Pt. 299+00.761 - 302+00.897



YEAR BUILT	PROJECT No	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS
S		Grading			
2017	8202-30	Bit. Mill & Overlay	24'	2"	Spec. 2360
		Bit. Turn La/shldrs	var.	6"	Agg. base 6", class 6

0.365 Mi.

1 2 3 4 5 6 7 8 9 10 11 12 13 14

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.

REMARKS:
