SHEET 1 OF 1

PREPARED BY
TRAFFIC AND PLANNING DIVISION
IN COOPERATION WITH
U.S. DEPARTMENT OF COMMERCE
BUREAU OF PUBLIC ROADS

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 0610
TRUNK HIGHWAY 7
COUNTY Big Stone
DISTRICT 4B

LIMITS: (In Ortonville) W. Jct. T.H. 75 – S. Jct. T.H. 12

Ref. Pt. 026+00.276 - 027+00.119



YEAR BUILT	PROJECT Nº	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS
					No Record of Constr.
		Mixed Bit.	24'		Added to System
					in 1959
		Grading			Agg base C5
2013	0610-01	Bit. Mill & Overlay	24'	3"	Spec 2360
	(0602-25)				Agg shldrng

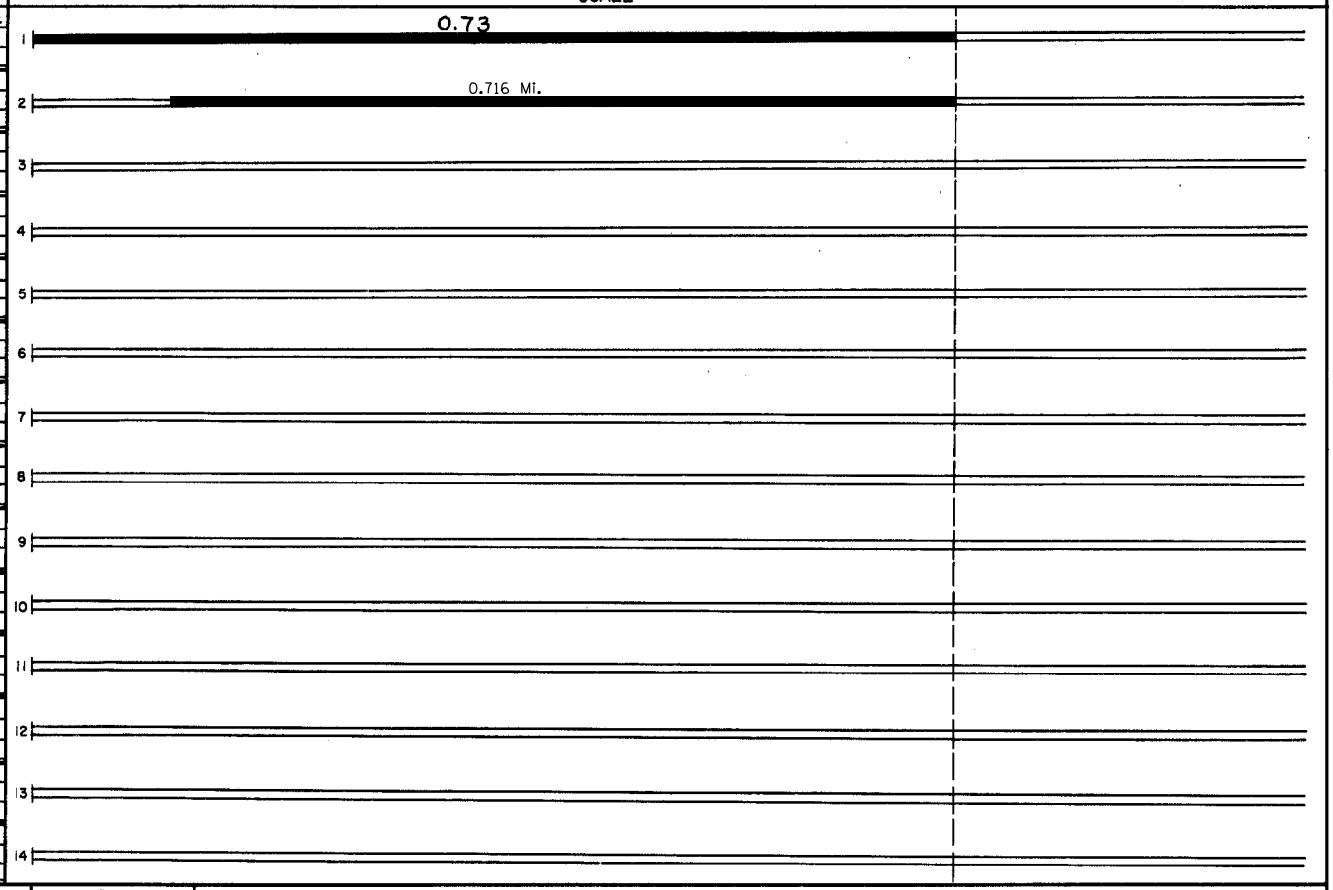

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.
1959		0.73	0.00	0.00	0.73	0.00	0.00	0.00	0.73	0.00

REMARKS:
