FORM R.L.-7 REV. 2-40

SHEET 1 OF 2

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 1010
TRUNK HIGHWAY 101
COUNTY Carver
DISTRICT 5A

LIMITS: In Chanhassen
Jct. T.H. 5 — E. Co. Line

YEAR BUILT	PROJECT Nº	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS	CODE Nº
		Gravel	30'	2"	No Record of Constr. Added in 1934.	
		Gravel	27'	2"	No Record of Constr. Added in 1934.	
1935		Oil Tr. Gravel	27'	2"	Maint. Dept. Direct Labor.	
M 1942	A.F.E. 5	Bit. Seal Coat	24'		AE-1, 3109 Gal./Mi. Sand (?) Maint. Dept.	
M 1947	A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'		SC-3, 2366 Gal. Agg. 144 C.Y.	
C 1954	A.F.E. 819	Scarify & Remix Mat'l imp. Bit. Resurfacing	24'	3"	SC-2&3, 7335 Gal. Agg. 308 Tons	
		Mixed Bit.	22'	1"		
M 1956	A.F.E. 605	Light Bit. Seal	24'		RC-2, 710 Gal. Agg. 32 C.Y.	
1946		Bit. Surf.-Treated	18'		Transferred into this	
		Mixed Bit. (0.86)	42'		C.S. in 1964	
		Bit. Surf	24'		Transferred into this	
		No record of Constr			C.S. in 1964	
C 1973	1010-04	Plant Mix Bit O-Lay	29'	3"		
		Gravel Shoulders				
C 1976	1002-29	Bit. Level. Course	18'-26'	1½"		
		Asph. Conc. Surf.	18'-36'	3/4"		
	RFU 014-3(1)	Turn Lanes				

PLAN

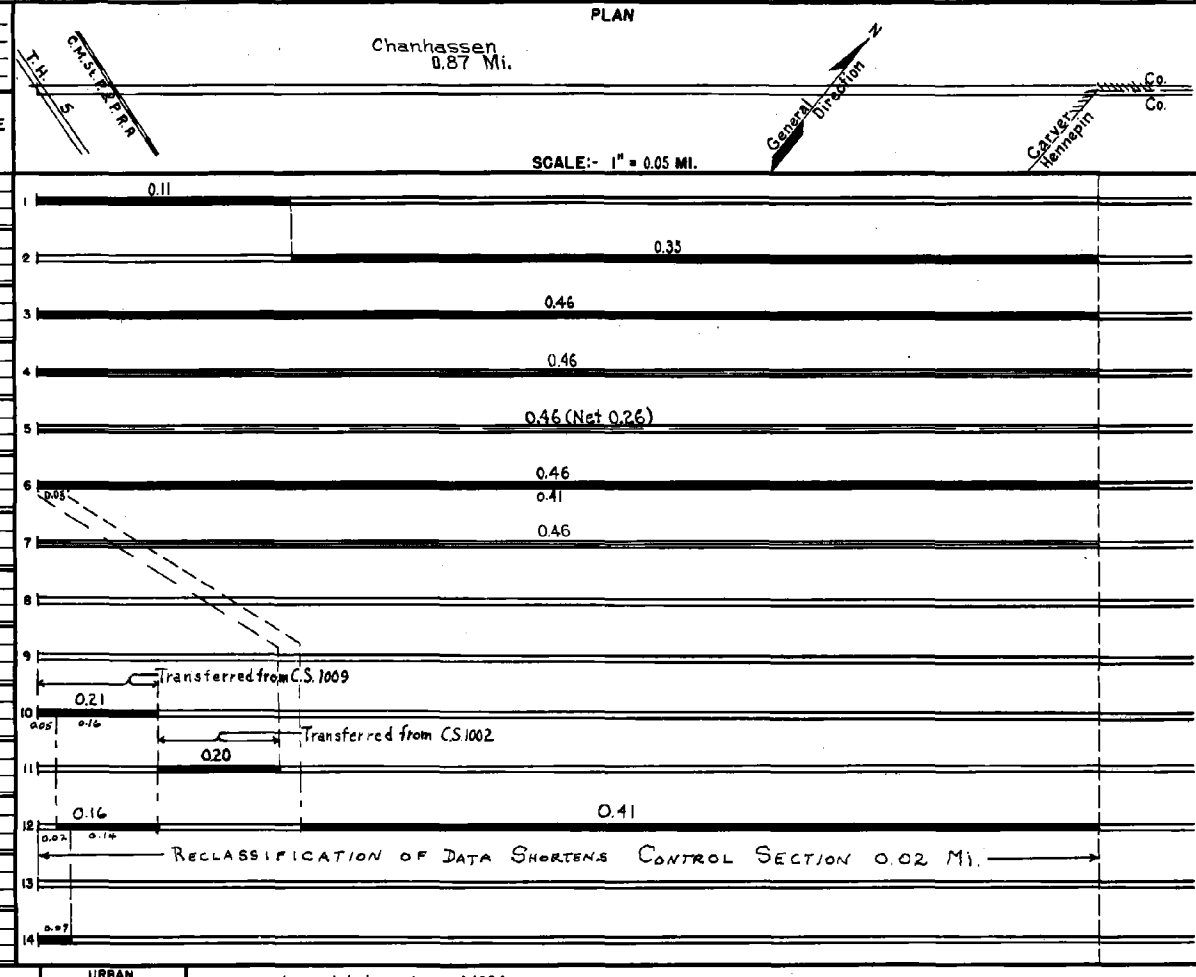

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.
1934	1963	0.46	0.35	0.00	0.11	0.00	0.46	0.00	0.00	0.00
1964	1965	0.87	0.35	0.00	0.52	0.00	0.87	0.00	0.00	0.00
1966	1966	0.87	0.00	0.00	0.87	0.00	0.87	0.00	0.00	0.00
1967		0.87	0.00	0.00	0.87	0.00	0.00	0.00	0.87	0.00

REMARKS: Layout is to scale as of 1934

1-75

FORM RL-7

PREPARED BY
BUREAU OF POLICY & PLANNING
IN COOPERATION WITH
U. S. DEPARTMENT OF TRANSPORTATION - FEDERAL HIGHWAY ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF TRANSPORTATION
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 1010
TRUNK HIGHWAY 101
COUNTY Carver
DISTRICT Metro

LIMITS: Jct. MNTH-5 E.B. - Carver/Hennepin Co. Line

Ref. Pt. 013+00.436 - 013+00.842

YEAR BUILT	PROJECT No	DESCRIPTION TYPE	WIDTH	THICKNESS	REMARKS
C					
1985	1002-46	Mill & Bit. Overlay	24'	1"	Spec. 2331
				1"	Spec. 2361
C		Grading.			
1988	88 - 22B	Agg. Base.	24'	4"	Spec. 2331
		Bit. Surfacing		2"	Spec. 2341

PLAN

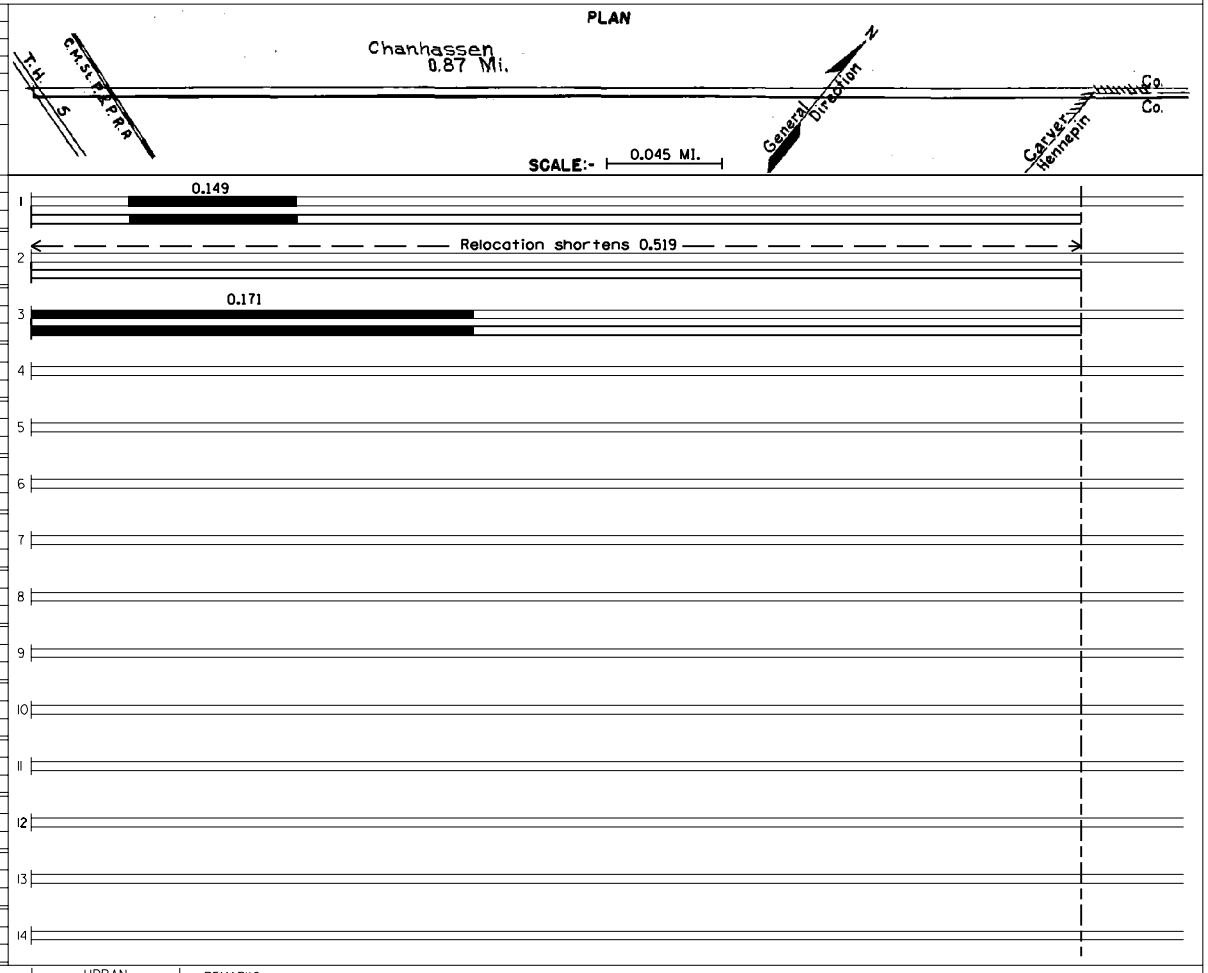

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.

REMARKS:
